
CMH139
Preliminary Schedule


Activity ID	Activity Name	OD	RD	Start	Finish
CMH139		510	389	28-Apr-26 A	28-Apr-28
Milestones		510	255	28-Apr-26 A	28-Apr-28
Project Milestones		510	0	28-Apr-26 A	28-Apr-28
MS1040	Milestone - ECPO Request Submission	0	0		28-Apr-26 A
MS1000	Milestone - Early Funding	0	0		13-May-26 A
MS1050	Milestone - Full Funding RFP Submission	0	0		05-Jun-26 A
MS60120	Milestone - Early Funding Part 2	0	0		01-Jul-26 A
MS1010	Milestone - Project Kickoff	0	0	27-Jul-26 A	
MS1020	Milestone - Full Funding	0	0		31-Aug-26 A
MS1130	Milestone - Final Completion	0	0		28-Apr-28
Construction Milestones		284	91	27-Jul-26 A	07-Sep-27
MS1025	Milestone - Site Commencement [AWS Contract Date 7/1/2026]	0	0	27-Jul-26 A	
MS1030	Milestone - Shell Commencement [AWS Contract Date 10/1/2026]	0	0	14-Oct-26 A	
MS1060	Milestone - Excavation Completion	0	0		28-Apr-27
MS1070	Milestone - Phase 1 Dry-In	0	0		19-May-27
MS1110	Milestone - Site / Shell Energize MV Switchgear	0	0		21-Jun-27
MS1080	Milestone - Building Dry-In Complete	0	0		26-Jul-27
MS1100	Milestone - Site Substantial Completion [AWS Contract Date 5/24/2027]	0	0		16-Aug-27*
MS1120	Milestone - Shell Substantial Completion [AWS Contract Date 10/14/2027]	0	0		07-Sep-27*
MS60110	Milestone - Shell Final Completion / PCO [AWS Contract Date 10/14/2027]	0	0		07-Sep-27*
Contract Milestones		240	240	20-May-27	28-Apr-28
Phase 1 (ROMP01 & 03)		205	205	20-May-27	10-Dec-27
MS10000	Milestone Phase 1 - Start Work Date [AWS Contract Date 3/29/2027]	0	0	20-May-27*	
MS10010	Milestone Phase 1 - H2C-9W	0	0		01-Jul-27*
MS10020	Milestone Phase 1 - Mechanical Equipment Startup Complete for Controls	0	0		20-Aug-27*
MS10050	Milestone Phase 1 - Ready for AWS Fiber Optic Install	0	0		20-Aug-27
MS10030	Milestone Phase 1 - H2C-5W	0	0		20-Aug-27*
MS10040	Milestone Phase 1 - H2C-4W	0	0		20-Aug-27*
MS10070	Milestone Phase 1 - Electric Room LV Panelboards Energized	0	0		27-Sep-27
MS10060	Milestone Phase 1 - FEA [AWS Contract Date 9/27/2027]	0	0		27-Sep-27*
MS10080	Milestone Phase 1 - NEA [AWS Contract Date 10/11/2027]	0	0		11-Oct-27*
MS10090	Milestone Phase 1 - H2C-2W	0	0		11-Oct-27*
MS10100	Milestone Phase 1 - H2C [AWS Contract Date 10/29/2027]	0	0		29-Oct-27*

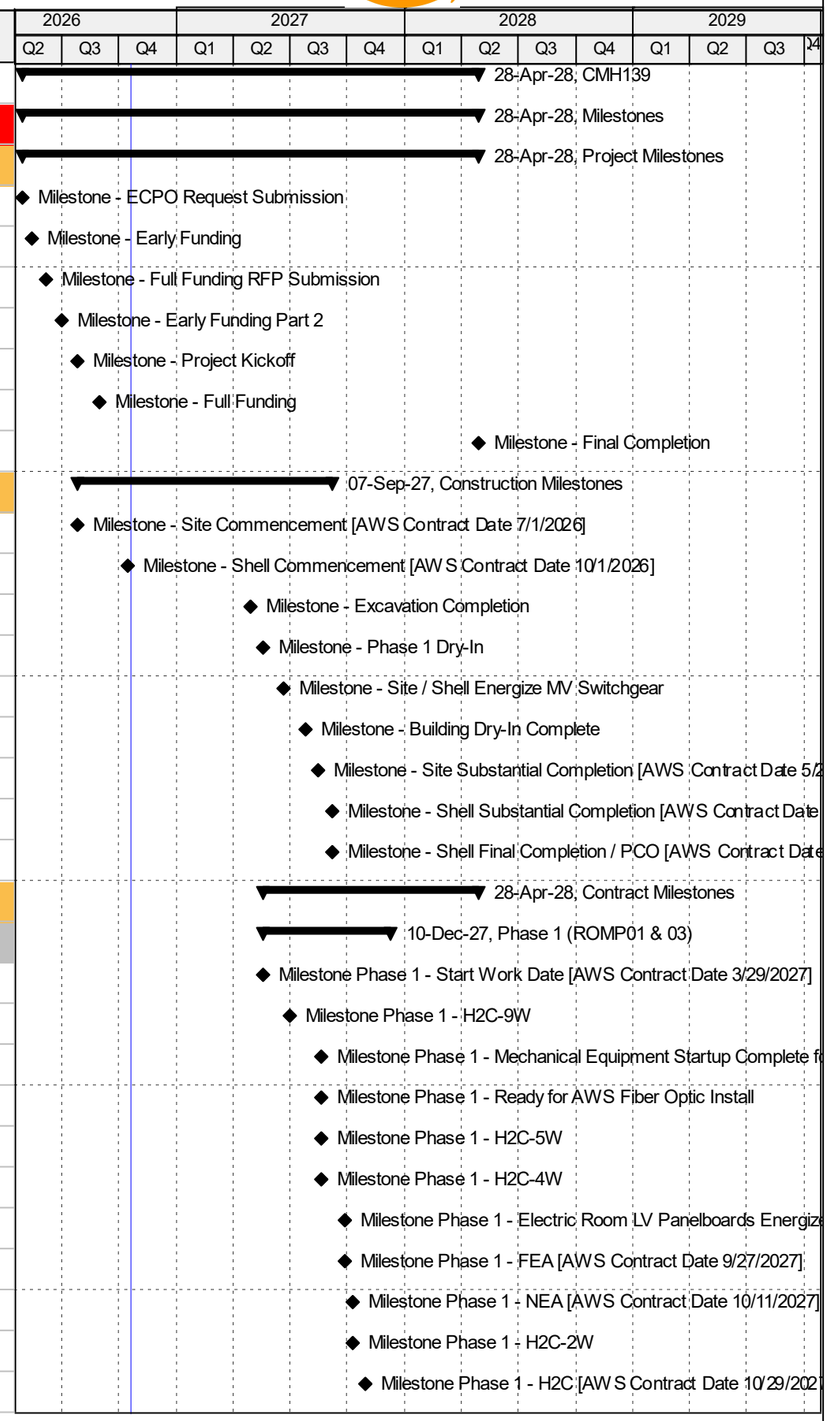

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary


Run Date: 15-Oct-26 14:16
Data Date: 19-Oct-26

Activity ID	Activity Name	OD	RD	Start	Finish
MS10110	Milestone Phase 1 - PFHO [AWS Contract Date 11/26/2027]	0	0		26-Nov-27*
MS10120	Milestone Phase 1 - PCO	0	0		10-Dec-27
Phase 2 (ROMP02 & 04)		163	163	31-May-27	21-Jan-28
MS20000	Milestone Phase 2 - Start Work Date [AWS Contract Date 5/31/2027]	0	0	31-May-27*	
MS20010	Milestone Phase 2 - H2C-9W	0	0		19-Jul-27*
MS20020	Milestone Phase 2 - H2C-5W	0	0		19-Jul-27*
MS20030	Milestone Phase 2 - H2C-4W	0	0		19-Jul-27*
MS20040	Milestone Phase 2 - Electric Room LV Panelboards Energized	0	0		02-Aug-27
MS20050	Milestone Phase 2 - Mechanical Equipment Startup Complete for Controls	0	0		11-Aug-27*
MS20070	Milestone Phase 2 - H2C-2W	0	0		25-Aug-27*
MS20060	Milestone Phase 2 - NEA [AWS Contract Date 11/29/2027]	0	0		29-Nov-27*
MS20080	Milestone Phase 2 - H2C [AWS Contract Date 12/17/2027]	0	0		17-Dec-27*
MS20090	Milestone Phase 2 - PFHO [AWS Contract Date 1/7/2028]	0	0		07-Jan-28*
MS20100	Milestone Phase 2 - PCO	0	0		21-Jan-28
Phase 3 (ROMP05 & 07)		183	183	31-May-27	18-Feb-28
MS30000	Milestone Phase 3 - Gray Early Start Work Date [AWS Contract Date 6/28/2027]	0	0	31-May-27*	
MS30010	Milestone Phase 3 - H2C-9W	0	0		05-Aug-27*
MS30020	Milestone Phase 3 - H2C-5W	0	0		05-Aug-27*
MS30030	Milestone Phase 3 - H2C-4W	0	0		05-Aug-27*
MS30040	Milestone Phase 3 - Electric Room LV Panelboards Energized	0	0		19-Aug-27
MS30050	Milestone Phase 3 - Mechanical Equipment Startup Complete for Controls	0	0		31-Aug-27*
MS30070	Milestone Phase 3 - H2C-2W	0	0		12-Oct-27*
MS30060	Milestone Phase 3 - NEA [AWS Contract Date 12/27/2027]	0	0		27-Dec-27*
MS30080	Milestone Phase 3 - H2C [AWS Contract Date 1/14/2028]	0	0		14-Jan-28*
MS30090	Milestone Phase 3 - PFHO [AWS Contract Date 2/04/2028]	0	0		04-Feb-28*
MS30100	Milestone Phase 3 - PCO	0	0		18-Feb-28
Phase 4 (ROMP06 & 08)		190	190	18-Jun-27	17-Mar-28
MS40000	Milestone Phase 4 - Gray Early Start Work Date [AWS Contract Date 7/26/2027]	0	0	18-Jun-27*	
MS40010	Milestone Phase 4 - H2C-9W	0	0		02-Sep-27*
MS40020	Milestone Phase 4 - H2C-5W	0	0		02-Sep-27*
MS40030	Milestone Phase 4 - H2C-4W	0	0		02-Sep-27*
MS40040	Milestone Phase 4 - Electric Room LV Panelboards Energized	0	0		17-Sep-27
MS40050	Milestone Phase 4 - Mechanical Equipment Startup Complete for Controls	0	0		15-Nov-27*

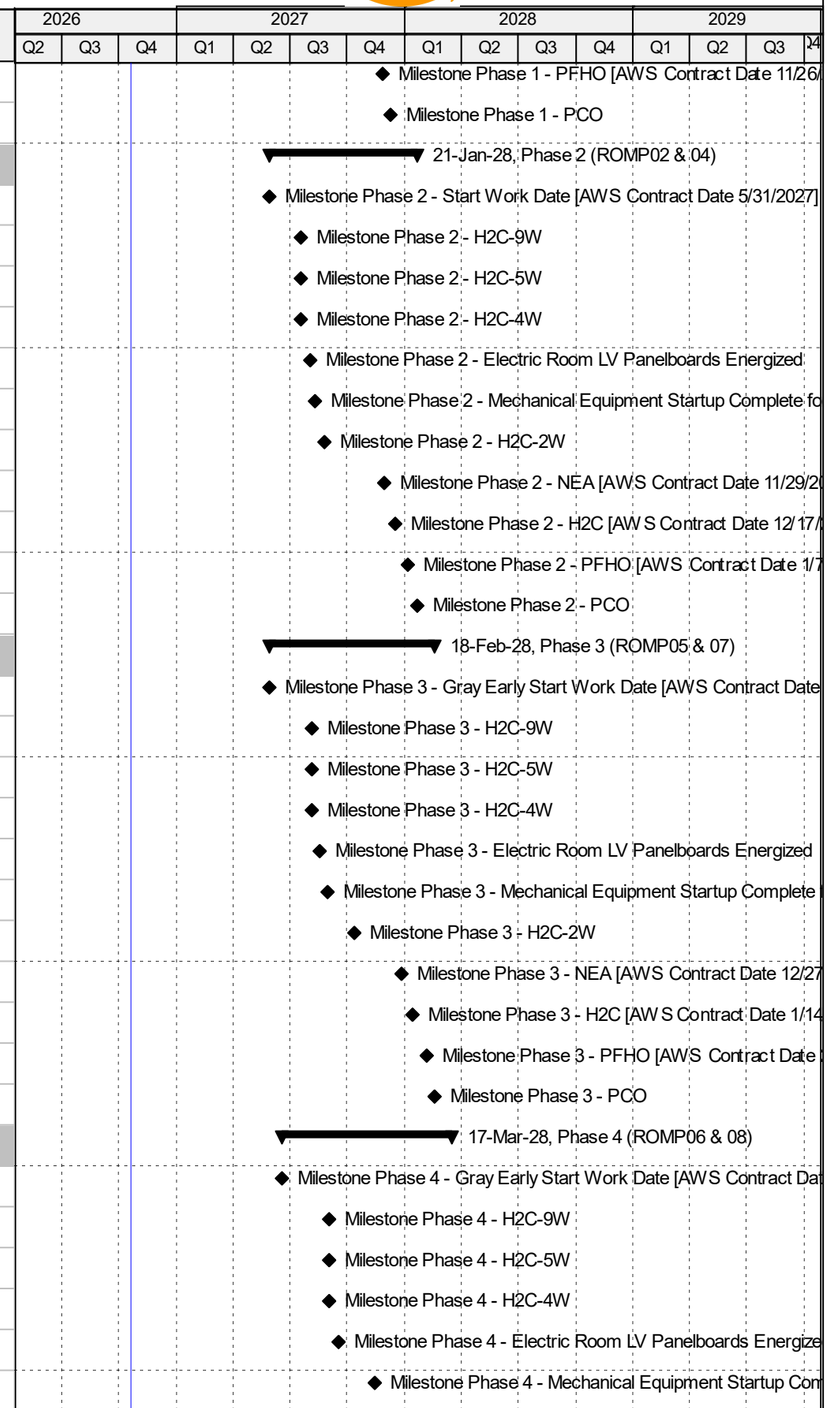

CMH139
Preliminary Schedule


Activity ID	Activity Name	OD	RD	Start	Finish
MS40070	Milestone Phase 4 - H2C-2W	0	0		01-Dec-27*
MS40060	Milestone Phase 4 - NEA [AWS Contract Date 1/24/2028]	0	0		24-Jan-28*
MS40080	Milestone Phase 4 - H2C [AWS Contract Date 2/11/2028]	0	0		11-Feb-28*
MS40090	Milestone Phase 4 - PFHO [AWS Contract Date 3/03/2028]	0	0		03-Mar-28*
MS40100	Milestone Phase 4 - PCO	0	0		17-Mar-28
Phase 5 (ROMP09 & 11)		186	186	23-Jul-27	14-Apr-28
MS50000	Milestone Phase 5 - Gray Early Start Work Date [AWS Contract Date 8/23/2027]	0	0	23-Jul-27*	
MS50010	Milestone Phase 5 - H2C-9W	0	0		30-Sep-27*
MS50020	Milestone Phase 5 - H2C-5W	0	0		30-Sep-27*
MS50030	Milestone Phase 5 - H2C-4W	0	0		30-Sep-27*
MS50040	Milestone Phase 5 - Electric Room LV Panelboards Energized	0	0		14-Oct-27
MS50050	Milestone Phase 5 - Mechanical Equipment Startup Complete for Controls	0	0		15-Nov-27*
MS50070	Milestone Phase 5 - H2C-2W	0	0		01-Dec-27*
MS50060	Milestone Phase 5 - NEA [AWS Contract Date 2/21/2028]	0	0		21-Feb-28*
MS50080	Milestone Phase 5 - H2C [AWS Contract Date 3/10/2028]	0	0		10-Mar-28*
MS50090	Milestone Phase 5 - PFHO [AWS Contract Date 3/31/2028]	0	0		31-Mar-28*
MS50100	Milestone Phase 5 - PCO	0	0		14-Apr-28
Phase 6 (ROMP10 & 12)		171	171	27-Aug-27	28-Apr-28
MS60000	Milestone Phase 6 - Gray Early Start Work Date [AWS Contract Date 9/27/2027]	0	0	27-Aug-27*	
MS60010	Milestone Phase 6 - H2C-9W	0	0		04-Nov-27*
MS60020	Milestone Phase 6 - H2C-5W	0	0		04-Nov-27*
MS60030	Milestone Phase 6 - H2C-4W	0	0		04-Nov-27*
MS60040	Milestone Phase 6 - Electric Room LV Panelboards Energized	0	0		18-Nov-27
MS60050	Milestone Phase 6 - Mechanical Equipment Startup Complete for Controls	0	0		02-Dec-27*
MS60070	Milestone Phase 6 - H2C-2W	0	0		16-Dec-27*
MS60060	Milestone Phase 6 - NEA [AWS Contract Date 3/20/2028]	0	0		20-Mar-28*
MS60080	Milestone Phase 6 - H2C [AWS Contract Date 4/07/2028]	0	0		07-Apr-28*
MS60090	Milestone Phase 6 - PFHO [AWS Contract Date 4/28/2028]	0	0		28-Apr-28*
MS60100	Milestone Phase 6 - PCO [AWS Contract Date 4/28/2028]	0	0		28-Apr-28*
Pre-Construction		380	271	14-May-26 A	10-Nov-27
Permitting & Design		96	50	13-Aug-26 A	30-Dec-26
Permits		0	0	13-Aug-26 A	13-Aug-26 A
P1MS.160	Permit - Building Permit	0	0		13-Aug-26 A

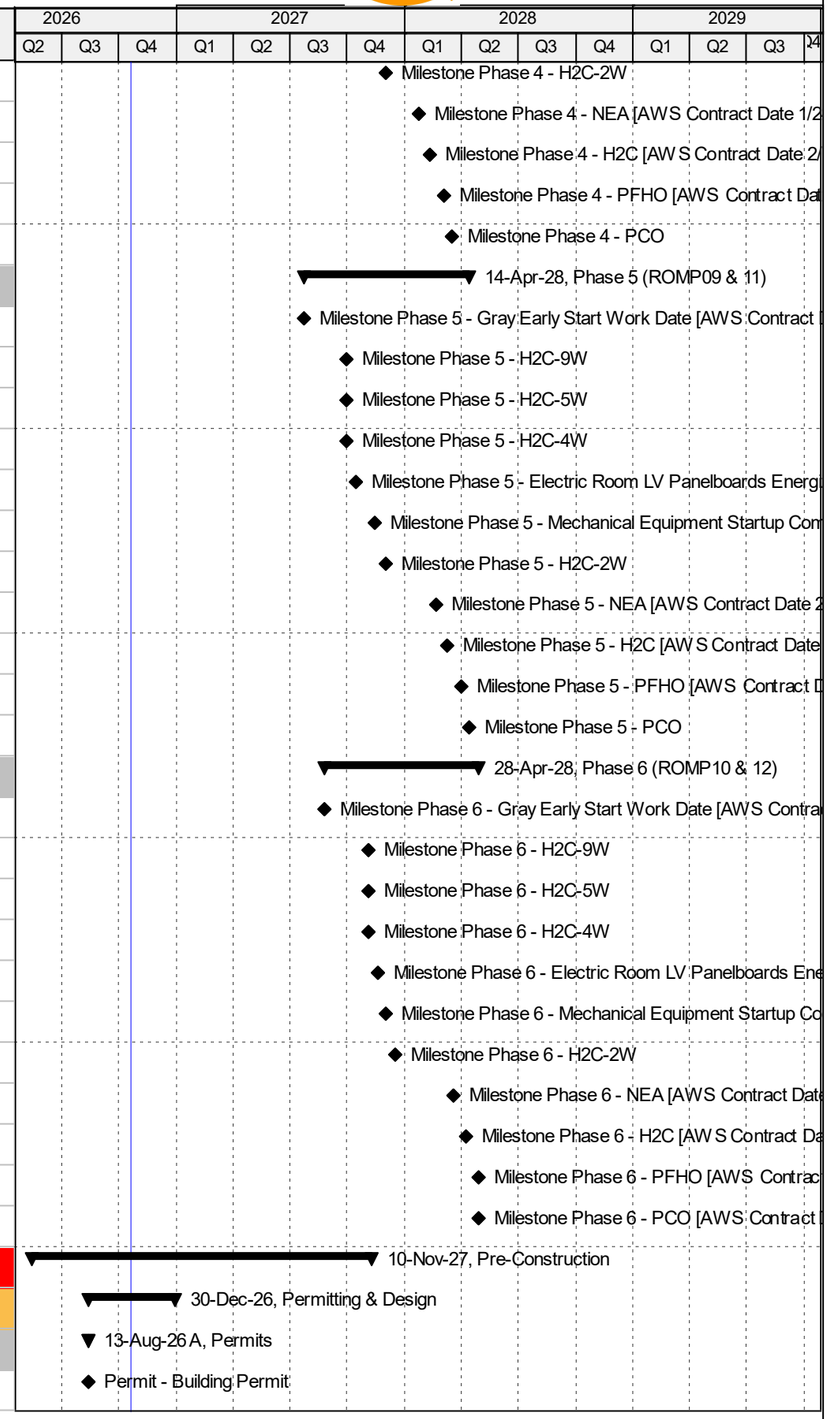


Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

Run Date: 15-Oct-26 14:16
Data Date: 19-Oct-26


Activity ID	Activity Name	OD	RD	Start	Finish
Design		89	50	20-Aug-26 A	30-Dec-26
DS1040	Design - BIM Kickoff	1	0	20-Aug-26 A	20-Aug-26 A
DS1050	Design - Site U/G Coordination Model Turnover	10	0	24-Aug-26 A	04-Sep-26 A
DS1070	Design - Building D U/G Coordination	25	0	31-Aug-26 A	05-Oct-26 A
DS1100	Design - Building D Office Coordination	20	13	08-Oct-26 A	04-Nov-26
DS1080	Design - Building D Interior MEP Coordination (Walls & MEP)	40	40	19-Oct-26	15-Dec-26
DS1110	Design - Gen Yard Coordination	30	30	16-Nov-26	30-Dec-26
Procurement		380	271	14-May-26 A	10-Nov-27
Subcontracts		279	170	14-May-26 A	18-Jun-27
Site & Shell		279	170	14-May-26 A	18-Jun-27
Site Utilities		55	26	08-Sep-26 A	23-Nov-26
PR.1620	Procurement / Site & Shell - Award Site Utilities Package (LOI)	10	0	08-Sep-26 A	09-Oct-26 A
PR.1650	Procurement / Site & Shell - Prepare Site Utilities (Plumbing) Submittals / Shop Drawings	10	1	14-Oct-26 A	19-Oct-26
PR.1660	Procurement / Site & Shell - Review & Approve Site Utilities (Plumbing) Submittals / Shop Drawings	10	10	20-Oct-26	02-Nov-26
PR.1030	Procurement / Site & Shell - Plumbing Materials Fabrication & Deliver	15	15	03-Nov-26	23-Nov-26
Fencing		45	45	19-Oct-26	22-Dec-26
PR.1630	Procurement / Site & Shell - Award Fencing Package	20	20	19-Oct-26	13-Nov-26
PR.1810	Procurement / Site & Shell - Prepare Fencing Submittals / Shop Drawings	10	10	16-Nov-26	01-Dec-26
PR.1820	Procurement / Site & Shell - Review & Approve Fencing Submittals / Shop Drawings	10	10	02-Dec-26	15-Dec-26
PR.1830	Procurement / Site & Shell - Fencing Fabrication & Deliver	5	5	16-Dec-26	22-Dec-26
Deep Foundation		56	0	14-May-26 A	13-Aug-26 A
PR.1575	Procurement / Site & Shell - Award Deep Foundations Package	7	0	14-May-26 A	04-Jun-26 A
PR.1850	Procurement / Site & Shell - Prepare Deep Foundations Submittals / Shop Drawings	10	0	05-Jun-26 A	15-Jun-26 A
PR.1860	Procurement / Site & Shell - Review & Approve Submittals / Shop Drawings (EOR)	10	0	16-Jun-26 A	23-Jun-26 A
PR.2300	Procurement / Site & Shell - Review & Approve Submittals / Shop Drawings (FAA City Submission)	30	0	29-Jun-26 A	13-Aug-26 A
PR.1840	Procurement / Site & Shell - Deep Foundations Delivery / Mobilization	5	0	22-Jul-26 A	28-Jul-26 A
Concrete		163	100	21-Jul-26 A	11-Mar-27
Cast In Place		52	0	21-Jul-26 A	09-Oct-26 A
PR.1480	Procurement / Site & Shell - Award CIP Concrete Package	20	0	21-Jul-26 A	10-Sep-26 A
PR.1890	Procurement / Site & Shell - Prepare CIP Submittals / Shop Drawings	10	0	31-Jul-26 A	13-Aug-26 A
PR.1900	Procurement / Site & Shell - Review & Approve CIP Submittals / Shop Drawings	10	0	14-Aug-26 A	27-Aug-26 A
PR.1040	Procurement / Site & Shell - Foundation Materials Fabrication & Deliver	10	0	18-Sep-26 A	09-Oct-26 A
Precast		159	100	27-Jul-26 A	11-Mar-27

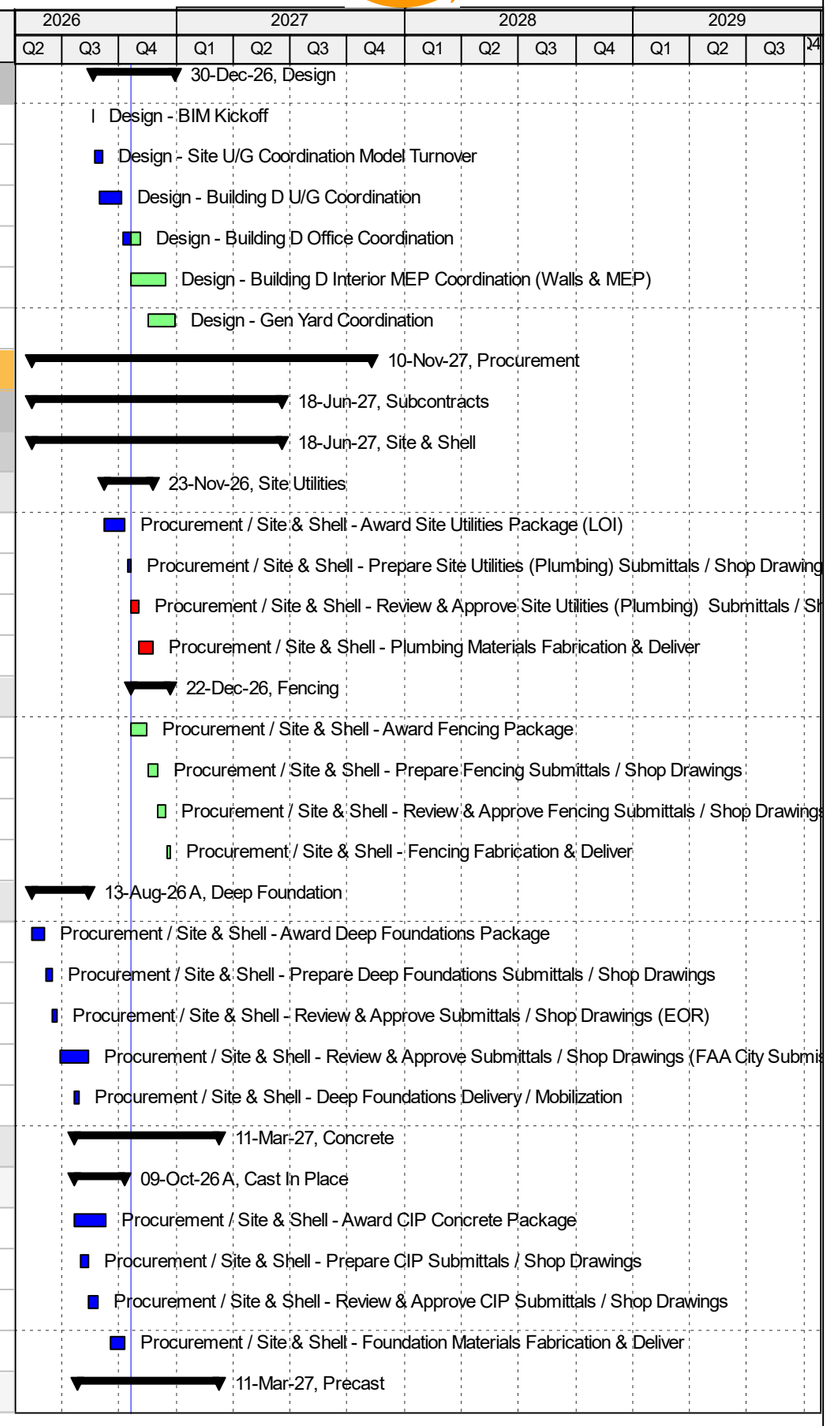

Activity ID	Activity Name	OD	RD	Start	Finish
PR.1470	Procurement / Site & Shell - Award Precast Concrete Package	20	5	27-Jul-26 A	23-Oct-26
PR.1870	Procurement / Site & Shell - Prepare Precast Concrete Submittals / Shop Drawings	20	20	26-Oct-26	20-Nov-26
PR.1880	Procurement / Site & Shell - Review & Approve Precast Concrete Submittals / Shop Drawings	10	10	23-Nov-26	08-Dec-26
PR.1090	Procurement / Site & Shell - Precast Concrete Seq 1 Fabrication & Deliver	30	30	09-Dec-26	21-Jan-27
PR.1730	Procurement / Site & Shell - Precast Concrete Seq 2 Fabrication & Deliver	30	30	31-Dec-26	11-Feb-27
PR.1740	Procurement / Site & Shell - Precast Concrete Seq 3 Fabrication & Deliver	30	30	22-Jan-27	04-Mar-27
PR.1750	Procurement / Site & Shell - Precast Concrete Seq 4 Fabrication & Deliver	30	30	29-Jan-27	11-Mar-27
Steel		195	86	14-May-26 A	19-Feb-27
PR.1460	Procurement / Site & Shell - Award Steel Package	7	0	14-May-26 A	10-Jun-26 A
PR.1140	<FRAG> Steel Early Funding Delay	131	22	14-May-26 A	17-Nov-26
PR.1910	Procurement / Site & Shell - Prepare Steel Submittals / Shop Drawings Seq. 1-3	15	0	24-Aug-26 A	23-Sep-26 A
PR.2820	Procurement / Site & Shell - Prepare Steel Submittals / Shop Drawings Seq. 4-6	10	0	04-Sep-26 A	24-Sep-26 A
PR.2830	Procurement / Site & Shell - Prepare Steel Submittals / Shop Drawings Seq. 7-9	10	0	11-Sep-26 A	29-Sep-26 A
PR.2840	Procurement / Site & Shell - Review & Approve Steel Submittals / Shop Drawings Seq 1-3	10	0	24-Sep-26 A	14-Oct-26 A
PR.2760	Procurement / Site & Shell - Review & Approve Steel Submittals / Shop Drawings Seq 4-6	10	5	25-Sep-26 A	23-Oct-26
PR.2770	Procurement / Site & Shell - Review & Approve Steel Submittals / Shop Drawings Seq 7-9	10	10	19-Oct-26	30-Oct-26
PR.2780	Procurement / Site & Shell - Review & Approve Steel Submittals / Shop Drawings (Screen Wall)	5	5	02-Nov-26	06-Nov-26
PR.1080	Procurement / Site & Shell - Structural Steel Fabrication & Deliver Seq 1-3	40	40	18-Nov-26	18-Jan-27
PR.1710	Procurement / Site & Shell - Structural Steel Fabrication & Deliver Screen Wall	23	23	04-Dec-26	07-Jan-27
PR.1690	Procurement / Site & Shell - Structural Steel Fabrication & Deliver Seq 4-6	14	14	19-Jan-27	05-Feb-27
PR.1150	Procurement / Site & Shell - Cooper Mobilization	5	5	19-Jan-27	23-Jan-27
PR.1700	Procurement / Site & Shell - Structural Steel Fabrication & Deliver Seq 7-9	9	9	09-Feb-27	19-Feb-27
Stairs		147	52	04-Jun-26 A	04-Jan-27
PR.2260	Procurement / Site & Shell - Award Stairs Package	5	0	04-Jun-26 A	10-Jun-26 A
PR.2150	Procurement / Site & Shell - Review & Approve Stairs Submittals / Shop Drawings	10	10	19-Oct-26	30-Oct-26
PR.1680	Procurement / Site & Shell - Stair Towers (1-3) Fabrication & Deliver	14	14	02-Nov-26	19-Nov-26
PR.1780	Procurement / Site & Shell - Stair Towers (4-6) Fabrication & Deliver	14	14	20-Nov-26	11-Dec-26
PR.1790	Procurement / Site & Shell - Stair Towers (7-9) Fabrication & Deliver	14	14	14-Dec-26	04-Jan-27
Screen Wall & Building Siding		80	80	19-Oct-26	11-Feb-27
PR.1570	Procurement / Site & Shell - Award Screen Wall & Building Siding Package	20	20	19-Oct-26	13-Nov-26
PR.1930	Procurement / Site & Shell - Prepare Screen Wall & Building Submittals / Shop Drawings	10	10	16-Nov-26	01-Dec-26
PR.1940	Procurement / Site & Shell - Review & Approve Screen Wall & Building Submittals / Shop Drawings	10	10	02-Dec-26	15-Dec-26
PR.1070	Procurement / Site & Shell - Screen Wall Fabrication & Deliver	40	40	16-Dec-26	11-Feb-27

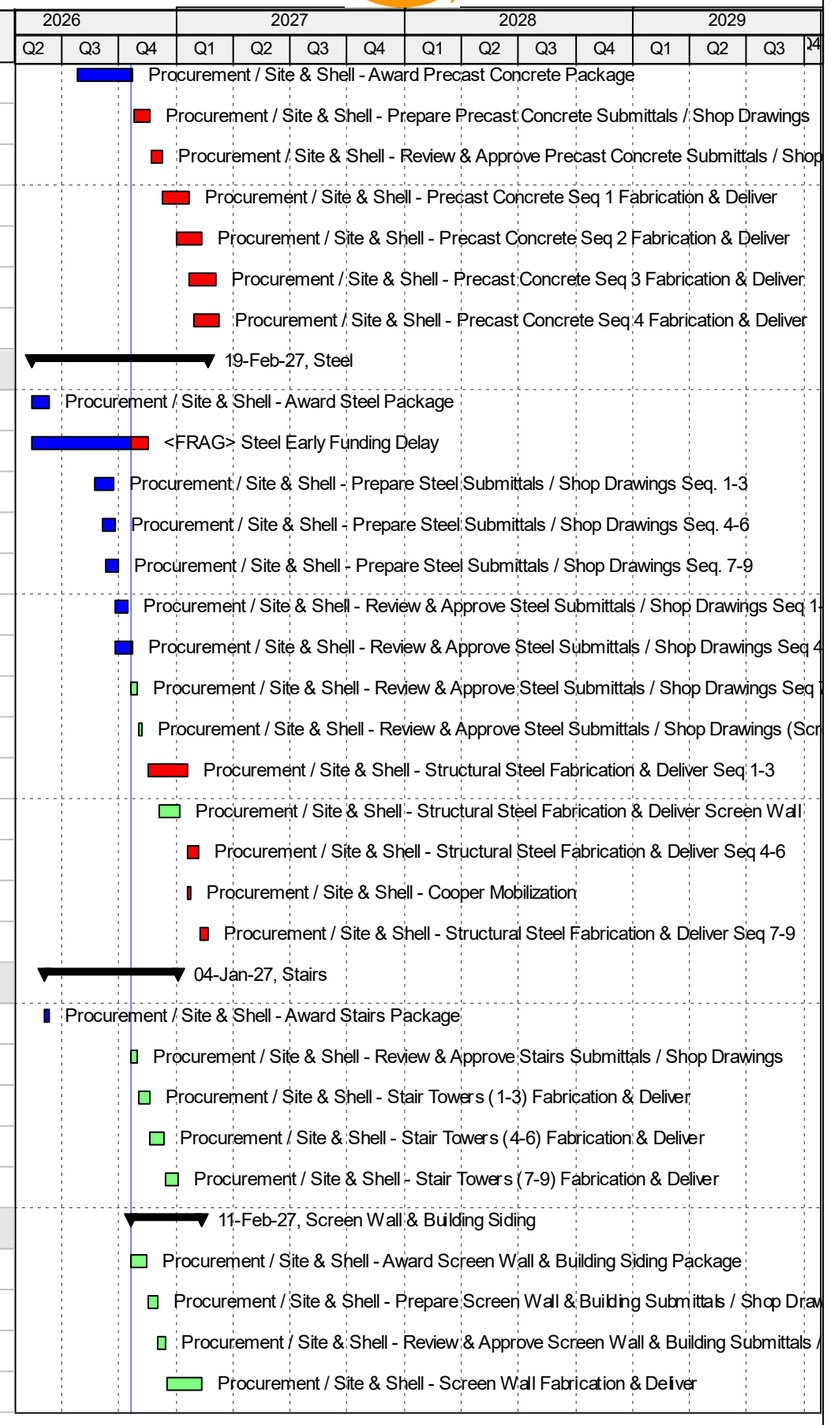


Activity ID	Activity Name	OD	RD	Start	Finish
PR.1060	Procurement / Site & Shell - Building Siding Fabrication & Deliver	40	40	16-Dec-26	11-Feb-27
Roofing		60	60	19-Oct-26	14-Jan-27
PR.1500	Procurement / Site & Shell - Award Roofing Package	20	20	19-Oct-26	13-Nov-26
PR.1950	Procurement / Site & Shell - Prepare Roofing Submittals / Shop Drawings	10	10	16-Nov-26	01-Dec-26
PR.1960	Procurement / Site & Shell - Review & Approve Roofing Submittals / Shop Drawings	10	10	02-Dec-26	15-Dec-26
PR.1050	Procurement / Site & Shell - Roofing Materials Fabrication & Deliver	20	20	16-Dec-26	14-Jan-27
Mechanical		61	32	08-Sep-26 A	03-Dec-26
PR.1450	Procurement / Site & Shell - Award Mechanical Package	10	2	08-Sep-26 A	20-Oct-26
PR.1970	Procurement / Site & Shell - Prepare Mechanical Submittals / Shop Drawings	10	10	21-Oct-26	03-Nov-26
PR.1980	Procurement / Site & Shell - Review & Approve Mechanical Submittals / Shop Drawings	10	10	04-Nov-26	17-Nov-26
PR.1990	Procurement / Site & Shell - Mechanical Fabrication & Deliver	10	10	18-Nov-26	03-Dec-26
Electrical		54	20	31-Aug-26 A	13-Nov-26
PR.2000	Procurement / Site & Shell - Award Electrical Package	10	0	31-Aug-26 A	08-Sep-26 A
PR.2010	Procurement / Site & Shell - Prepare Electrical Submittals / Shop Drawings	10	5	14-Sep-26 A	23-Oct-26
PR.1440	Procurement / Site & Shell - Review & Approve Electrical Submittals / Shop Drawings	10	10	26-Oct-26	06-Nov-26
PR.1020	Procurement / Site & Shell - Electrical U/G Conduits Fabrication & Deliver	5	5	09-Nov-26	13-Nov-26
PR.1010	Procurement / Site & Shell - Electrical Duct Bank Material Fabrication & Deliver	5	5	09-Nov-26	13-Nov-26
Fire Protection		94	40	03-Aug-26 A	15-Dec-26
PR.1430	Procurement / Site & Shell - Award Fire Protection Package	20	5	03-Aug-26 A	23-Oct-26
PR.2020	Procurement / Site & Shell - Prepare Fire Protection Submittals / Shop Drawings	20	5	08-Sep-26 A	23-Oct-26
PR.2030	Procurement / Site & Shell - Review & Approve Fire Protection Submittals / Shop Drawings (EOR)	10	10	26-Oct-26	06-Nov-26
PR.2450	Procurement / Site & Shell - Review & Approve Fire Protection Submittals / Shop Drawings (City)	25	25	26-Oct-26	01-Dec-26
PR.1120	Procurement / Site & Shell - Fire Protection Fabricate & Deliver	10	10	02-Dec-26	15-Dec-26
Masonry		45	45	19-Oct-26	22-Dec-26
PR.1560	Procurement / Site & Shell - Award Masonry Package	20	20	19-Oct-26	13-Nov-26
PR.2040	Procurement / Site & Shell - Prepare Masonry Submittals / Shop Drawings	10	10	16-Nov-26	01-Dec-26
PR.2050	Procurement / Site & Shell - Review & Approve Masonry Submittals / Shop Drawings	10	10	02-Dec-26	15-Dec-26
PR.2180	Procurement / Site & Shell - Masonry Material Fabrication & Deliver	5	5	16-Dec-26	22-Dec-26
Drywall		45	45	19-Oct-26	22-Dec-26
PR.1550	Procurement / Site & Shell - Award Drywall Package	20	20	19-Oct-26	13-Nov-26
PR.2060	Procurement / Site & Shell - Prepare Drywall Submittals / Shop Drawings	10	10	16-Nov-26	01-Dec-26
PR.2070	Procurement / Site & Shell - Review & Approve Drywall Submittals / Shop Drawings	10	10	02-Dec-26	15-Dec-26
PR.2190	Procurement / Site & Shell - Drywall Material Fabrication & Deliver	5	5	16-Dec-26	22-Dec-26

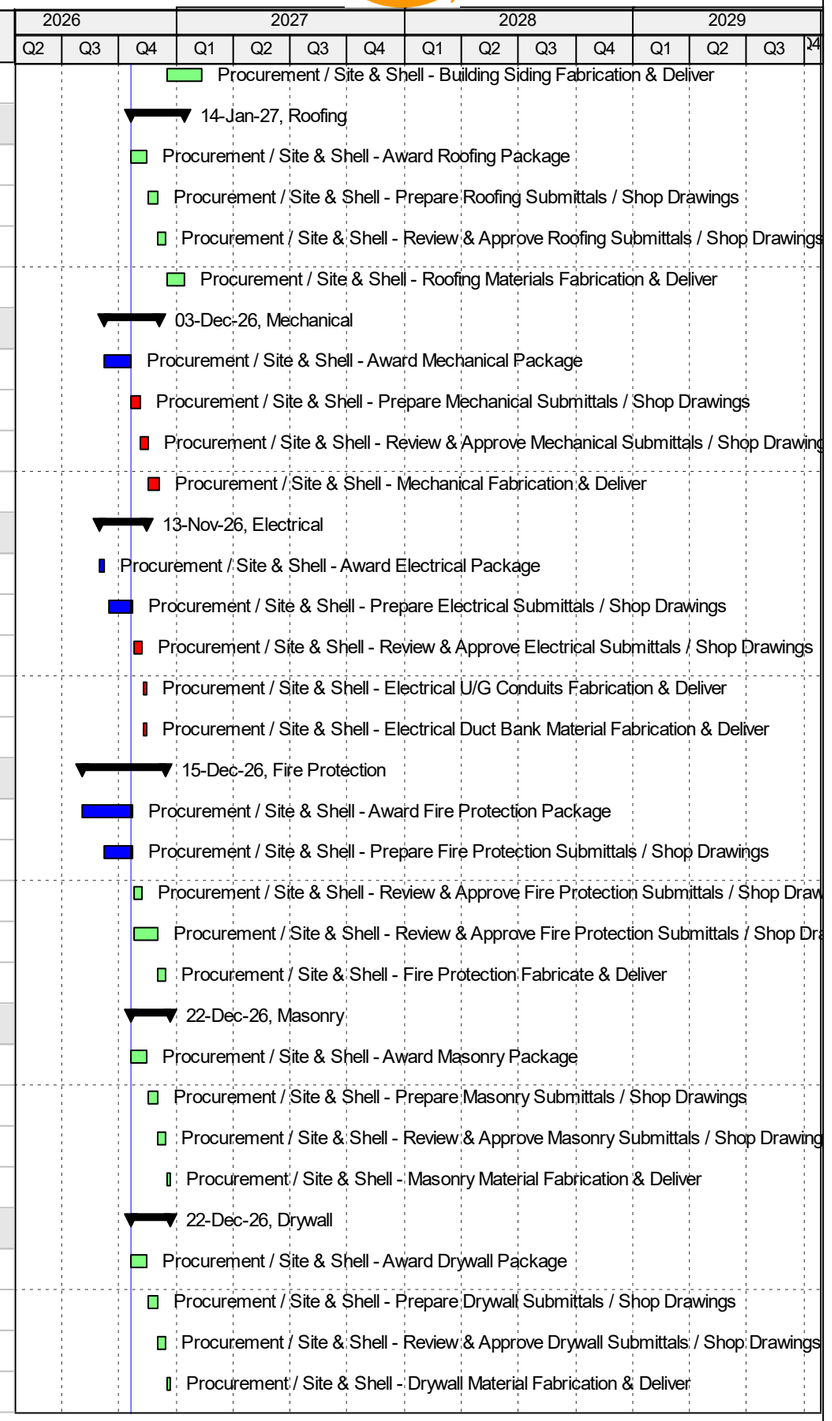

CMH139
Preliminary Schedule


Activity ID	Activity Name	OD	RD	Start	Finish
Paint		45	45	19-Oct-26	22-Dec-26
PR.1540	Procurement / Site & Shell - Award Paint Package	20	20	19-Oct-26	13-Nov-26
PR.2080	Procurement / Site & Shell - Prepare Paint Submittals / Shop Drawings	10	10	16-Nov-26	01-Dec-26
PR.2090	Procurement / Site & Shell - Review & Approve Paint Submittals / Shop Drawings	10	10	02-Dec-26	15-Dec-26
PR.2200	Procurement / Site & Shell - Paint Material Fabrication & Deliver	5	5	16-Dec-26	22-Dec-26
Dock Equipment / Levelers		100	100	19-Oct-26	11-Mar-27
PR.2340	Procurement / Site & Shell - Award Dock Equipment Package	20	20	19-Oct-26	13-Nov-26
PR.2350	Procurement / Site & Shell - Prepare Dock Equipment Submittals / Shop Drawings	10	10	16-Nov-26	01-Dec-26
PR.2360	Procurement / Site & Shell - Review & Approve Dock Equipment Submittals / Shop Drawings	10	10	02-Dec-26	15-Dec-26
PR.1800	Procurement / Site & Shell - Dock Equipment Fabrication & Deliver	60	60	16-Dec-26	11-Mar-27
Turn Stiles		100	100	19-Oct-26	11-Mar-27
PR.2720	Procurement / Site & Shell - Award Turn Stile Package	20	20	19-Oct-26	13-Nov-26
PR.2740	Procurement / Site & Shell - Prepare Turn Stile Submittals / Shop Drawings	10	10	16-Nov-26	01-Dec-26
PR.2750	Procurement / Site & Shell - Review & Approve Turn Stile Submittals / Shop Drawings	10	10	02-Dec-26	15-Dec-26
PR.2730	Procurement / Site & Shell - Fab and Deliver Turn Stiles	60	60	16-Dec-26	11-Mar-27
Glazing		170	170	19-Oct-26	18-Jun-27
PR.2420	Procurement / Site & Shell - Award Glazing Package	20	20	19-Oct-26	13-Nov-26
PR.2430	Procurement / Site & Shell - Prepare Glazing Submittals / Shop Drawings	10	10	16-Nov-26	01-Dec-26
PR.2440	Procurement / Site & Shell - Review & Approve Glazing Submittals / Shop Drawings	10	10	02-Dec-26	15-Dec-26
PR.2410	Procurement / Site & Shell - Glazing Deliver	30	30	07-May-27	18-Jun-27
Louvers & Backdraft Dampers		90	90	19-Oct-26	25-Feb-27
PR.1130	Procurement / Site & Shell - Award Louvers / Backdraft Dampers Package	20	20	19-Oct-26	13-Nov-26
PR.2100	Procurement / Site & Shell - Prepare Louvers / Backdraft Dampers Submittals / Shop Drawings	10	10	16-Nov-26	01-Dec-26
PR.2110	Procurement / Site & Shell - Review & Approve Louvers / Backdraft Dampers Submittals / Shop Drawings	10	10	02-Dec-26	15-Dec-26
PR.1000	Procurement / Site & Shell - Louvers Dampers Fabrication & Deliver	50	50	16-Dec-26	25-Feb-27
PR.2850	Procurement / Site & Shell - Backdraft Dampers Fabrication & Deliver	50	50	16-Dec-26	25-Feb-27
Elevator		160	51	14-May-26 A	31-Dec-26
PR.1420	Procurement / Site & Shell - Award Elevator Package	11	0	14-May-26 A	11-Sep-26 A
PR.1110	Procurement / Site & Shell - Elevators Fabricate & Deliver	90	51	24-Aug-26 A	31-Dec-26
PR.2120	Procurement / Site & Shell - Prepare Elevator Submittals / Shop Drawings	30	5	03-Sep-26 A	23-Oct-26
PR.2130	Procurement / Site & Shell - Review & Approve Elevator Submittals / Shop Drawings	10	10	26-Oct-26	06-Nov-26
Interior		99	70	08-Sep-26 A	28-Jan-27
Doors		70	70	19-Oct-26	28-Jan-27

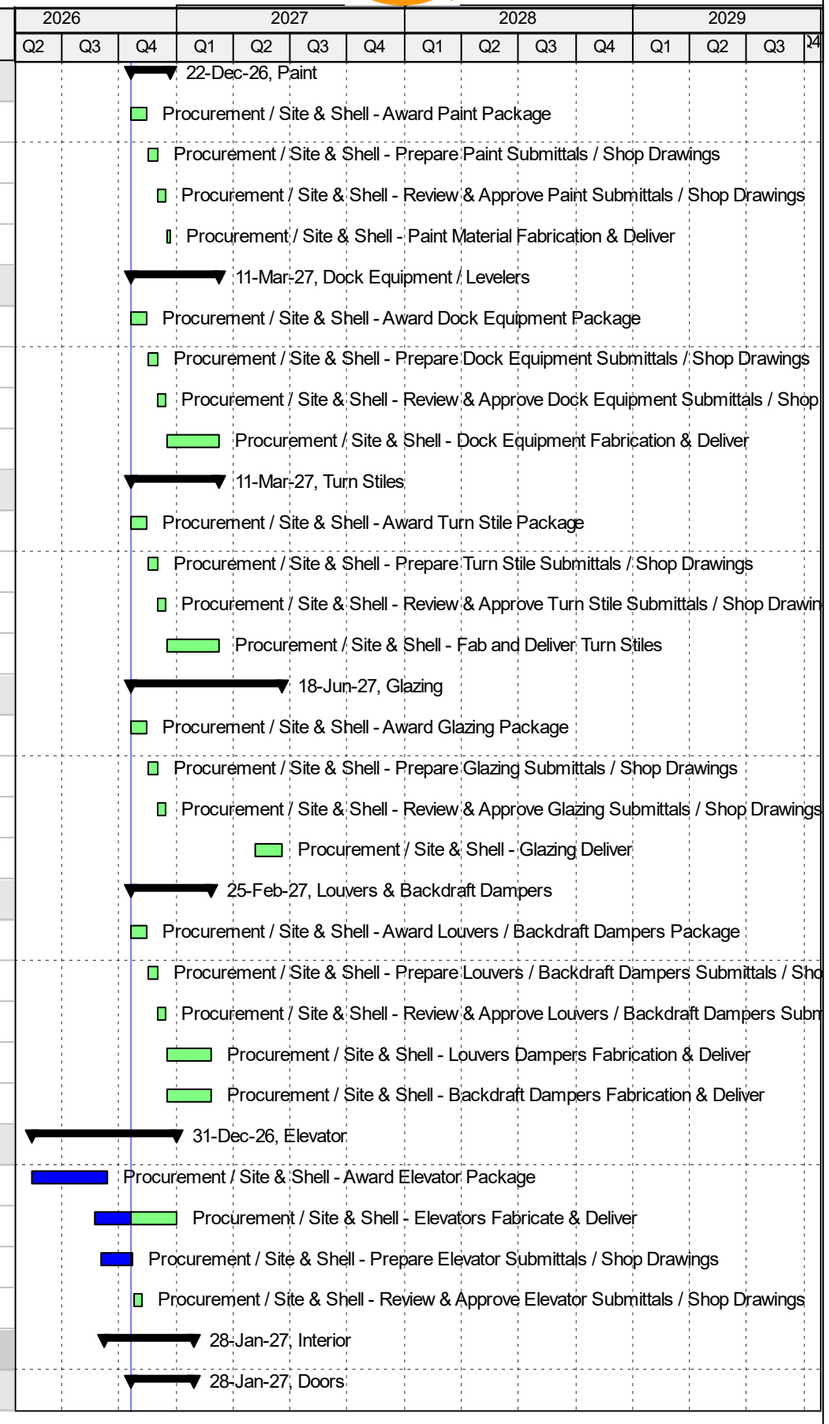

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary


Run Date: 15-Oct-26 14:16
Data Date: 19-Oct-26

Activity ID	Activity Name	OD	RD	Start	Finish
Overhead Doors		45	45	19-Oct-26	22-Dec-26
PR.1530	Procurement / Site & Shell - Award OH Doors Package	20	20	19-Oct-26	13-Nov-26
PR.2230	Procurement / Site & Shell - Prepare OH Doors Submittals / Shop Drawings	10	10	16-Nov-26	01-Dec-26
PR.2240	Procurement / Site & Shell - Review & Approve OH Doors Submittals / Shop Drawings	10	10	02-Dec-26	15-Dec-26
PR.2250	Procurement / Site & Shell - OH Doors Fabrication & Deliver	5	5	16-Dec-26	22-Dec-26
Personnel Doors		70	70	19-Oct-26	28-Jan-27
PR.1520	Procurement / Site & Shell - Award Personnel Doors Package	20	20	19-Oct-26	13-Nov-26
PR.2210	Procurement / Site & Shell - Prepare Personnel Doors Submittals / Shop Drawings	10	10	16-Nov-26	01-Dec-26
PR.2220	Procurement / Site & Shell - Review & Approve Personnel Doors Submittals / Shop Drawings	10	10	02-Dec-26	15-Dec-26
PR.1100	Procurement / Site & Shell - Fab and Deliver Personnel Doors	30	30	16-Dec-26	28-Jan-27
Mechanical		74	45	08-Sep-26 A	22-Dec-26
PR.2570	Procurement / Interior - Award Mechanical Package	5	5	08-Sep-26 A	23-Oct-26
PR.2630	Procurement / Interior - Prepare Mechanical Submittals / Shop Drawings	10	10	26-Oct-26	06-Nov-26
PR.2640	Procurement / Interior - Review & Approve Mechanical Submittals / Shop Drawings	10	10	09-Nov-26	20-Nov-26
PR.2620	Procurement / Interior - Mechanical Fabrication & Deliver	20	20	23-Nov-26	22-Dec-26
Electrical		30	30	19-Oct-26	01-Dec-26
PR.2650	Procurement / Interior - Award Electrical Package	5	5	19-Oct-26	23-Oct-26
PR.2660	Procurement / Interior - Prepare Electrical Submittals / Shop Drawings	10	10	26-Oct-26	06-Nov-26
PR.2580	Procurement / Interior - Review & Approve Electrical Submittals / Shop Drawings	10	10	09-Nov-26	20-Nov-26
PR.2600	Procurement / Interior - Electrical Material Fabrication & Deliver	5	5	23-Nov-26	01-Dec-26
Fire Protection		30	30	19-Oct-26	01-Dec-26
PR.2700	Procurement / Interior - Award Fire Protection Package	20	20	19-Oct-26	13-Nov-26
PR.2710	Procurement / Interior - Fire Protection Fabricate & Deliver	10	10	16-Nov-26	01-Dec-26
Drywall		30	30	19-Oct-26	01-Dec-26
PR.2530	Procurement / Interior - Award Drywall Package	5	5	19-Oct-26	23-Oct-26
PR.2540	Procurement / Interior - Prepare Drywall Submittals / Shop Drawings	10	10	26-Oct-26	06-Nov-26
PR.2550	Procurement / Interior - Review & Approve Drywall Submittals / Shop Drawings	10	10	09-Nov-26	20-Nov-26
PR.2560	Procurement / Interior - Drywall Material Fabrication & Deliver	5	5	23-Nov-26	01-Dec-26
Paint		30	30	19-Oct-26	01-Dec-26
PR.2610	Procurement / Interior - Award Paint Package	5	5	19-Oct-26	23-Oct-26
PR.2670	Procurement / Interior - Prepare Paint Submittals / Shop Drawings	10	10	26-Oct-26	06-Nov-26
PR.2680	Procurement / Interior - Review & Approve Paint Submittals / Shop Drawings	10	10	09-Nov-26	20-Nov-26
PR.2690	Procurement / Interior - Paint Material Fabrication & Deliver	5	5	23-Nov-26	01-Dec-26

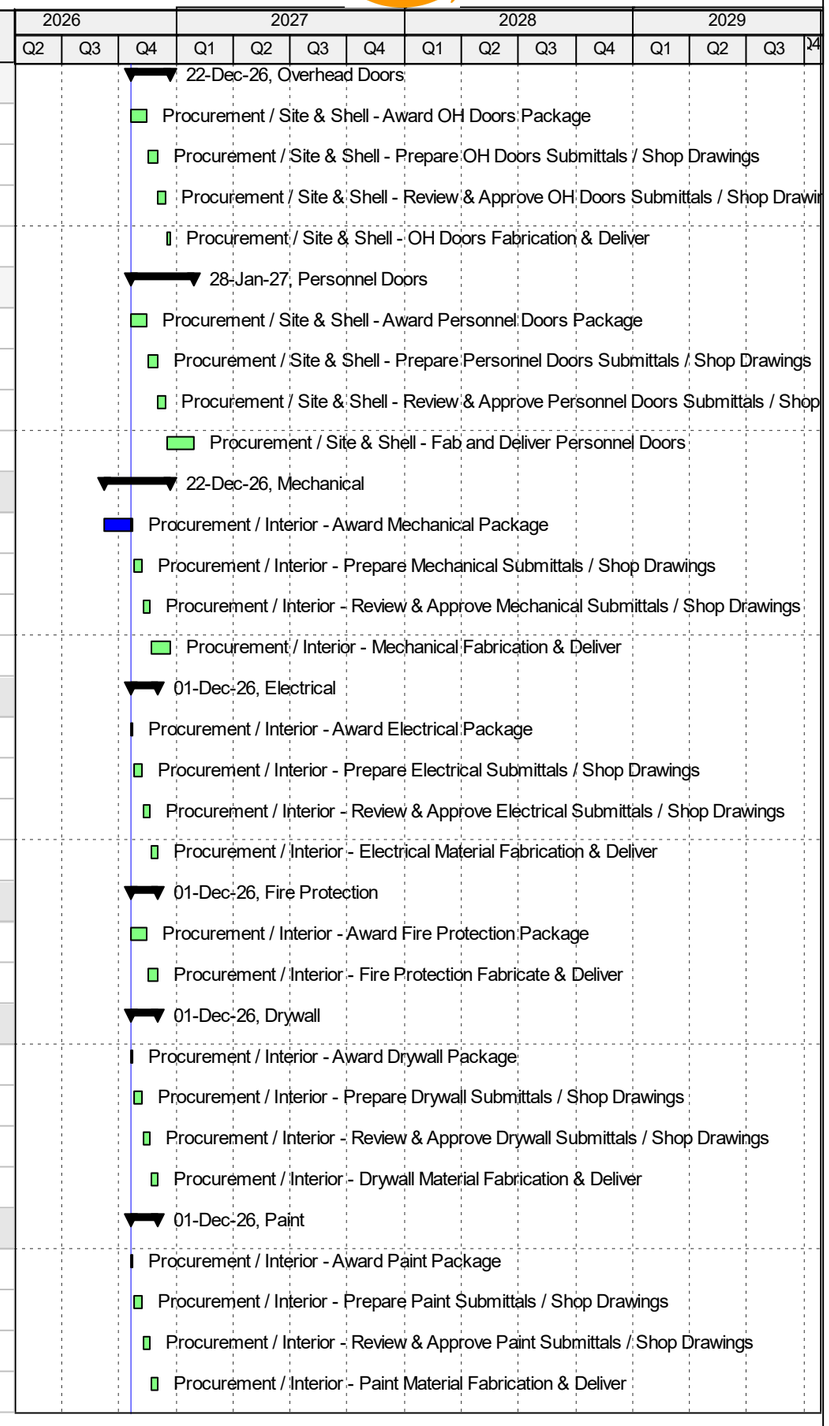

CMH139
Preliminary Schedule


Activity ID	Activity Name	OD	RD	Start	Finish
OFCI		127	127	12-Apr-27	11-Oct-27
Phase 1 (ROMP01 & 03)		0	0	12-Apr-27	12-Apr-27
OFCIP1.310	Phase 1 - OFCI Deliver House Generators [AWS Contract Date 4/12/2027]	0	0		12-Apr-27*
OFCIP1.190	Phase 1 - OFCI Deliver PDCs [AWS Contract Date 4/12/2027]	0	0		12-Apr-27*
OFCIP1.180	Phase 1 - OFCI Deliver Main Service and House UPS [AWS Contract Date 4/12/2027]	0	0		12-Apr-27*
OFCIP1.210	Phase 1 - OFCI Deliver Bus Duct [AWS Contract Date 4/12/2027]	0	0		12-Apr-27*
OFCIP1.160	Phase 1 - OFCI Deliver USB [AWS Contract Date 4/12/2027]	0	0		12-Apr-27*
OFCIP1.150	Phase 1 - OFCI Deliver LV Panels [AWS Contract Date 4/12/2027]	0	0		12-Apr-27*
OFCIP1.140	Phase 1 - OFCI Deliver Transformers [AWS Contract Date 4/12/2027]	0	0		12-Apr-27*
OFCIP1.130	Phase 1 - OFCI Deliver House and MV SWGR [AWS Contract Date 4/12/2027]	0	0		12-Apr-27*
OFCIP1.200	Phase 1 - OFCI Deliver Generators [AWS Contract Date 4/12/2027]	0	0		12-Apr-27*
OFCIP1.120	Phase 1 - OFCI Deliver TAHUs [AWS Contract Date 4/12/2027]	0	0		12-Apr-27*
OFCIP1.100	Phase 1 - OFCI Deliver Racking [AWS Contract Date 4/12/2027]	0	0		12-Apr-27*
OFCIP1.110	Phase 1 - OFCI Deliver AMCOP & BACOP [AWS Contract Date 4/12/2027]	0	0		12-Apr-27*
OFCIP1.330	Phase 1 - OFCI Deliver PDC Whips [AWS Contract Date 4/12/2027]	0	0		12-Apr-27*
OFCIP1.170	Phase 1 - OFCI Deliver UPS [AWS Contract Date 4/12/2027]	0	0		12-Apr-27*
Phase 2 (ROMP02 & 04)		44	44	12-Apr-27	14-Jun-27
OFCIP2.140	Phase 2 - OFCI Deliver Transformers [AWS Contract Date 6/14/2027]	0	0		12-Apr-27*
OFCIP2.190	Phase 2 - OFCI Deliver PDCs & PDC Whips [AWS Contract Date 6/14/2027]	0	0		14-Jun-27*
OFCIP2.210	Phase 2 - OFCI Deliver Bus Duct [AWS Contract Date 6/14/2027]	0	0		14-Jun-27*
OFCIP2.160	Phase 2 - OFCI Deliver USB [AWS Contract Date 6/14/2027]	0	0		14-Jun-27*
OFCIP2.150	Phase 2 - OFCI Deliver LV Panels [AWS Contract Date 6/14/2027]	0	0		14-Jun-27*
OFCIP2.200	Phase 2 - OFCI Deliver Generators [AWS Contract Date 6/14/2027]	0	0		14-Jun-27*
OFCIP2.120	Phase 2 - OFCI Deliver TAHUs [AWS Contract Date 6/14/2027]	0	0		14-Jun-27*
OFCIP2.100	Phase 2 - OFCI Deliver Racking [AWS Contract Date 6/14/2027]	0	0		14-Jun-27*
OFCIP2.110	Phase 2 - OFCI Deliver AMCOP & BACOP [AWS Contract Date 6/14/2027]	0	0		14-Jun-27*
OFCIP2.340	Phase 2 - OFCI Deliver UPS [AWS Contract Date 6/14/2027]	0	0		14-Jun-27*
Phase 3 (ROMP05 & 07)		63	63	12-Apr-27	12-Jul-27
OFCIP5.140	Phase 3 - OFCI Deliver Transformers [AWS Contract Date 7/12/2027]	0	0		12-Apr-27*
OFCIP5.190	Phase 3 - OFCI Deliver PDCs & PDC Whips [AWS Contract Date 7/12/2027]	0	0		12-Jul-27*
OFCIP5.180	Phase 3 - OFCI Deliver UPS [AWS Contract Date 7/12/2027]	0	0		12-Jul-27*
OFCIP5.210	Phase 3 - OFCI Deliver Bus Duct [AWS Contract Date 7/12/2027]	0	0		12-Jul-27*
OFCIP5.160	Phase 3 - OFCI Deliver USB [AWS Contract Date 7/12/2027]	0	0		12-Jul-27*

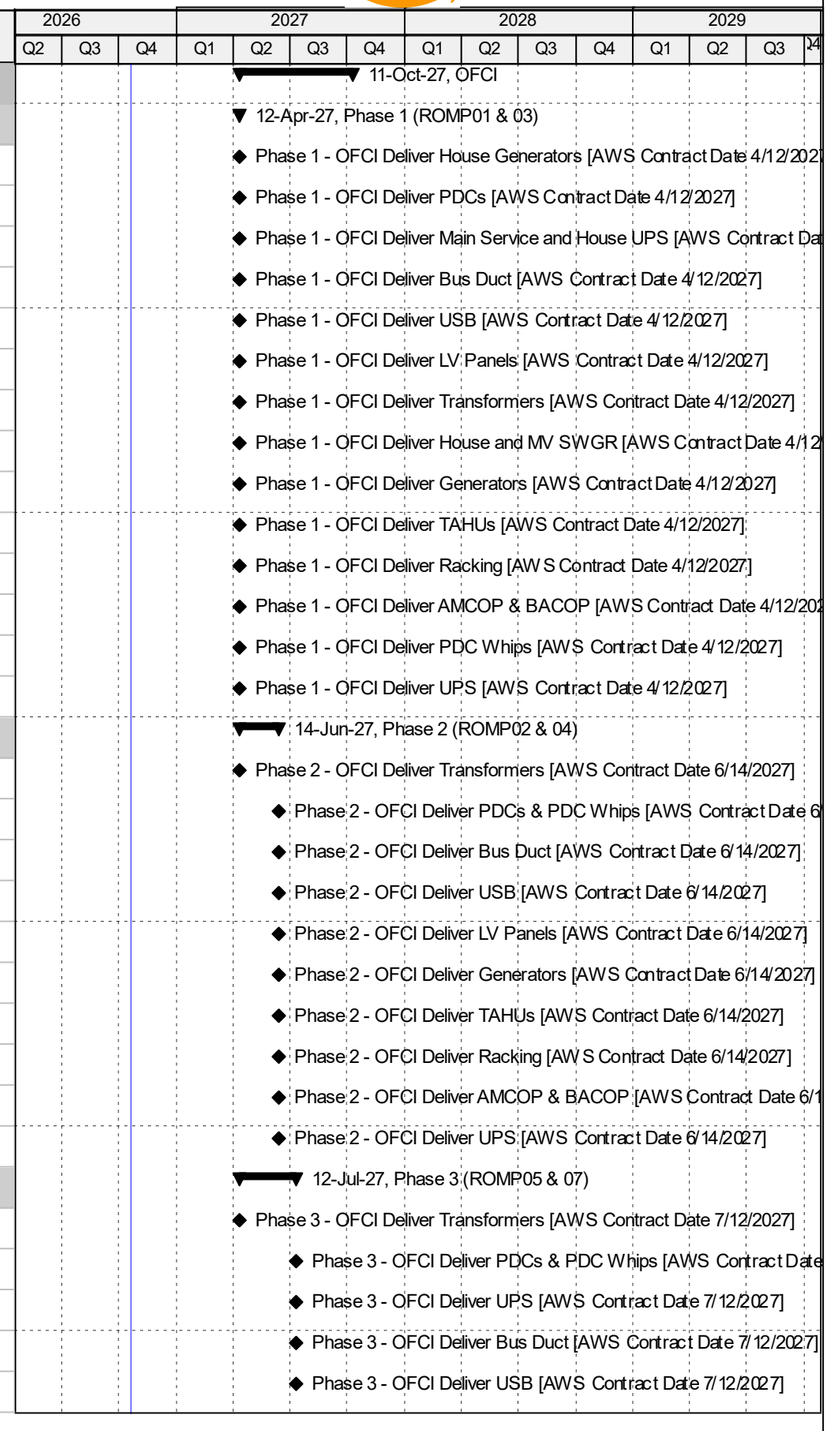


Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

Run Date: 15-Oct-26 14:16
Data Date: 19-Oct-26


Activity ID	Activity Name	OD	RD	Start	Finish
OFCIP5.150	Phase 3 - OFCI Deliver LV Panels [AWS Contract Date 7/12/2027]	0	0		12-Jul-27*
OFCIP5.200	Phase 3 - OFCI Deliver Generators [AWS Contract Date 7/12/2027]	0	0		12-Jul-27*
OFCIP5.120	Phase 3 - OFCI Deliver TAHUs [AWS Contract Date 7/12/2027]	0	0		12-Jul-27*
OFCIP5.100	Phase 3 - OFCI Deliver Racking [AWS Contract Date 7/12/2027]	0	0		12-Jul-27*
OFCIP5.110	Phase 3 - OFCI Deliver AMCOP & BACOP [AWS Contract Date 7/12/2027]	0	0		12-Jul-27*
Phase 4 (ROMP06 & 08)		83	83	12-Apr-27	09-Aug-27
OFCIP6.140	Phase 4 - OFCI Deliver Transformers [AWS Contract Date 8/09/2027]	0	0		12-Apr-27*
OFCIP6.190	Phase 4 - OFCI Deliver PDCs & PDC Whips [AWS Contract Date 8/09/2027]	0	0		09-Aug-27*
OFCIP6.180	Phase 4 - OFCI Deliver UPS [AWS Contract Date 8/09/2027]	0	0		09-Aug-27*
OFCIP6.210	Phase 4 - OFCI Deliver Bus Duct [AWS Contract Date 8/09/2027]	0	0		09-Aug-27*
OFCIP6.160	Phase 4 - OFCI Deliver USB [AWS Contract Date 8/09/2027]	0	0		09-Aug-27*
OFCIP6.150	Phase 4 - OFCI Deliver LV Panels [AWS Contract Date 8/09/2027]	0	0		09-Aug-27*
OFCIP6.200	Phase 4 - OFCI Deliver Generators [AWS Contract Date 8/09/2027]	0	0		09-Aug-27*
OFCIP6.120	Phase 4 - OFCI Deliver TAHUs [AWS Contract Date 8/09/2027]	0	0		09-Aug-27*
OFCIP6.100	Phase 4 - OFCI Deliver Racking [AWS Contract Date 8/09/2027]	0	0		09-Aug-27*
OFCIP6.110	Phase 4 - OFCI Deliver AMCOP & BACOP [AWS Contract Date 8/09/2027]	0	0		09-Aug-27*
Phase 5 (ROMP09 & 11)		102	102	12-Apr-27	07-Sep-27
OFCIP6.500	Phase 5 - OFCI Deliver Transformers [AWS Contract Date 9/06/2027]	0	0		12-Apr-27*
OFCIP6.440	Phase 5 - OFCI Deliver PDCs & PDC Whips [AWS Contract Date 9/06/2027]	0	0		07-Sep-27*
OFCIP6.450	Phase 5 - OFCI Deliver UPS [AWS Contract Date 9/06/2027]	0	0		07-Sep-27*
OFCIP6.460	Phase 5 - OFCI Deliver Bus Duct [AWS Contract Date 9/06/2027]	0	0		07-Sep-27*
OFCIP6.480	Phase 5 - OFCI Deliver USB [AWS Contract Date 9/06/2027]	0	0		07-Sep-27*
OFCIP6.490	Phase 5 - OFCI Deliver LV Panels [AWS Contract Date 9/06/2027]	0	0		07-Sep-27*
OFCIP6.510	Phase 5 - OFCI Deliver Generators [AWS Contract Date 9/06/2027]	0	0		07-Sep-27*
OFCIP9.120	Phase 5 - OFCI Deliver TAHUs [AWS Contract Date 9/06/2027]	0	0		07-Sep-27*
OFCIP6.530	Phase 5 - OFCI Deliver Racking [AWS Contract Date 9/06/2027]	0	0		07-Sep-27*
OFCIP6.540	Phase 5 - OFCI Deliver AMCOP & BACOP [AWS Contract Date 9/06/2027]	0	0		07-Sep-27*
Phase 6 (ROMP10 & 12)		127	127	12-Apr-27	11-Oct-27
OFCIP6.610	Phase 6 - OFCI Deliver Transformers [AWS Contract Date 10/11/2027]	0	0		12-Apr-27*
OFCIP6.550	Phase 6 - OFCI Deliver PDCs & PDC Whips [AWS Contract Date 10/11/2027]	0	0		11-Oct-27*
OFCIP6.560	Phase 6 - OFCI Deliver UPS [AWS Contract Date 10/11/2027]	0	0		11-Oct-27*
OFCIP6.570	Phase 6 - OFCI Deliver Bus Duct [AWS Contract Date 10/11/2027]	0	0		11-Oct-27*
OFCIP6.590	Phase 6 - OFCI Deliver USB [AWS Contract Date 10/11/2027]	0	0		11-Oct-27*

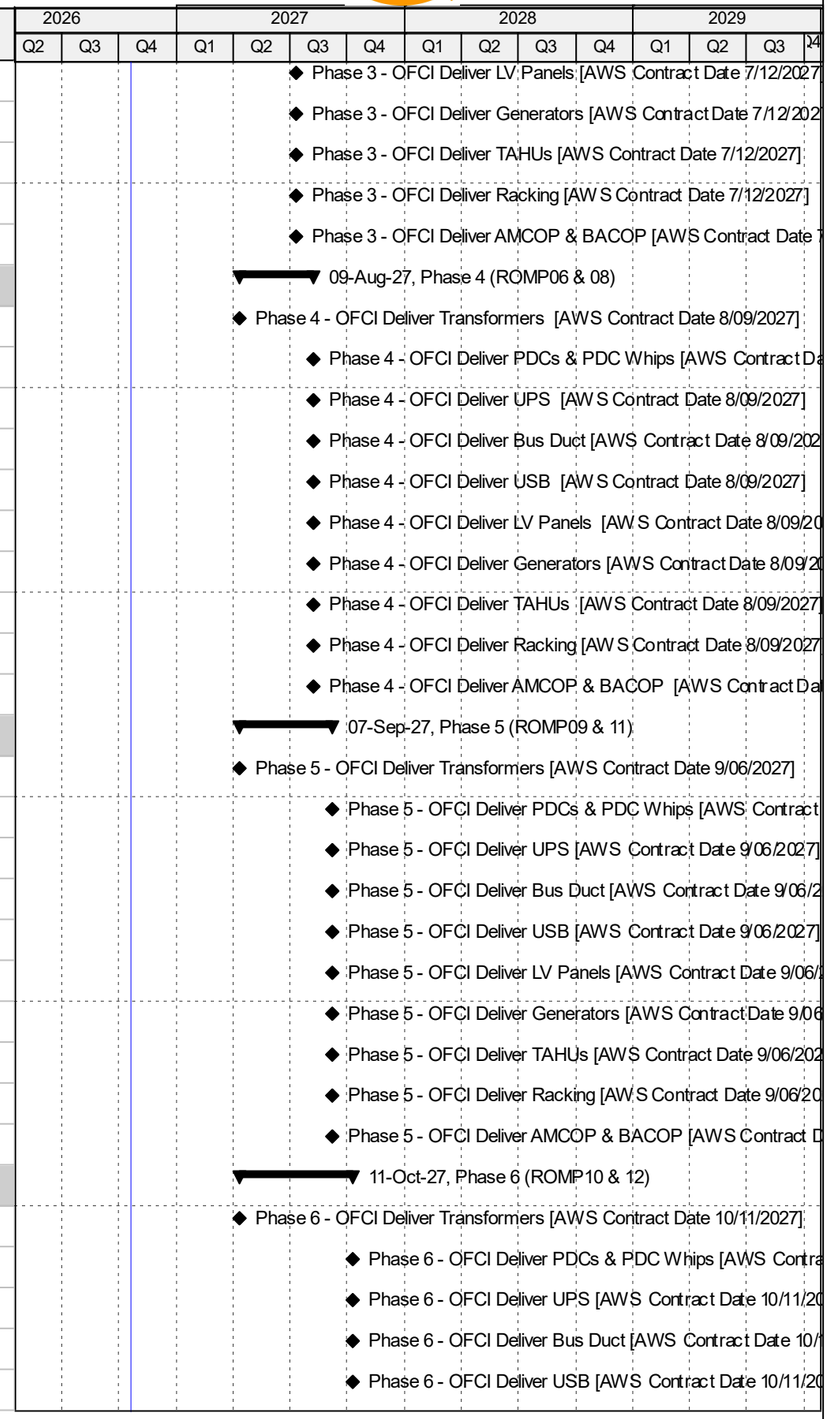


Activity ID	Activity Name	OD	RD	Start	Finish
OFCIP6.600	Phase 6 - OFCI Deliver LV Panels [AWS Contract Date 10/11/2027]	0	0		11-Oct-27*
OFCIP6.620	Phase 6 - OFCI Deliver Generators [AWS Contract Date 10/11/2027]	0	0		11-Oct-27*
OFCIP10.120	Phase 6 - OFCI Deliver TAHUs [AWS Contract Date 10/11/2027]	0	0		11-Oct-27*
OFCIP6.640	Phase 6 - OFCI Deliver Racking [AWS Contract Date 10/11/2027]	0	0		11-Oct-27*
OFCIP6.650	Phase 6 - OFCI Deliver AMCOP & BACOP [AWS Contract Date 10/11/2027]	0	0		11-Oct-27*
Long Lead Equipment		271	271	19-Oct-26	10-Nov-27
Phase 1 (ROMP01 & 03)		230	230	19-Oct-26	14-Sep-27
P1LLE160	Phase 1 LLE - VRF Delivery	20	20	19-Oct-26	13-Nov-26
P1LLE150	Phase 1 LLE - Doors & Hardware	60	60	19-Oct-26	14-Jan-27
P1LLE170	Phase 1 LLE - Hot Aisle Containment (Polycarbonate Panels)	50	50	19-Oct-26	30-Dec-26
P1LLE130	Phase 1 LLE - Pressure Relief Dampers	45	45	19-Oct-26	22-Dec-26
P1LLE120	Phase 1 LLE - Cable Bus/Tray/Basket/Wire	30	30	19-Oct-26	01-Dec-26
P1LLE110	Phase 1 LLE - Fab & Deliver CFCI IW Tanks	60	60	19-Oct-26	14-Jan-27
P1LLE100	Phase 1 LLE - MV Cable	160	160	19-Oct-26	04-Jun-27
P1LLE140	Phase 1 LLE - CRAC Units	230	230	19-Oct-26	14-Sep-27
P1LLE180	Phase 1 LLE - Generator Platforms	20	20	09-Jul-27	05-Aug-27
Phase 2 (ROMP02 & 04)		230	230	19-Oct-26	14-Sep-27
P2LLE140	Phase 2 LLE - Doors & Hardware	10	10	19-Oct-26	30-Oct-26
P2LLE150	Phase 2 LLE - Hot Aisle Containment (Polycarbonate Panels)	10	10	19-Oct-26	30-Oct-26
P2LLE130	Phase 2 LLE - Pressure Relief Dampers	10	10	19-Oct-26	30-Oct-26
P2LLE100	Phase 2 LLE - Cable Bus/Tray/Basket/Wire	10	10	19-Oct-26	30-Oct-26
P2LLE160	Phase 2 LLE - CRAC Units	230	230	19-Oct-26	14-Sep-27
P2LLE120	Phase 2 LLE - Generator Platforms	20	20	12-Jul-27	06-Aug-27
Phase 3 (ROMP05 & 07)		230	230	19-Oct-26	14-Sep-27
P3LLE130	Phase 3 LLE - Doors & Hardware	10	10	19-Oct-26	30-Oct-26
P3LLE150	Phase 3 LLE - Hot Aisle Containment (Polycarbonate Panels)	10	10	19-Oct-26	30-Oct-26
P3LLE140	Phase 3 LLE - Pressure Relief Dampers	10	10	19-Oct-26	30-Oct-26
P3LLE100	Phase 3 LLE - Cable Bus/Tray/Basket/Wire	10	10	19-Oct-26	30-Oct-26
P3LLE160	Phase 3 LLE - CRAC Units	230	230	19-Oct-26	14-Sep-27
P3LLE110	Phase 3 LLE - Generator Platforms	20	20	19-Jul-27	13-Aug-27
Phase 4 (ROMP06 & 08)		230	230	19-Oct-26	14-Sep-27
P4LLE120	Phase 4 LLE - Doors & Hardware	10	10	19-Oct-26	30-Oct-26
P4LLE140	Phase 4 LLE - Hot Aisle Containment (Polycarbonate Panels)	10	10	19-Oct-26	30-Oct-26

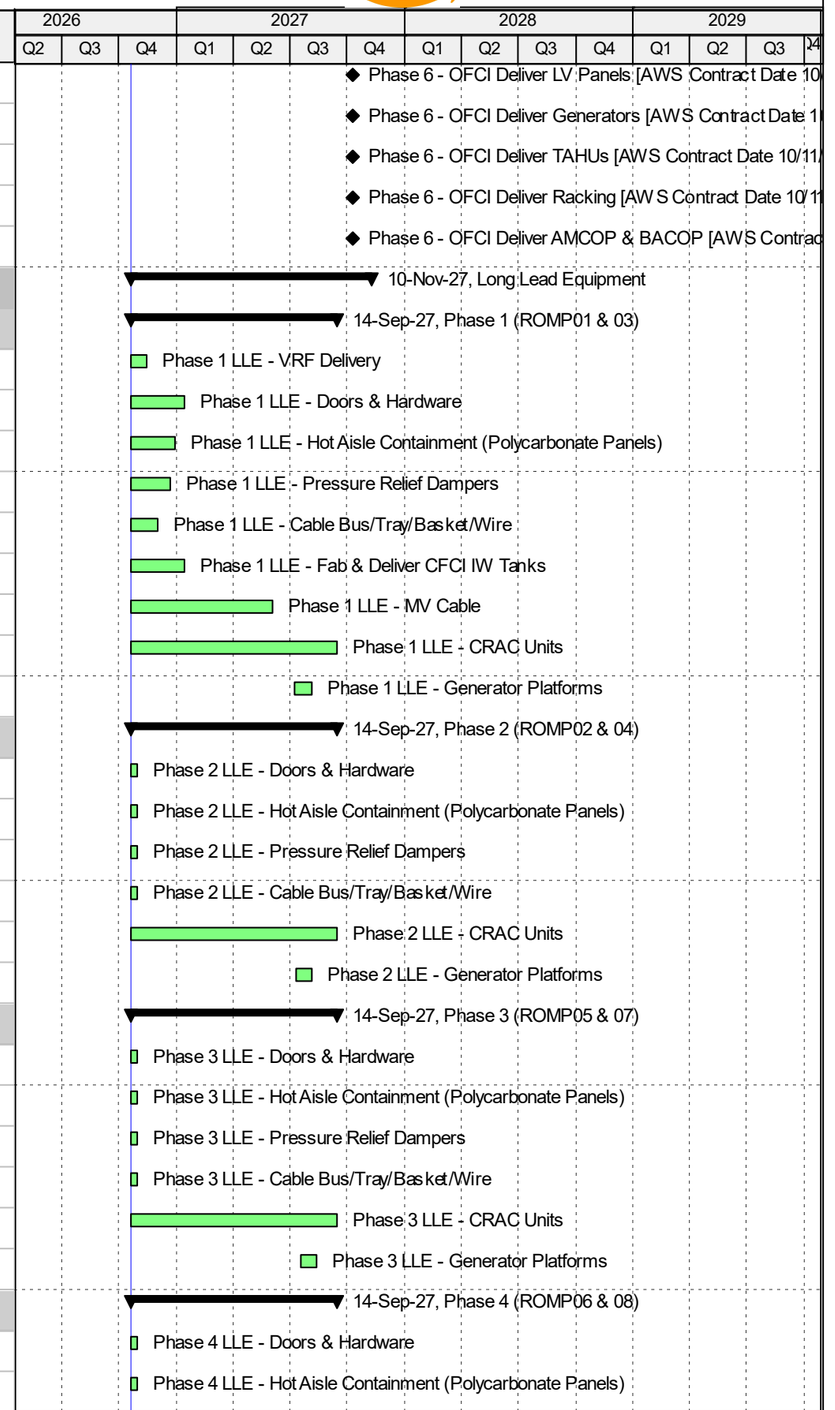


Activity ID	Activity Name	OD	RD	Start	Finish
P4LLE130	Phase 4 LLE - Pressure Relief Dampers	10	10	19-Oct-26	30-Oct-26
P4LLE110	Phase 4 LLE - Cable Bus/Tray/Basket/Wire	10	10	19-Oct-26	30-Oct-26
P4LLE150	Phase 4 LLE - CRAC Units	230	230	19-Oct-26	14-Sep-27
P4LLE160	Phase 4 LLE - Generator Platforms	20	20	12-Aug-27	09-Sep-27
Phase 5 (ROMP09 & 11)		246	246	19-Oct-26	06-Oct-27
P5LLE120	Phase 5 LLE - Doors & Hardware	10	10	19-Oct-26	30-Oct-26
P5LLE140	Phase 5 LLE - Hot Aisle Containment (Polycarbonate Panels)	10	10	19-Oct-26	30-Oct-26
P5LLE130	Phase 5 LLE - Pressure Relief Dampers	10	10	19-Oct-26	30-Oct-26
P5LLE100	Phase 5 LLE - Cable Bus/Tray/Basket/Wire	10	10	19-Oct-26	30-Oct-26
P5LLE150	Phase 5 LLE - CRAC Units	230	230	19-Oct-26	14-Sep-27
P5LLE170	Phase 5 LLE - Generator Platforms	20	20	09-Sep-27	06-Oct-27
Phase 6 (ROMP10 & 12)		271	271	19-Oct-26	10-Nov-27
P6LLE120	Phase 6 LLE - Doors & Hardware	10	10	19-Oct-26	30-Oct-26
P6LLE140	Phase 6 LLE - Hot Aisle Containment (Polycarbonate Panels)	10	10	19-Oct-26	30-Oct-26
P6LLE130	Phase 6 LLE - Pressure Relief Dampers	10	10	19-Oct-26	30-Oct-26
P6LLE100	Phase 6 LLE - Cable Bus/Tray/Basket/Wire	10	10	19-Oct-26	30-Oct-26
P6LLE150	Phase 6 LLE - CRAC Units	230	230	19-Oct-26	14-Sep-27
P6LLE180	Phase 6 LLE - Generator Platforms	20	20	14-Oct-27	10-Nov-27
Construction		448	389	27-Jul-26 A	28-Apr-28
Site		269	190	27-Jul-26 A	16-Aug-27
Sitework		269	190	27-Jul-26 A	16-Aug-27
SI.1000	Site - Mobilization	1	0	27-Jul-26 A	27-Jul-26 A
SI.1010	Site - Install Rammed Aggregate Piers	20	0	29-Jul-26 A	05-Aug-26 A
SI.1470	Site - DLB Conduits (FLORES)	10	10	16-Nov-26	01-Dec-26
SI.3130	Site - Set Security Poles	5	5	16-Nov-26	20-Nov-26
SI.1390	Site - Connect SA & IWW to Vault	3	3	05-Jan-27	07-Jan-27
SI.1440	Site - Install IWW Meter / Pump	3	3	08-Jan-27	12-Jan-27
SI.1500	Site - Energize IWW / SA Commission	5	5	13-Jan-27	19-Jan-27
SI.1800	Site - Fine Grade & Stone Utility / Gen Yard	5	5	15-Jan-27	21-Jan-27
SI.1620	Site - Excavate Loading Dock	3	3	26-Apr-27	28-Apr-27
SI.1750	Site - South Storm Bldg Tie In	6	6	28-Apr-27	05-May-27
SI.1760	Site - MV-A, MV-B Pad - Prep / Place / Cure	3	3	30-Apr-27	04-May-27
SI.1770	Site - North Storm Bldg Tie In	3	3	30-Apr-27	04-May-27

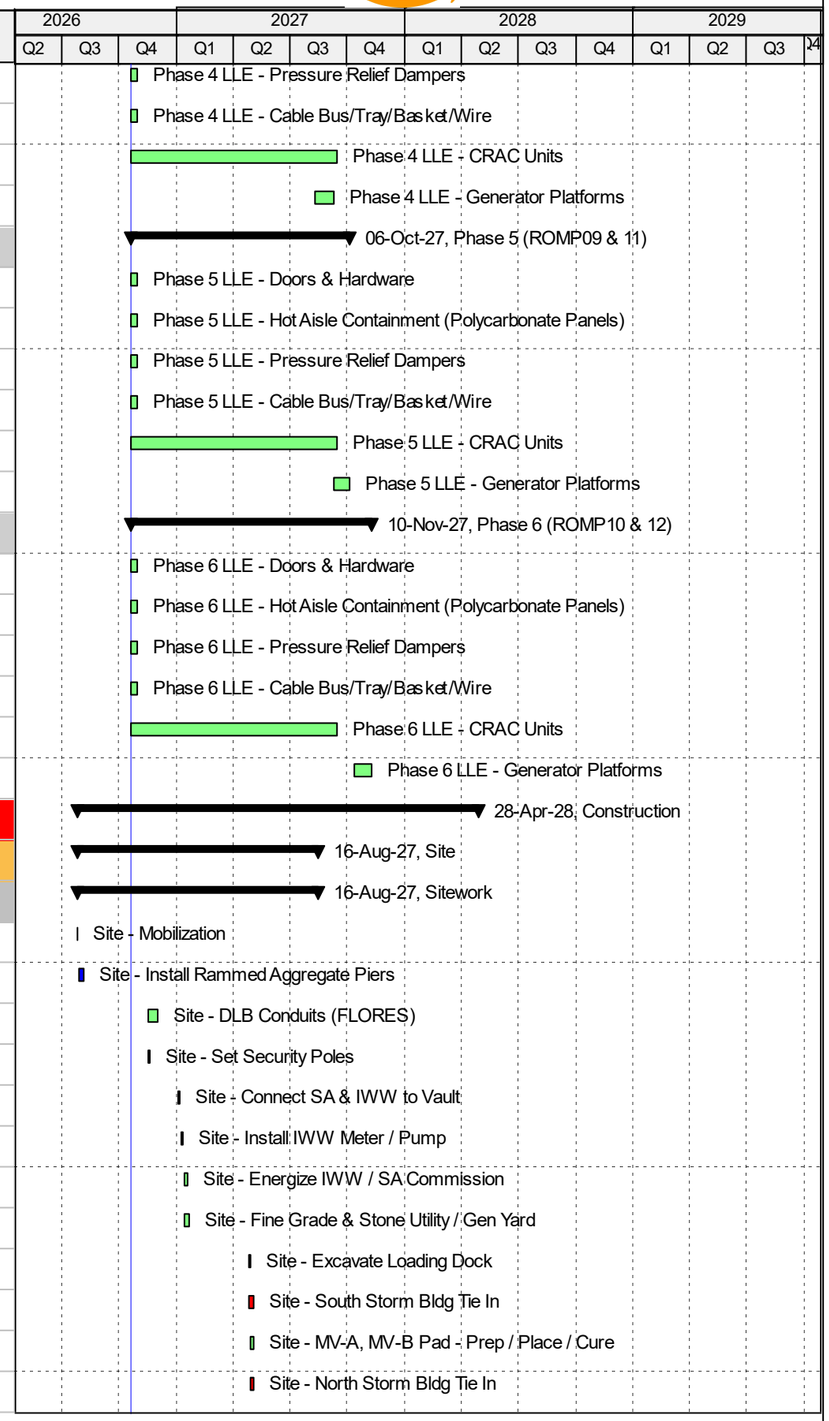

Activity ID	Activity Name	OD	RD	Start	Finish
SI.1810	Site - Set MV-A & MV-B Switchgears	4	4	05-May-27	10-May-27
SI.1830	Site - Inspection of MV Gear	2	2	12-May-27	13-May-27
SI.1740	Site - Prep / Place / Cure East Screen Wall / Dumpster Foundations	3	3	13-May-27	17-May-27
SI.1820	Site - Pull MV Feeders - MV-A & MV-B	5	5	07-Jun-27	11-Jun-27
SI.1700	Site - Prep / Place / Cure Concrete Pavement (Loading Dock)	7	7	07-Jun-27	15-Jun-27
SI.1840	Site - Power Solutions Terminate & Testing of MV Feeders	4	4	14-Jun-27	17-Jun-27
SI.1850	Site - Energize MV Switchgear	2	2	18-Jun-27	21-Jun-27
SI.1710	Site - Prep / Place / Cure Sidewalks	15	15	29-Jun-27	20-Jul-27
SI.1720	Site - Site Finalization	19	19	21-Jul-27	16-Aug-27
Structure		320	261	27-Jul-26 A	27-Oct-27
Foundation		209	205	13-Oct-26 A	09-Aug-27
CN1720	Structure / Foundations - F/R/P Fdns Seq 1 - Blue Elevator Pits	5	1	13-Oct-26 A	19-Oct-26
CN1730	Structure / Foundations - F/R/P Fdns Seq 2 - Red 14-1 Line	5	5	19-Oct-26	23-Oct-26
CN1750	Structure / Foundations - F/R/P Fdns Seq 4 - Green	5	5	26-Oct-26	30-Oct-26
CN1820	Structure / Foundations - Install Stem Wall (Red)	10	10	26-Oct-26	06-Nov-26
CN1760	Structure / Foundations - F/R/P Fdns Seq 5 - Light Blue	4	4	02-Nov-26	05-Nov-26
CN1980	Structure / Foundations - Install Stem Wall (Green)	10	10	02-Nov-26	13-Nov-26
CN1780	Structure / Foundations - F/R/P Fdns Seq 7 - Yellow	7	7	06-Nov-26	16-Nov-26
CN1770	Structure / Foundations - F/R/P Fdns Seq 6 - Gray	3	3	17-Nov-26	19-Nov-26
CN1740	Structure / Foundations - F/R/P Fdns Seq 3 - Screen Wall Foundations & Piers (G.1 Line - 3-20.1)	10	10	31-Dec-26	14-Jan-27
CN1810	Structure / Foundations - F/R/P Fdns Seq 9 - MV Pads	4	4	31-Dec-26	06-Jan-27
SH.1620	Structure / Foundations - SOG Prep / Pour 1 (CL 1-4)	5	5	05-Jan-27	11-Jan-27
SH.1670	Structure / Foundations - SOG Prep / Pour 2 (CL 4-7)	5	5	08-Jan-27	14-Jan-27
SH.1720	Structure / Foundations - SOG Prep / Pour 3 (CL 7-12)	6	6	13-Jan-27	20-Jan-27
SH.1750	Structure / Foundations - SOG Prep / Pour 4 (CL 12-16)	6	6	26-Jan-27	02-Feb-27
SH.2500	Structure / Foundations - SOG Prep / Pour 5 (16-21)	6	6	29-Jan-27	05-Feb-27
SH.2510	Structure / Foundations - L2 Mezz SOMD Prep / Pour 1 (CL 3-10)	3	3	26-Mar-27	30-Mar-27
SH.2841	Structure / Foundations - L2 SOMD Prep / Pour 1 (CL 1-3)	4	4	31-Mar-27	05-Apr-27
SH.2851	Structure / Foundations - L2 SOMD Prep / Pour 2 (CL 3-5)	4	4	05-Apr-27	08-Apr-27
SH.2861	Structure / Foundations - L2 SOMD Prep / Pour 3 (CL 5-7)	4	4	08-Apr-27	13-Apr-27
SH.2871	Structure / Foundations - L2 SOMD Prep / Pour 4 (CL 7-10)	4	4	13-Apr-27	16-Apr-27
SH.2921	Structure / Foundations - L1 Mezz SOMD Prep / Pour 1 (CL 1-3)	3	3	16-Apr-27	20-Apr-27
SH.2931	Structure / Foundations - L1 Mezz SOMD Prep / Pour 2 (CL 3-10)	3	3	20-Apr-27	22-Apr-27

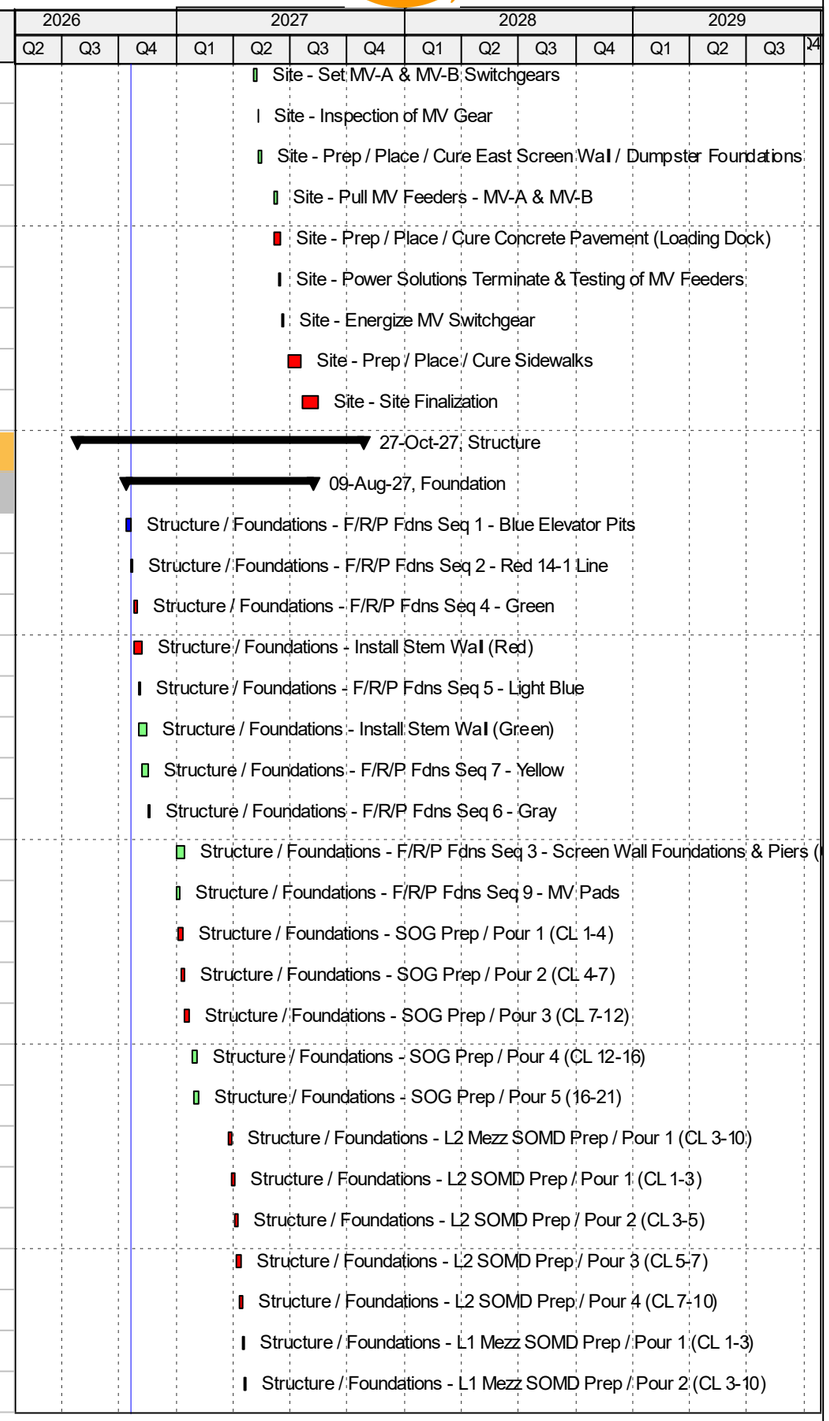

Activity ID	Activity Name	OD	RD	Start	Finish
SH.2831	Structure / Foundations - L2 Mezz SOMD Prep / Pour 2 (CL 10-21)	3	3	22-Apr-27	26-Apr-27
SH.2881	Structure / Foundations - L2 SOMD Prep / Pour 5 (CL 10-14)	4	4	26-Apr-27	29-Apr-27
SH.2891	Structure / Foundations - L2 SOMD Prep / Pour 6 (CL 14-17)	4	4	29-Apr-27	04-May-27
SH.2901	Structure / Foundations - L2 SOMD Prep / Pour 7 (CL 17-20)	4	4	04-May-27	07-May-27
CN1840	Structure / Foundations - F/R/P Fdns Seq 12 - IW Tank Foundation	4	4	07-May-27	12-May-27
SH.2941	Structure / Foundations - L1 Mezz SOMD Prep / Pour 3	3	3	07-May-27	11-May-27
CN1850	Structure / Foundations - F/R/P Fdns Seq 13 - Fuel Tank Pads	4	4	13-May-27	18-May-27
CN1830	Structure / Foundations - F/R/P Fdns Seq 11 - Loading Dock Foundation / Walls	9	9	16-Jun-27	28-Jun-27
CN1860	Structure / Foundations - F/R/P Fdns Seq 14 - T-Steel Foundations	22	22	09-Jul-27	09-Aug-27
Underground		127	48	27-Jul-26 A	26-Jan-27
CN15870	Structure / UG - Install Soil Improvements	8	0	27-Jul-26 A	05-Aug-26 A
CN3000	Structure / UG - Install Domestic Water & Fire Suppression Piping	10	10	16-Nov-26	01-Dec-26
SH.1460	Structure / UG - Install U/G Fiber	10	10	16-Nov-26	01-Dec-26
CN1390	Structure / UG - Install U/G Sanitary Piping	5	5	24-Nov-26	02-Dec-26
SH.1470	Structure / UG - Install U/G Security Conduits	5	5	02-Dec-26	08-Dec-26
SH.1500	Structure / UG - Install U/G Electrical	5	5	02-Dec-26	08-Dec-26
CN6610	Structure / UG - Install U/G Plumbing (Line 1 - 10)	20	20	04-Dec-26	04-Jan-27
SH.1280	Structure / UG - Underslab Power (MV)	4	4	05-Jan-27	08-Jan-27
CN6620	Structure / UG - Install U/G Plumbing (Line 10 - 22)	15	15	05-Jan-27	25-Jan-27
SH.1310	Structure / UG - Underslab Controls	5	5	07-Jan-27	13-Jan-27
SH.1400	Structure / UG - Underslab Grounding - Pour 1	2	2	11-Jan-27	12-Jan-27
SH.2590	Structure / UG - Underslab Grounding - Pours 2 to 6	9	9	14-Jan-27	26-Jan-27
Structural Steel		54	54	25-Jan-27	08-Apr-27
Erection		42	42	25-Jan-27	13-Mar-27
SH.1150	Structural Steel - Erect Steel Frame & Joists Seq 1 (CL 1-3)	11	11	25-Jan-27	05-Feb-27
SH.1200	Structural Steel - Erect Steel Frame & Joists Seq 2 (CL 3-5)	9	9	01-Feb-27	10-Feb-27
SH.1250	Structural Steel - Erect Steel Frame & Joists Seq 3 (CL 5-7)	9	9	05-Feb-27	15-Feb-27
SH.1370	Structural Steel - Erect Steel Frame & Joists Seq 4 (CL 7-9)	9	9	10-Feb-27	19-Feb-27
SH.1430	Structural Steel - Erect Steel Frame & Joists Seq 5 (CL 9-11)	8	8	15-Feb-27	23-Feb-27
SH.1480	Structural Steel - Erect Steel Frame & Joists Seq 6 (CL 11-13)	8	8	19-Feb-27	27-Feb-27
SH.2310	Structural Steel - Erect Steel Frame & Joists Seq 7 (CL 13-16)	8	8	24-Feb-27	04-Mar-27
SH.1110	Structural Steel - Erect Steel Frame & Joists Seq 8 (CL 16-18)	8	8	01-Mar-27	09-Mar-27
SH.3361	Structural Steel - Erect Steel Frame & Joists Seq 9 (CL 18-20)	8	8	05-Mar-27	13-Mar-27

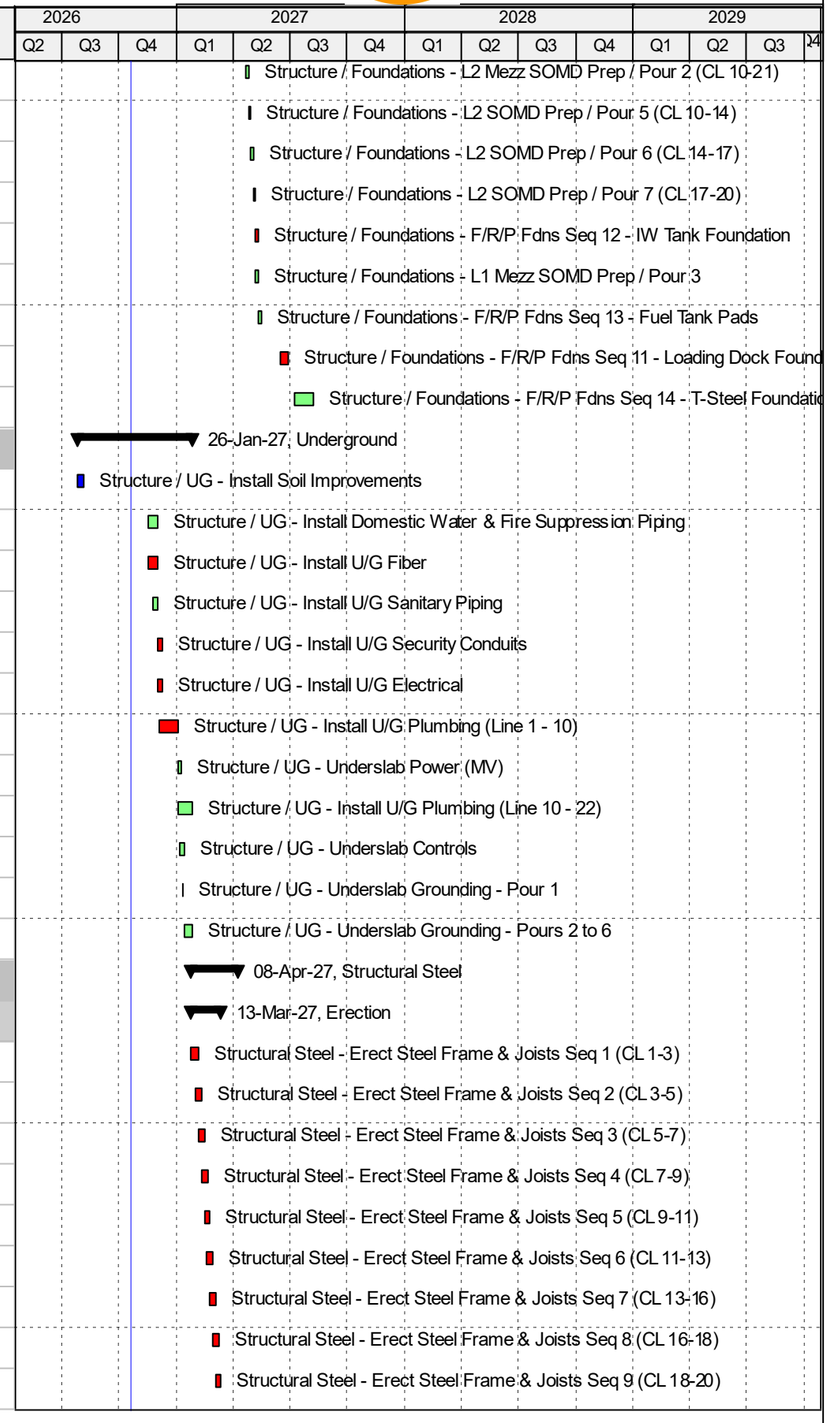


Gray

CMH139
Preliminary Schedule

aws


Activity ID	Activity Name	OD	RD	Start	Finish
Detailing		42	42	01-Feb-27	20-Mar-27
SH.1170	Structural Steel - Steel Detailing Seq 1 (CL 1-3)	12	12	01-Feb-27	13-Feb-27
SH.2400	Structural Steel - Steel Detailing Seq 2 (CL 3-5)	9	9	05-Feb-27	15-Feb-27
SH.2430	Structural Steel - Steel Detailing Seq 3 (CL 5-7)	11	11	10-Feb-27	22-Feb-27
SH.2410	Structural Steel - Steel Detailing Seq 4 (CL 7-9)	11	11	15-Feb-27	26-Feb-27
SH.2420	Structural Steel - Steel Detailing Seq 5 (CL 9-11)	10	10	19-Feb-27	02-Mar-27
SH.2440	Structural Steel - Steel Detailing Seq 6 (CL 11-13)	10	10	24-Feb-27	06-Mar-27
SH.2390	Structural Steel - Steel Detailing Seq 7 (CL 13-16)	10	10	01-Mar-27	11-Mar-27
SH.2450	Structural Steel - Steel Detailing Seq 8 (CL 16-18)	10	10	05-Mar-27	16-Mar-27
SH.3371	Structural Steel - Steel Detailing Seq 9 (CL 18-20)	10	10	10-Mar-27	20-Mar-27
Decking		39	39	15-Feb-27	08-Apr-27
SH.1290	Structural Steel - Steel Decking & Studs Seq 1 (CL 1-3)	16	16	15-Feb-27	04-Mar-27
SH.1350	Structural Steel - Steel Decking & Studs Seq 2 (CL 3-5)	16	16	19-Feb-27	09-Mar-27
SH.1520	Structural Steel - Steel Decking & Studs Seq 3 (CL 5-7)	16	16	24-Feb-27	13-Mar-27
SH.1420	Structural Steel - Steel Decking & Studs Seq 4 (CL 7-9)	16	16	01-Mar-27	18-Mar-27
SH.1550	Structural Steel - Steel Decking & Studs Seq 5 (CL 9-11)	16	16	05-Mar-27	23-Mar-27
SH.1570	Structural Steel - Steel Decking & Studs Seq 6 (CL 11-13)	16	16	08-Mar-27	25-Mar-27
SH.1190	Structural Steel - Steel Decking & Studs Seq 7 (CL 13-16)	16	16	12-Mar-27	30-Mar-27
SH.2340	Structural Steel - Steel Decking & Studs Seq 8 (CL 16-18)	16	16	17-Mar-27	03-Apr-27
SH.3381	Structural Steel - Steel Decking & Studs Seq 9 (CL 18-20)	16	16	22-Mar-27	08-Apr-27
SH.3131	Structural Steel - Decking Sign-Off (Intermediate EOR)	1	1	25-Mar-27	25-Mar-27
SH.3141	Structural Steel - Decking Sign-Off (Full)	1	1	08-Apr-27	08-Apr-27
Penthouse		27	27	05-Mar-27	12-Apr-27
SH.2680	Structure / Penthouse - Deck & Detail	3	3	05-Mar-27	09-Mar-27
SH.1740	Structure / Penthouse - Penthouse Roofing	5	5	10-Mar-27	16-Mar-27
SH.1650	Structure / Penthouse - Metal Studs & Sheathing at Penthouse	7	7	26-Mar-27	05-Apr-27
SH.1700	Structure / Penthouse - Penthouse Siding	5	5	06-Apr-27	12-Apr-27
Stair Towers		54	54	06-Apr-27	21-Jun-27
SH.1680	Structure / Stair Tower - Steel Stair #2	7	7	06-Apr-27	14-Apr-27
SH.1830	Structure / Stair Tower - Steel Stair #1	5	5	15-Apr-27	21-Apr-27
SH.1990	Structure / Stair Tower - Steel Stair #4	5	5	15-Apr-27	21-Apr-27
SH.2240	Structure / Stair Tower - Frame & Hang Drywall in Stair Tower #2	4	4	15-Apr-27	20-Apr-27
SH.1930	Structure / Stair Tower - Steel Stair #3	5	5	22-Apr-27	28-Apr-27

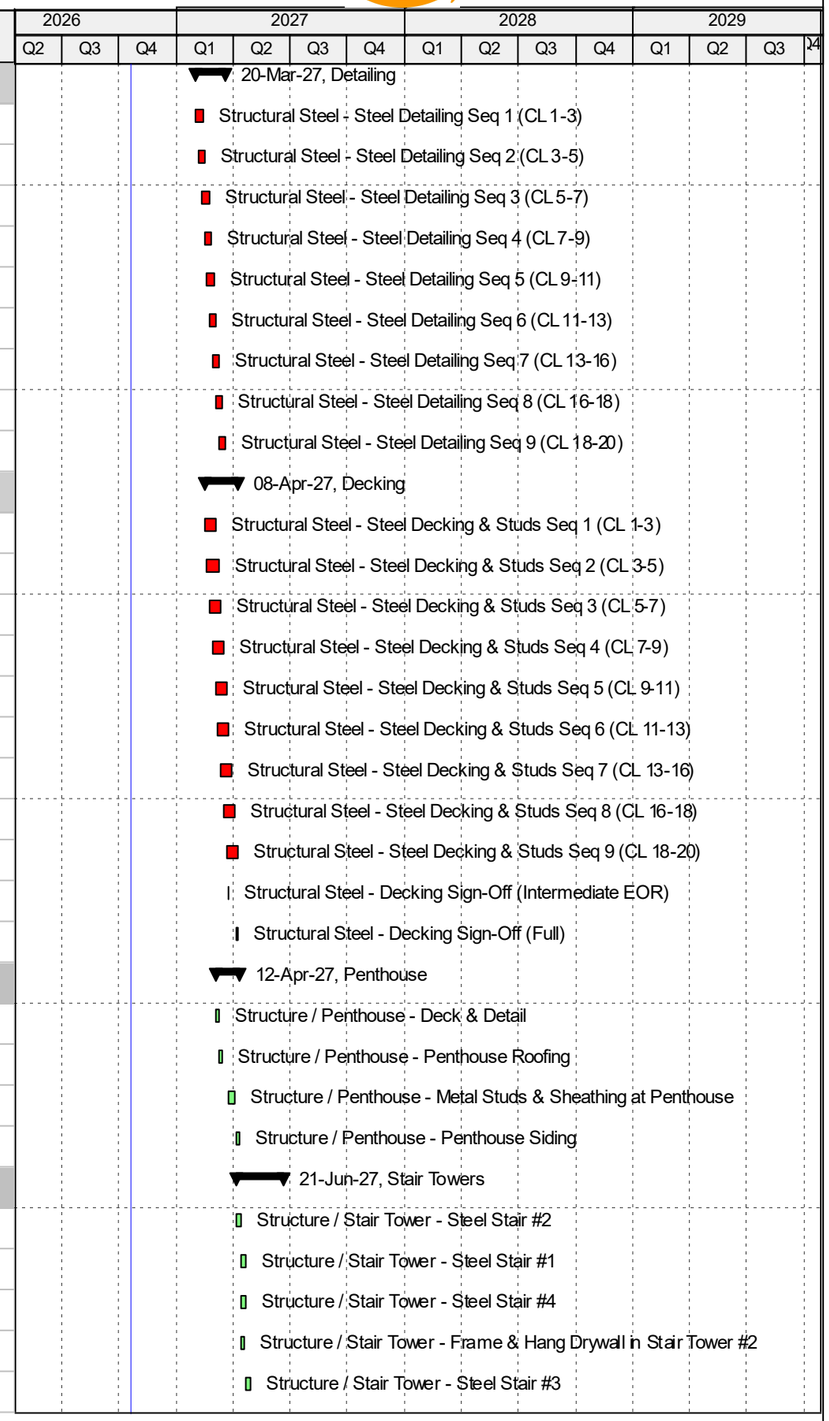


Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

Run Date: 15-Oct-26 14:16
Data Date: 19-Oct-26


Activity ID	Activity Name	OD	RD	Start	Finish
SH.2220	Structure / Stair Tower - Frame & Hang Drywall in Stair Tower #1	4	4	22-Apr-27	27-Apr-27
SH.2250	Structure / Stair Tower - Frame & Hang Drywall in Stair Tower #3	4	4	29-Apr-27	04-May-27
SH.2260	Structure / Stair Tower - Frame & Hang Drywall in Stair Tower #4	4	4	05-May-27	10-May-27
SH.2270	Structure / Stair Tower - Frame & Hang Drywall in Stair Tower #5	4	4	11-May-27	14-May-27
SH.2020	Structure / Stair Tower - Steel Stair #5	5	5	17-May-27	21-May-27
SH.2280	Structure / Stair Tower - Frame out & Hang Drywall in Stair Tower #6	4	4	17-May-27	20-May-27
SH.2230	Structure / Stair Tower - Frame & Hang Drywall in Stair Tower #7	4	4	21-May-27	26-May-27
SH.2060	Structure / Stair Tower - Steel Stair #6	5	5	24-May-27	28-May-27
SH.2801	Structure / Stair Tower - Frame & Hang Drywall in Stair Tower #8	4	4	27-May-27	02-Jun-27
SH.2811	Structure / Stair Tower - Frame & Hang Drywall in Stair Tower #9	4	4	27-May-27	02-Jun-27
SH.2140	Structure / Stair Tower - Steel Stair #7	5	5	01-Jun-27	07-Jun-27
SH.2150	Structure / Stair Tower - Steel Stair #8	5	5	08-Jun-27	14-Jun-27
SH.2821	Structure / Stair Tower - Steel Stair #9	5	5	15-Jun-27	21-Jun-27
Roof		69	69	15-Mar-27	18-Jun-27
SH.1300	Structure / Roof - Set Curbs & Cut Roof Opening For RTU / Admin	3	3	15-Mar-27	17-Mar-27
SH.1730	Structure / Roof - Roofing Field	20	20	18-Mar-27	14-Apr-27
SH.2741	Structure / Roof - Detailing	15	15	14-May-27	04-Jun-27
SH.2000	Structure / Roof - Scuppers & Downspouts	5	5	28-May-27	04-Jun-27
SH.2080	Structure / Roof - Install Roof Walkway Pads	10	10	07-Jun-27	18-Jun-27
Exterior		195	195	19-Oct-26	26-Jul-27
SH.1610	Structure / Exterior - Underslab Dock Pits	5	5	19-Oct-26	23-Oct-26
SH.1710	Structure / Exterior - Frame IMP Seq 1 (CL 4 - 9)	10	10	31-Mar-27	13-Apr-27
SH.1760	Structure / Exterior - Frame IMP Seq 2 (CL 9 - 15)	10	10	14-Apr-27	27-Apr-27
SH.1940	Structure / Exterior - Install IMP Seq 1 (CL 4 - 9)	10	10	14-Apr-27	27-Apr-27
SH.1590	Structure / Exterior - Install Precast Seq 1 (CL 3F to E)	5	5	23-Apr-27	29-Apr-27
SH.1910	Structure / Exterior - Frame IMP Seq 3 (CL 15 - 22)	10	10	28-Apr-27	11-May-27
SH.1950	Structure / Exterior - Install IMP Seq 2 (CL 9 - 15)	10	10	28-Apr-27	11-May-27
SH.1640	Structure / Exterior - Install Precast Seq 2 (CL E to 5A)	5	5	30-Apr-27	06-May-27
SH.1880	Structure / Exterior - External Caulking at Precast Seq 1	2	2	30-Apr-27	01-May-27
SH.2771	Structure / Exterior - Install Exterior Personnel Doors Office & Phase 1	10	10	30-Apr-27	13-May-27
SH.1890	Structure / Exterior - Internal Caulking at Precast Seq 1	3	3	03-May-27	05-May-27
SH.1980	Structure / Exterior - Texture / Paint Seq 1-3	15	15	03-May-27	21-May-27
SH.1690	Structure / Exterior - Install Precast Seq 3 (CL 5A to 20A)	5	5	07-May-27	13-May-27

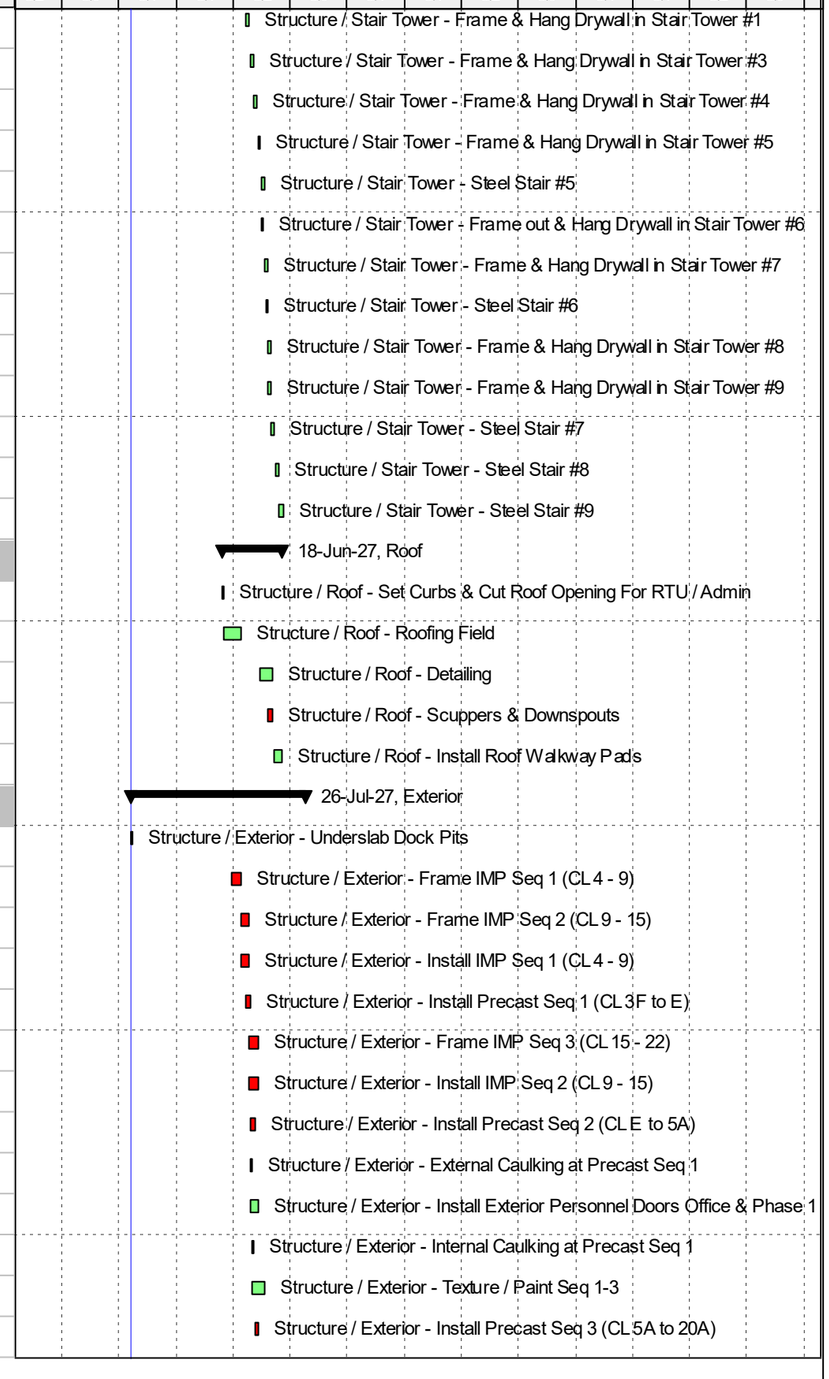


Activity ID	Activity Name	OD	RD	Start	Finish
SH.3241	Structure / Exterior - External Caulking at Precast Seq 2	2	2	07-May-27	08-May-27
SH.3201	Structure / Exterior - Internal Caulking at Precast Seq 2	3	3	10-May-27	12-May-27
SH.1960	Structure / Exterior - Install IMP Seq 3 (CL 15 - 22)	10	10	12-May-27	25-May-27
SH.2460	Structure / Exterior - Install Precast Seq 4 (CL 20A to 20F)	5	5	14-May-27	20-May-27
SH.3251	Structure / Exterior - External Caulking at Precast Seq 3	2	2	14-May-27	15-May-27
SH.3211	Structure / Exterior - Internal Caulking at Precast Seq 3	3	3	17-May-27	19-May-27
SH.1660	Structure / Exterior - Install Overhead Doors	5	5	21-May-27	27-May-27
SH.3261	Structure / Exterior - External Caulking at Precast Seq 4	2	2	21-May-27	22-May-27
SH.1891	Structure / Exterior - Internal Caulking at Precast Lines 4	3	3	24-May-27	26-May-27
SH.3351	Structure / Exterior - Texture / Paint Seq 4-6	15	15	24-May-27	10-Jun-27
SH.2070	Structure / Exterior - Parapet Wall Coping	8	8	14-Jun-27	23-Jun-27
SH.2781	Structure / Exterior - Install Exterior Storefront & Door	8	8	21-Jun-27	30-Jun-27
SH.1860	Structure / Exterior - Install Glazing	10	10	21-Jun-27	02-Jul-27
SH.2110	Structure / Exterior - Lightning Protection	10	10	28-Jun-27	12-Jul-27
SH.2480	Structure / Exterior - Install Dock Equipment	10	10	29-Jun-27	13-Jul-27
North Louvers		50	50	14-May-27	26-Jul-27
SH.2580	Structure / Exterior - Install Louver Supplemental Steel CL 1-10	10	10	14-May-27	27-May-27
SH.2600	Structure / Exterior - Louver Opening Waterproofing CL 1-10	10	10	21-May-27	04-Jun-27
SH.2530	Structure / Exterior - Install Louvers North - 2nd Floor 1-10	10	10	28-May-27	11-Jun-27
SH.3991	Structure / Exterior - Install Louver Supplemental Steel CL 11-20	10	10	28-May-27	11-Jun-27
SH.4001	Structure / Exterior - Louver Opening Waterproofing CL 11-20	10	10	07-Jun-27	18-Jun-27
SH.2520	Structure / Exterior - Install Louvers North - 1st Floor 1-10	10	10	14-Jun-27	25-Jun-27
SH.1920	Structure / Exterior - Install Louvers North - 2nd Floor 10-19	10	10	28-Jun-27	12-Jul-27
SH.2560	Structure / Exterior - Install Louvers North - 1st Floor 10-19	10	10	13-Jul-27	26-Jul-27
South Backdraft Dampers		35	35	23-Apr-27	11-Jun-27
SH.4011	Structure / Exterior - Install Backdraft Damper Supplemental Steel CL 1-10	10	10	23-Apr-27	06-May-27
SH.4031	Structure / Exterior - Install Backdraft Damper Supplemental Steel CL 11-20	10	10	23-Apr-27	06-May-27
SH.4021	Structure / Exterior - Backdraft Damper Opening Waterproofing CL 1-10	10	10	30-Apr-27	13-May-27
SH.4041	Structure / Exterior - Backdraft Damper Opening Waterproofing CL 11-20	10	10	30-Apr-27	13-May-27
SH.2550	Structure / Exterior - Install Backdraft Dampers South - 2nd Floor 1-10	5	5	14-May-27	20-May-27
SH.1800	Structure / Exterior - Install Backdraft Dampers South - 1st Floor 1-10	5	5	21-May-27	27-May-27
SH.2540	Structure / Exterior - Install Backdraft Dampers South - 2nd Floor 10-19	5	5	28-May-27	04-Jun-27
SH.2570	Structure / Exterior - Install Backdraft Dampers South - 1st Floor 10-19	5	5	07-Jun-27	11-Jun-27

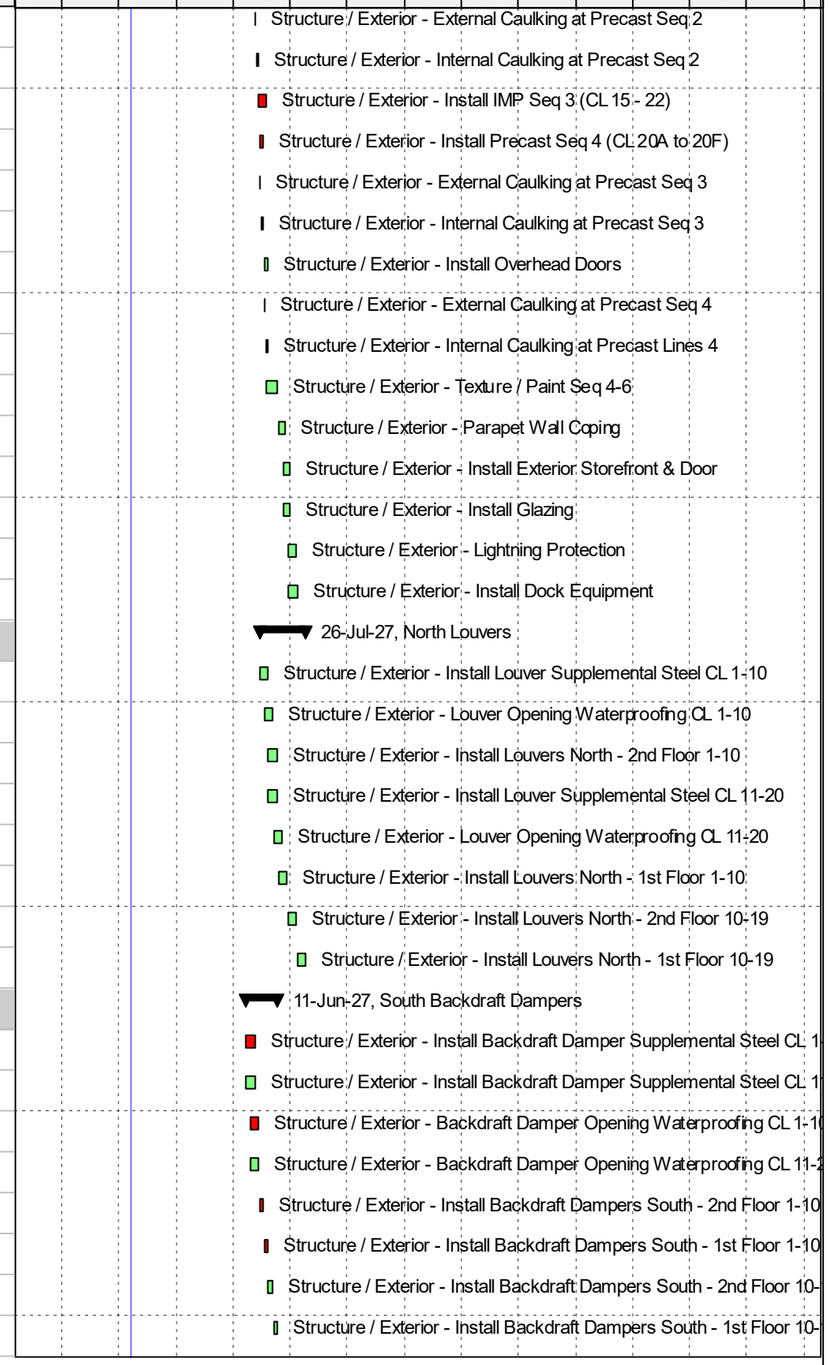


Activity ID	Activity Name	OD	RD	Start	Finish
Elevators		166	166	05-Mar-27	27-Oct-27
SH.2650	Structure / Elevators - Steel Install 2nd Floor to Roof	7	7	05-Mar-27	15-Mar-27
SH.2660	Structure / Elevators - Steel Install 2nd Floor to Penthouse	7	7	10-Mar-27	18-Mar-27
SH.1140	Structure / Elevators - Set Elevator Equipment	5	5	17-Mar-27	23-Mar-27
SH.1100	Structure / Elevators - Install Sump Pump Drain	2	2	30-Jul-27	02-Aug-27
SH.1120	Structure / Elevators - Elevator Pit Light & Receptacle Install	2	2	30-Jul-27	02-Aug-27
Freight		139	139	05-Mar-27	20-Sep-27
SH.2670	Elevators / Freight - Steel Install 1st Floor to 2nd Floor (Freight)	7	7	05-Mar-27	15-Mar-27
SH.2675	Elevators / Freight - Supplemental Elevator Steel (Freight)	5	5	16-Mar-27	22-Mar-27
SH.2690	Elevators / Freight - Frame & Hang Drywall (Freight)	8	8	15-Apr-27	26-Apr-27
SH.1900	Elevators / Freight - Mobilize, Survey Hoistway & Hand Rigging	3	3	10-May-27	12-May-27
SH.3711	Elevators / Freight - Install Machine Room Equipment	3	3	13-May-27	18-May-27
SH.3721	Elevators / Freight - Install Starter Rails	3	3	19-May-27	24-May-27
SH.1970	Elevators / Freight - Build Work Deck	2	2	25-May-27	26-May-27
SH.2040	Elevators / Freight - Install Remaining Brackets & Rails	6	6	27-May-27	08-Jun-27
SH.2050	Elevators / Freight - Install Jacks	3	3	09-Jun-27	14-Jun-27
SH.2090	Elevators / Freight - Remove Workdeck	2	2	15-Jun-27	16-Jun-27
SH.3731	Elevators / Freight - Install Oil Line	5	5	17-Jun-27	24-Jun-27
SH.2120	Elevators / Freight - Build Car Sling	3	3	28-Jun-27	30-Jun-27
SH.2130	Elevators / Freight - Install Platform	5	5	01-Jul-27	12-Jul-27
SH.2160	Elevators / Freight - Build Cab	3	3	13-Jul-27	15-Jul-27
SH.2720	Elevators / Freight - Intumescent Paint	4	4	19-Jul-27	22-Jul-27
SH.3061	Elevators / Freight - Install Fire Alarm	1	1	19-Jul-27	19-Jul-27
SH.2170	Elevators / Freight - Install Entrances	8	8	19-Jul-27	29-Jul-27
SH.2700	Elevators / Freight - Install Fire Suppression	1	1	20-Jul-27	20-Jul-27
SH.2290	Elevators / Freight - Install Doors	4	4	02-Aug-27	05-Aug-27
SH.2190	Elevators / Freight - Install Raceway & Hoistway Wiring	2	2	09-Aug-27	10-Aug-27
SH.2200	Elevators / Freight - Build Cab Fronts & Install Door Operators	3	3	11-Aug-27	16-Aug-27
SH.2300	Elevators / Freight - Install Top of Car & COPs	3	3	17-Aug-27	19-Aug-27
SH.2330	Elevators / Freight - Pull / Wire	2	2	23-Aug-27	24-Aug-27
SH.2320	Elevators / Freight - Wire Controller & Car	2	2	25-Aug-27	26-Aug-27
SH.2210	Elevators / Freight - Elevator Adjustments & Startup	12	12	30-Aug-27	20-Sep-27
Passenger		166	166	05-Mar-27	27-Oct-27

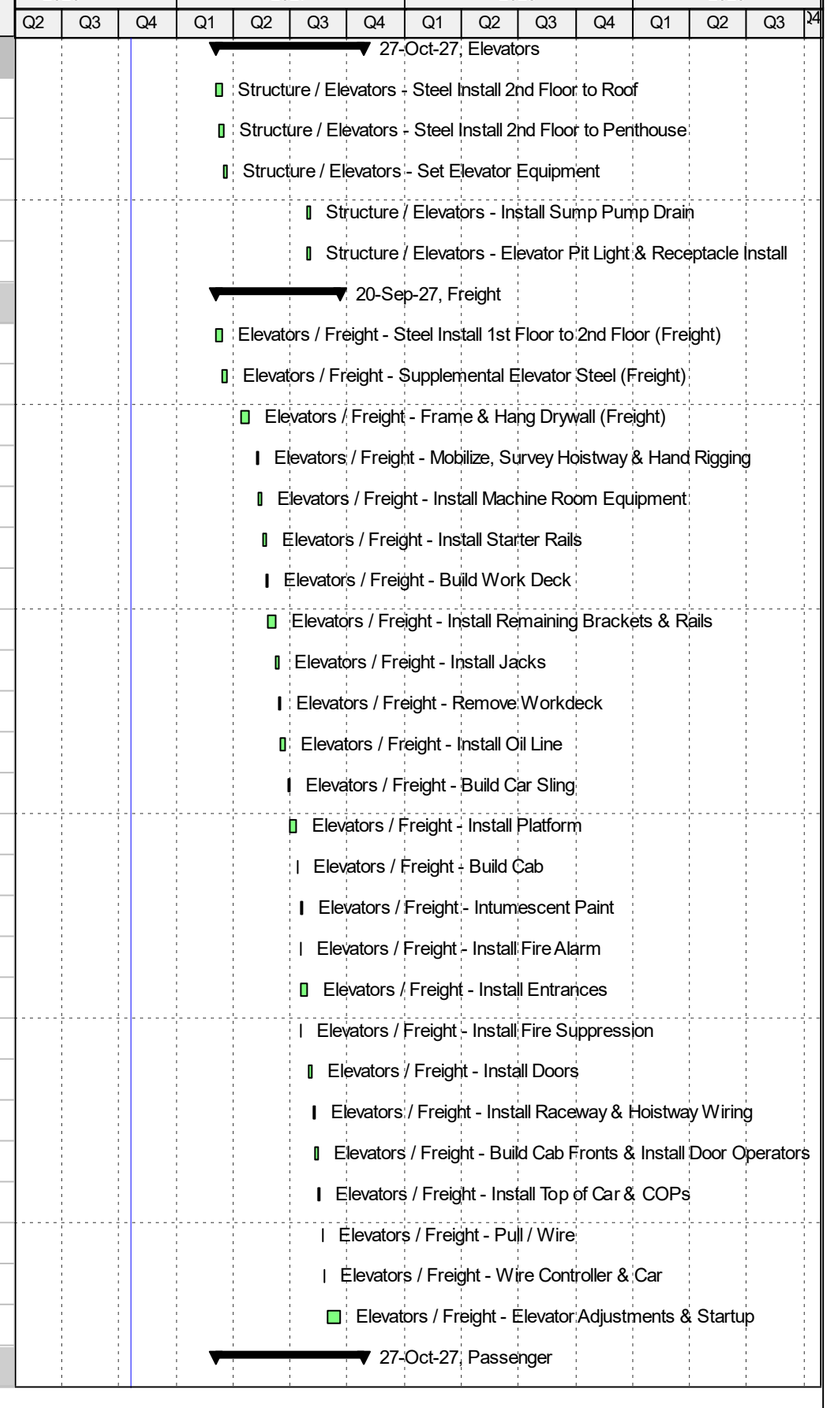


Activity ID	Activity Name	OD	RD	Start	Finish
SH.2640	Elevators / Passenger - Steel Install 1st Floor to 2nd Floor (Passenger)	7	7	05-Mar-27	15-Mar-27
SH.2645	Elevators / Passenger - Supplemental Elevator Steel (Passenger)	7	7	19-Mar-27	29-Mar-27
SH.1810	Elevators / Passenger - Frame & Hang Drywall (Passenger)	10	10	15-Apr-27	28-Apr-27
SH.2470	Elevators / Passenger - Mobilize, Survey, & Hang Rigging	3	3	28-Jun-27	30-Jun-27
SH.3741	Elevators / Passenger - Install Machine Room Equipment	3	3	01-Jul-27	07-Jul-27
SH.3851	Elevators / Passenger - Install Starter Rails	3	3	08-Jul-27	13-Jul-27
SH.3841	Elevators / Passenger - Install False Car	2	2	14-Jul-27	15-Jul-27
SH.3751	Elevators / Passenger - Install Remaining Brackets & Rails	6	6	19-Jul-27	27-Jul-27
SH.3761	Elevators / Passenger - Build Jack Pedestals	2	2	28-Jul-27	29-Jul-27
SH.3861	Elevators / Passenger - Install Jack, Sheaves, & Governor	5	5	02-Aug-27	09-Aug-27
SH.3771	Elevators / Passenger - Install Oil Line & Raceway	3	3	10-Aug-27	12-Aug-27
SH.3781	Elevators / Passenger - Build Car Sling	3	3	16-Aug-27	18-Aug-27
SH.3871	Elevators / Passenger - Install Platform / Cab Walls	3	3	19-Aug-27	24-Aug-27
SH.3791	Elevators / Passenger - Install Ropes	2	2	25-Aug-27	26-Aug-27
SH.3881	Elevators / Passenger - Remove False Car	1	1	30-Aug-27	30-Aug-27
SH.2761	Elevators / Passenger - Intumescent Paint	4	4	31-Aug-27	03-Sep-27
SH.3691	Elevators / Passenger - Install Fire Alarm	1	1	31-Aug-27	31-Aug-27
SH.3801	Elevators / Passenger - Install Entrances	9	9	31-Aug-27	15-Sep-27
SH.3701	Elevators / Passenger - Install Fire Suppression	1	1	01-Sep-27	01-Sep-27
SH.3811	Elevators / Passenger - Install Raceway & Hoistway Wiring	2	2	16-Sep-27	20-Sep-27
SH.3821	Elevators / Passenger - Build Cab Fronts, Door Operators	3	3	21-Sep-27	23-Sep-27
SH.3891	Elevators / Passenger - Install Top / COPs	3	3	27-Sep-27	29-Sep-27
SH.3831	Elevators / Passenger - Pull Wire	2	2	30-Sep-27	04-Oct-27
SH.3901	Elevators / Passenger - Wire Controller & Car	2	2	05-Oct-27	06-Oct-27
SH.2791	Elevators / Passenger - Elevator Adjustments & Startup	12	12	07-Oct-27	27-Oct-27
Gen Yard (Structure)		225	225	02-Dec-26	19-Oct-27
CN1250	Structure / Gen Yard - Install Gen Yard U/G Electrical (MV Transformer)	20	20	02-Dec-26	30-Dec-26
CN1020	Structure / Gen Yard - Install Downspout Drains	5	5	15-Jan-27	21-Jan-27
CN1800	Structure / Gen Yard - F/R/P Transformer Pads (Phases 1 & 2)	14	14	22-Jan-27	10-Feb-27
CN10230	Structure / Gen Yard - F/R/P Transformer Pads (Phases 3 & 4)	3	3	11-Feb-27	13-Feb-27
CN10240	Structure / Gen Yard - F/R/P Transformer Pads (Phases 5 & 6)	3	3	15-Feb-27	17-Feb-27
CN1080	Structure / Gen Yard - Seq 4 - Set Screen Wall Steel (CL 3 - 10)	15	15	07-May-27	27-May-27
CN1090	Structure / Gen Yard - Start Screen Wall Metal Panels (CL 3 - 10)	15	15	18-May-27	08-Jun-27

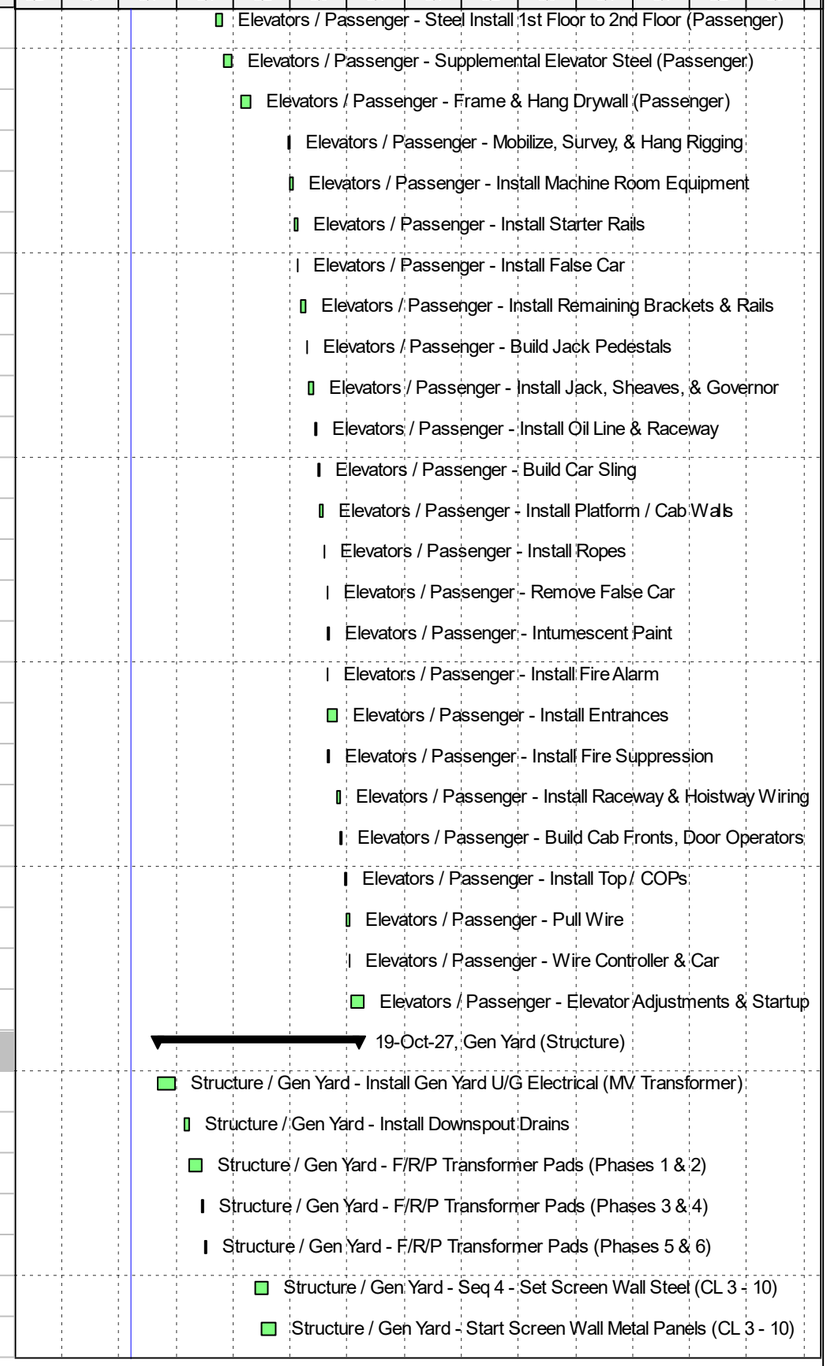

Activity ID	Activity Name	OD	RD	Start	Finish
CN1110	Structure / Gen Yard - Install OFCI Protection (Scaffolding) (CL 3 - 10)	15	15	28-May-27	18-Jun-27
CN10170	Structure / Gen Yard - Seq 4 - Set Screen Wall Steel (CL 10 - 22)	12	12	28-May-27	11-Jun-27
CN1070	Structure / Gen Yard - Install Stone Out To The Face Of T-Steel (CL 3 - 10)	5	5	07-Jun-27	11-Jun-27
CN10180	Structure / Gen Yard - Seq 5 - Start Screen Wall Metal Panels (CL 10 - 22)	15	15	09-Jun-27	25-Jun-27
CN10220	Structure / Gen Yard - Seq 7 - Install OFCI Protection (Scaffolding) (CL 10 - 22)	15	15	11-Jun-27	28-Jun-27
CN15860	Structure / Gen Yard - Seq 3C - Install Stone Out To The Face Of T-Steel (CL 10 - 22)	5	5	12-Jun-27	17-Jun-27
CN1120	Structure / Gen Yard - Seq 8 - F/R/P Gen Pads (Phases 1 & 2)	8	8	21-Jun-27	30-Jun-27
CN1210	Structure / Gen Yard - Cure Time (Phase 1 & 2)	7	7	01-Jul-27	07-Jul-27
CN10130	Structure / Gen Yard - Seq 8 - F/R/P Gen Pads (Phases 3 & 4)	4	4	01-Jul-27	06-Jul-27
CN10140	Structure / Gen Yard - Seq 8 - F/R/P Gen Pads (Phases 5 & 6)	2	2	07-Jul-27	08-Jul-27
CN10150	Structure / Gen Yard - Seq 8 - Cure Time (Phase 3 & 4)	7	7	07-Jul-27	14-Jul-27
CN1130	Structure / Gen Yard - Install Security Pole Bases / Security Conduits	5	5	09-Jul-27	15-Jul-27
CN1160	Structure / Gen Yard - Install Gen Grounding	5	5	09-Jul-27	15-Jul-27
CN10160	Structure / Gen Yard - Seq 8 - Cure Time (Phase 5 & 6)	7	7	09-Jul-27	16-Jul-27
CN1320	Structure / Gen Yard - Seq 4 - Set Trestle Steel (CL 3 - 10)	5	5	10-Jul-27	15-Jul-27
CN1140	Structure / Gen Yard - Install Pipe Bollards	5	5	13-Jul-27	19-Jul-27
CN1150	Structure / Gen Yard - Install Security Fence Poles	5	5	13-Jul-27	19-Jul-27
CN1170	Structure / Gen Yard - Install Stone In Between Gen Pads	5	5	16-Jul-27	22-Jul-27
CN1180	Structure / Gen Yard - Verify Generators Setting	1	1	10-Aug-27	10-Aug-27
CN1190	Structure / Gen Yard - Form / Pour Remaining Sidewalk Near Curb	5	5	11-Aug-27	17-Aug-27
CN1200	Structure / Gen Yard - Set Remaining Gen Steel / Platforms	5	5	13-Aug-27	19-Aug-27
CN1220	Structure / Gen Yard - Install Remaining Stone	5	5	18-Aug-27	24-Aug-27
CN1230	Structure / Gen Yard - Install Fence Fabric / Gates / Hardware	5	5	25-Aug-27	31-Aug-27
CN3100	Structure / Gen Yard - Seq 4 - Set Trestle Steel (CL 10-22)	5	5	14-Oct-27	19-Oct-27
Interior Buildout		118	118	23-Mar-27	07-Sep-27
SH.1820	Structure / Interior - Install IW Mains & Insulation Phase 1	15	15	23-Mar-27	12-Apr-27
SH.1630	Structure / Interior - Construction Power	15	15	09-Apr-27	29-Apr-27
SH.2951	Structure / Interior - Install IW Mains & Insulation Phase 2	15	15	13-Apr-27	03-May-27
SH.1870	Structure / Interior - IW Mains Testing Phase 1	1	1	13-Apr-27	13-Apr-27
SH.2961	Structure / Interior - Install IW Mains & Insulation Phase 3	15	15	04-May-27	24-May-27
SH.3001	Structure / Interior - IW Mains Testing Phase 2	1	1	04-May-27	04-May-27
SH.2971	Structure / Interior - Install IW Mains & Insulation Phase 4	15	15	25-May-27	15-Jun-27
SH.3011	Structure / Interior - IW Mains Testing Phase 3	1	1	25-May-27	25-May-27

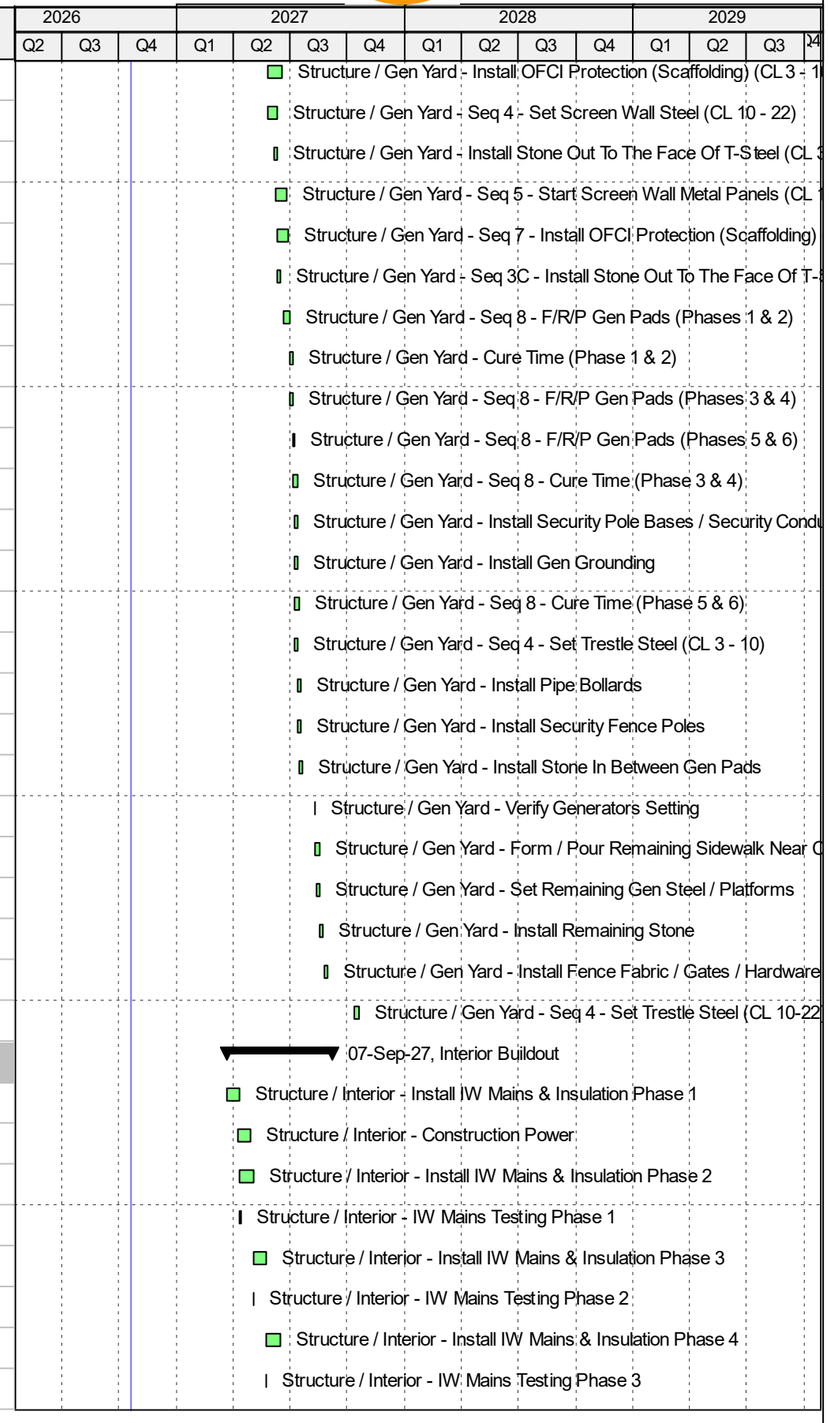

Activity ID	Activity Name	OD	RD	Start	Finish
SH.1850	Structure / Interior - Install Fire Alarm	15	15	14-Jun-27	02-Jul-27
SH.2981	Structure / Interior - Install IW Mains & Insulation Phase 5	10	10	16-Jun-27	29-Jun-27
SH.3021	Structure / Interior - IW Mains Testing Phase 4	1	1	16-Jun-27	16-Jun-27
SH.2991	Structure / Interior - Install IW Mains & Insulation Phase 6	10	10	30-Jun-27	14-Jul-27
SH.3031	Structure / Interior - IW Mains Testing Phase 5	1	1	30-Jun-27	30-Jun-27
SH.3041	Structure / Interior - IW Mains Testing Phase 6	1	1	15-Jul-27	15-Jul-27
SH.2010	Structure / Interior - Fire Riser Room	15	15	04-Aug-27	24-Aug-27
SH.2100	Structure / Interior - L1 Fire Sprinkler Testing	2	2	01-Sep-27	02-Sep-27
SH.2180	Structure / Interior - L2 Fire Sprinkler Testing	2	2	03-Sep-27	07-Sep-27
Main Building - Building D		313	313	08-Feb-27	28-Apr-28
Admin		124	124	06-Apr-27	29-Sep-27
CN6490	Admin - Install Elevator Pit Sump Pumps	1	1	03-Aug-27	03-Aug-27
OFF.1130	Admin - Set OFCI Panels	5	5	04-Aug-27	10-Aug-27
OFF.1200	Admin - Toilet Room Accessories	5	5	04-Aug-27	10-Aug-27
OFF.1990	Admin - Set Electrical LV Panelboards	5	5	11-Aug-27	17-Aug-27
OFF.1140	Admin - House Electrical Room LV Terminations	5	5	18-Aug-27	24-Aug-27
OFF.1270	Admin - Final Paint	5	5	07-Sep-27	13-Sep-27
OFF.1260	Admin - Devices & Trim	5	5	07-Sep-27	13-Sep-27
Admin - Level 1		124	124	06-Apr-27	29-Sep-27
OFF.1950	Admin / Lvl 1 - Layout	2	2	06-Apr-27	07-Apr-27
CN6350	Admin / Lvl 1 - Framing & Door Frames (Blue)	7	7	08-Apr-27	16-Apr-27
CN6470	Admin / Lvl 1 - Install Masonry Walls Conference OARB	10	10	08-Apr-27	21-Apr-27
CN1900	Admin / Lvl 1 - Install Drywall Seq 1 - Blue (Top 12')	10	10	14-Apr-27	24-Apr-27
CN6360	Admin / Lvl 1 - Framing & Door Frames (Red)	7	7	14-Apr-27	22-Apr-27
CN6370	Admin / Lvl 1 - Framing & Door Frames (Green)	7	7	20-Apr-27	28-Apr-27
CN6640	Admin / Lvl 1 - Install Beams & Decking For Masonry Walls	2	2	22-Apr-27	23-Apr-27
CN6380	Admin / Lvl 1 - Framing & Door Frames (Magenta)	7	7	26-Apr-27	04-May-27
CN6390	Admin / Lvl 1 - Prime & Paint Drywall (Blue)	5	5	26-Apr-27	30-Apr-27
CN6630	Admin / Lvl 1 - Prep & Pour Concrete Cap For Masonry Walls	2	2	26-Apr-27	27-Apr-27
CN1910	Admin / Lvl 1 - Install Drywall Seq 2 - Red (Top 12')	21	21	28-Apr-27	21-May-27
CN6430	Admin / Lvl 1 - In Wall Plumbing (Office)	15	15	29-Apr-27	19-May-27
CN1920	Admin / Lvl 1 - Install Drywall Seq 3 - Green (Top 12')	15	15	10-May-27	26-May-27
CN6560	Admin / Lvl 1 - Install Fire Proofing	10	10	17-May-27	28-May-27

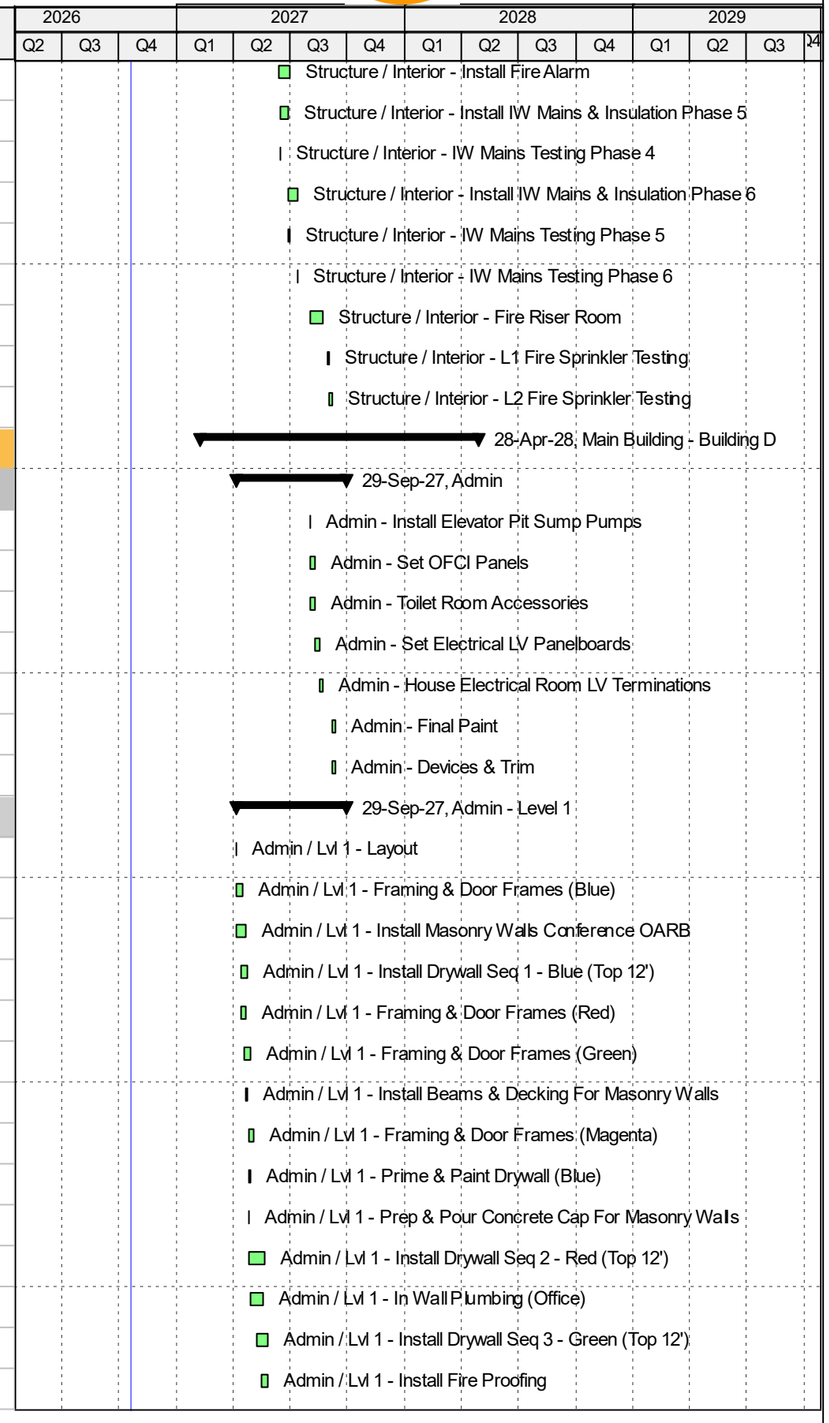

Gray


CMH139
Preliminary Schedule

aws

Activity ID	Activity Name	OD	RD	Start	Finish
CN1930	Admin / Lvl 1 - Install Drywall Seq 4 - Magenta (Top 12')	10	10	18-May-27	28-May-27
CN1940	Admin / Lvl 1 - In Wall Electrical Rough In (Blue)	5	5	20-May-27	26-May-27
CN6400	Admin / Lvl 1 - Install Fire Protection	10	10	24-May-27	07-Jun-27
CN6520	Admin / Lvl 1 - Prime & Paint Drywall (Red)	5	5	24-May-27	28-May-27
CN1950	Admin / Lvl 1 - In Wall Electrical Rough In (Red)	5	5	24-May-27	28-May-27
CN1960	Admin / Lvl 1 - In Wall Electrical Rough In (Green)	5	5	26-May-27	02-Jun-27
OFF.1010	Admin / Lvl 1 - Fiber Closets Electrical & Fire Alarm Rough-In	3	3	27-May-27	01-Jun-27
CN6530	Admin / Lvl 1 - Prime & Paint Drywall (Green)	5	5	27-May-27	03-Jun-27
CN6660	Admin / Lvl 1 - In Wall Electrical Inspection (Blue)	5	5	27-May-27	03-Jun-27
OFF.1980	Admin / Lvl 1 - IW Supply	10	10	01-Jun-27	14-Jun-27
CN6540	Admin / Lvl 1 - Prime & Paint Drywall (Magenta)	5	5	01-Jun-27	07-Jun-27
CN6710	Admin / Lvl 1 - In Wall Electrical Inspection (Red)	5	5	01-Jun-27	07-Jun-27
CN6670	Admin / Lvl 1 - In Wall Electrical Inspection (Green)	5	5	03-Jun-27	09-Jun-27
CN6310	Admin / Lvl 1 - Install Drywall Seq 1 - Blue (Remaining)	10	10	04-Jun-27	15-Jun-27
CN6410	Admin / Lvl 1 - Install OH Electrical Rough In	15	15	04-Jun-27	24-Jun-27
CN6420	Admin / Lvl 1 - Install Duct Work	20	20	04-Jun-27	01-Jul-27
CN6450	Admin / Lvl 1 - Install Plumbing (Mechanical Room)	15	15	04-Jun-27	24-Jun-27
CN6460	Admin / Lvl 1 - Install Split System & Refrigeration	20	20	08-Jun-27	06-Jul-27
CN15910	Admin / Lvl 1 - Install EUHs	10	10	08-Jun-27	21-Jun-27
CN15920	Admin / Lvl 1 - Install ERVs	3	3	08-Jun-27	10-Jun-27
CN6500	Admin / Lvl 1 - OH Plumbing (Office)	15	15	11-Jun-27	01-Jul-27
CN1970	Admin / Lvl 1 - In Wall Electrical Rough In (Magenta)	5	5	11-Jun-27	17-Jun-27
CN6320	Admin / Lvl 1 - Install Drywall Seq 2 - Red (Remaining)	15	15	16-Jun-27	02-Jul-27
CN6440	Admin / Lvl 1 - Install VAVs	20	20	18-Jun-27	16-Jul-27
CN6650	Admin / Lvl 1 - In Wall Electrical Inspection (Magenta)	5	5	18-Jun-27	24-Jun-27
CN6330	Admin / Lvl 1 - Install Drywall Seq 3 - Green (Remaining)	15	15	24-Jun-27	12-Jul-27
CN6340	Admin / Lvl 1 - Install Drywall Seq 4 - Magenta (Remaining)	10	10	01-Jul-27	13-Jul-27
OFF.1280	Admin / Lvl 1 - Office Doors & Hardware	5	5	13-Jul-27	19-Jul-27
OFF.1050	Admin / Lvl 1 - A/G Plumbing Rough In	15	15	14-Jul-27	03-Aug-27
CN6570	Admin / Lvl 1 - Mechanical Inspection	1	1	19-Jul-27	19-Jul-27
OFF.1180	Admin / Lvl 1 - Overhead Electrical Rough In	5	5	28-Jul-27	03-Aug-27
OFF.1330	Admin / Lvl 1 - Casework	3	3	04-Aug-27	06-Aug-27
OFF.1060	Admin / Lvl 1 - Fiber Closets Fire Protection Connections	1	1	04-Aug-27	04-Aug-27




Activity ID	Activity Name	OD	RD	Start	Finish
OFF.2030	Admin / Lvl 1 - 1st Floor Seismic Install	5	5	04-Aug-27	10-Aug-27
OFF.1110	Admin / Lvl 1 - Fiber Closets Basket Tray	4	4	05-Aug-27	10-Aug-27
OFF.1240	Admin / Lvl 1 - Ceiling Grid	8	8	11-Aug-27	20-Aug-27
OFF.1080	Admin / Lvl 1 - Fiber Closets Light Fixtures / Devices / Trim	2	2	11-Aug-27	12-Aug-27
CN6590	Admin / Lvl 1 - Hard Lids	10	10	11-Aug-27	24-Aug-27
OFF.1340	Admin / Lvl 1 - Ceiling Tile	3	3	23-Aug-27	25-Aug-27
OFF.1320	Admin / Lvl 1 - Grilles / Registers / Diffusers	5	5	23-Aug-27	27-Aug-27
OFF.1350	Admin / Lvl 1 - Tile Flooring & Walls	10	10	23-Aug-27	03-Sep-27
CN6510	Admin / Lvl 1 - DFH Finish Carpentry	10	10	23-Aug-27	03-Sep-27
OFF.1120	Admin / Lvl 1 - Fiber Room Finalization	25	25	23-Aug-27	27-Sep-27
OFF.1250	Admin / Lvl 1 - Overhead Inspections	1	1	30-Aug-27	30-Aug-27
OFF.1290	Admin / Lvl 1 - Fire Protection Heads	2	2	31-Aug-27	01-Sep-27
OFF.1310	Admin / Lvl 1 - Light Fixtures	5	5	31-Aug-27	07-Sep-27
CN6580	Admin / Lvl 1 - Fire Alarm Devices	2	2	31-Aug-27	01-Sep-27
CN1990	Admin / Lvl 1 - Install Turn Stiles	5	5	31-Aug-27	07-Sep-27
OFF.1300	Admin / Lvl 1 - Carpet Flooring & Resilient Base	3	3	08-Sep-27	10-Sep-27
CN6600	Admin / Lvl 1 - Toilet Partitions	5	5	08-Sep-27	14-Sep-27
CN6480	Admin / Lvl 1 - Install Plumbing Fixtures	10	10	15-Sep-27	28-Sep-27
CN6550	Admin / Lvl 1 - Final Plumbing Inspection	1	1	29-Sep-27	29-Sep-27
Admin - Level 2		122	122	08-Apr-27	29-Sep-27
OFF.2040	Admin / Lvl 2 - Layout	2	2	08-Apr-27	09-Apr-27
CN7010	Admin / Lvl 2 - Framing & Door Frames (Blue)	7	7	12-Apr-27	20-Apr-27
CN6680	Admin / Lvl 2 - Install Drywall Seq 1 - Blue (Top 12')	10	10	16-Apr-27	27-Apr-27
CN6690	Admin / Lvl 2 - Framing & Door Frames (Red)	7	7	16-Apr-27	26-Apr-27
CN6700	Admin / Lvl 2 - Framing & Door Frames (Green)	7	7	22-Apr-27	30-Apr-27
CN6760	Admin / Lvl 2 - Install Drywall Seq 2 - Red (Top 12')	18	18	27-Apr-27	17-May-27
CN6750	Admin / Lvl 2 - Framing & Door Frames (Magenta)	7	7	28-Apr-27	06-May-27
CN6730	Admin / Lvl 2 - Prime & Paint Drywall (Blue)	5	5	28-Apr-27	04-May-27
CN6840	Admin / Lvl 2 - In Wall Plumbing (Office)	15	15	03-May-27	21-May-27
CN6780	Admin / Lvl 2 - Install Drywall Seq 3 - Green (Top 12')	12	12	07-May-27	20-May-27
CN6820	Admin / Lvl 2 - Install Fire Proofing	10	10	12-May-27	25-May-27
CN6800	Admin / Lvl 2 - Install Drywall Seq 4 - Magenta (Top 12')	10	10	14-May-27	25-May-27
CN6830	Admin / Lvl 2 - Install Fire Protection	10	10	18-May-27	01-Jun-27

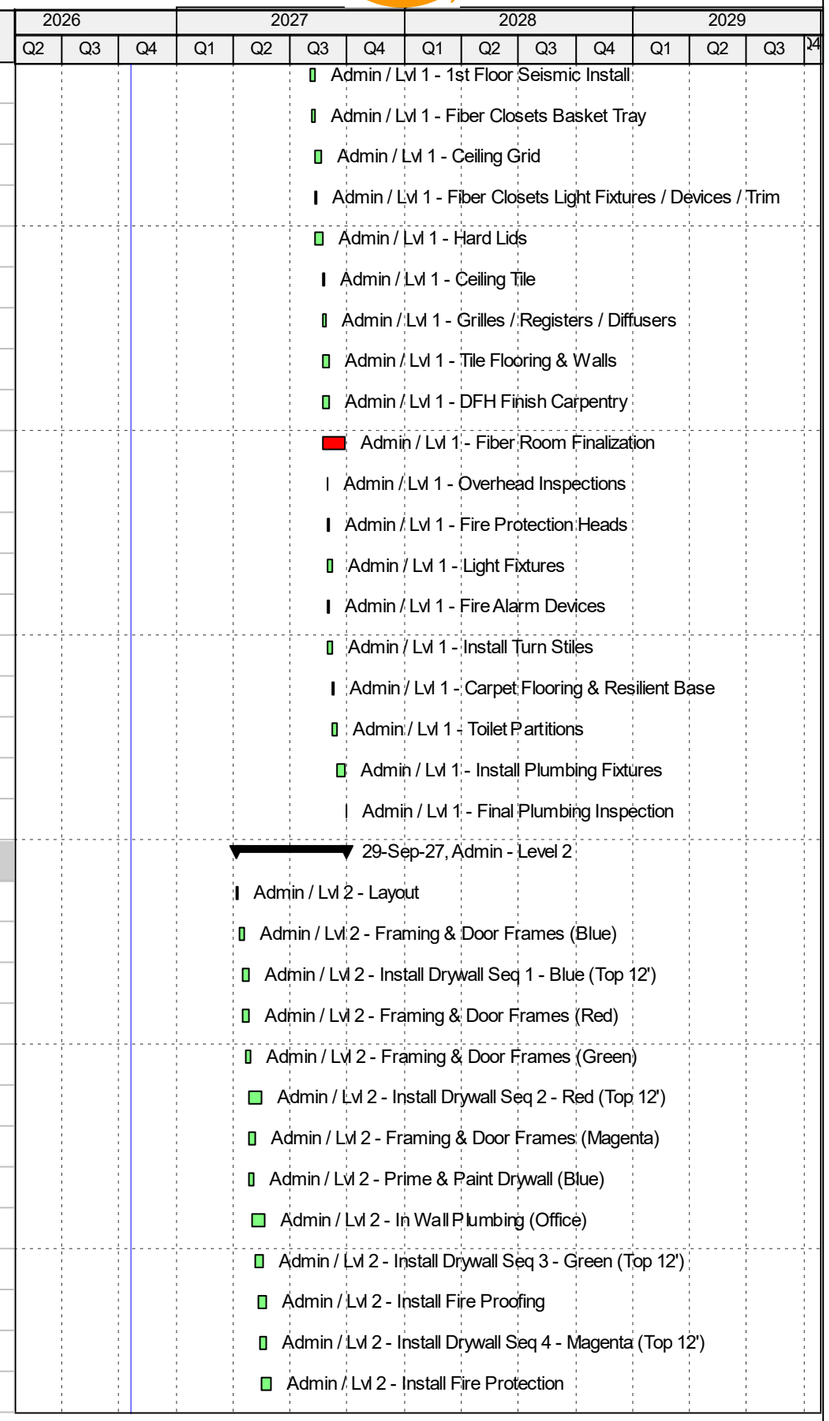

Activity ID	Activity Name	OD	RD	Start	Finish
CN6770	Admin / Lvl 2 - Prime & Paint Drywall (Red)	5	5	18-May-27	24-May-27
CN7030	Admin / Lvl 2 - In Wall Electrical Rough In (Blue)	5	5	20-May-27	26-May-27
OFF.2050	Admin / Lvl 2 - Fiber Closets Electrical & Fire Alarm Rough-In	3	3	21-May-27	25-May-27
CN6790	Admin / Lvl 2 - Prime & Paint Drywall (Green)	5	5	21-May-27	27-May-27
CN15880	Admin / Lvl 2 - In Wall Electrical Rough In (Red)	5	5	24-May-27	28-May-27
OFF.1970	Admin / Lvl 2 - IW Supply	10	10	26-May-27	09-Jun-27
CN6810	Admin / Lvl 2 - Prime & Paint Drywall (Magenta)	5	5	26-May-27	02-Jun-27
CN15890	Admin / Lvl 2 - In Wall Electrical Rough In (Green)	5	5	26-May-27	02-Jun-27
CN7040	Admin / Lvl 2 - In Wall Electrical Inspection (Blue)	5	5	27-May-27	03-Jun-27
CN6850	Admin / Lvl 2 - Install Plumbing (Mechanical Room)	15	15	28-May-27	18-Jun-27
CN15900	Admin / Lvl 2 - In Wall Electrical Rough In (Magenta)	5	5	28-May-27	04-Jun-27
CN7050	Admin / Lvl 2 - In Wall Electrical Inspection (Red)	5	5	01-Jun-27	07-Jun-27
CN6870	Admin / Lvl 2 - Install Split System & Refrigeration	20	20	03-Jun-27	30-Jun-27
CN15930	Admin / Lvl 2 - Install EUHs	10	10	03-Jun-27	16-Jun-27
CN15940	Admin / Lvl 2 - Install ERVs	3	3	03-Jun-27	07-Jun-27
CN7060	Admin / Lvl 2 - In Wall Electrical Inspection (Green)	5	5	03-Jun-27	09-Jun-27
CN6740	Admin / Lvl 2 - Install Drywall Seq 1 - Blue (Remaining)	10	10	04-Jun-27	15-Jun-27
CN6880	Admin / Lvl 2 - In Wall Electrical Inspection (Magenta)	5	5	07-Jun-27	11-Jun-27
CN6900	Admin / Lvl 2 - Install Duct Work	20	20	10-Jun-27	08-Jul-27
CN6930	Admin / Lvl 2 - Install Drywall Seq 2 - Red (Remaining)	18	18	16-Jun-27	07-Jul-27
CN6860	Admin / Lvl 2 - OH Plumbing (Office)	15	15	17-Jun-27	08-Jul-27
CN7020	Admin / Lvl 2 - Install OH Electrical Rough In	15	15	17-Jun-27	08-Jul-27
CN6940	Admin / Lvl 2 - Install Drywall Seq 3 - Green (Remaining)	15	15	24-Jun-27	12-Jul-27
CN6910	Admin / Lvl 2 - Install VAVs	20	20	24-Jun-27	22-Jul-27
CN6950	Admin / Lvl 2 - Install Drywall Seq 4 - Magenta (Remaining)	10	10	01-Jul-27	13-Jul-27
OFF.2060	Admin / Lvl 2 - Office Doors & Hardware	5	5	13-Jul-27	19-Jul-27
OFF.1900	Admin / Lvl 2 - A/G Plumbing Rough In	15	15	14-Jul-27	03-Aug-27
CN6920	Admin / Lvl 2 - Mechanical Inspection	1	1	23-Jul-27	23-Jul-27
OFF.2140	Admin / Lvl 2 - Overhead Electrical Rough In	5	5	28-Jul-27	03-Aug-27
OFF.1910	Admin / Lvl 2 - Casework	3	3	04-Aug-27	06-Aug-27
OFF.2000	Admin / Lvl 2 - 2nd Floor Seismic Install	5	5	04-Aug-27	10-Aug-27
OFF.2090	Admin / Lvl 2 - Fiber Closets Fire Protection Connections	1	1	04-Aug-27	04-Aug-27
OFF.2130	Admin / Lvl 2 - Fiber Closets Basket Tray	4	4	05-Aug-27	10-Aug-27




Activity ID	Activity Name	OD	RD	Start	Finish
OFF.2120	Admin / Lvl 2 - Fiber Closets Light Fixtures / Devices / Trim	2	2	05-Aug-27	06-Aug-27
OFF.1840	Admin / Lvl 2 - Ceiling Grid	8	8	11-Aug-27	20-Aug-27
CN6960	Admin / Lvl 2 - Hard Lids	10	10	11-Aug-27	24-Aug-27
OFF.1920	Admin / Lvl 2 - Tile Flooring & Walls	10	10	23-Aug-27	03-Sep-27
OFF.1880	Admin / Lvl 2 - Ceiling Tile	3	3	23-Aug-27	25-Aug-27
OFF.1860	Admin / Lvl 2 - Grilles / Registers / Diffusers	5	5	23-Aug-27	27-Aug-27
CN6980	Admin / Lvl 2 - DFH Finish Carpentry	10	10	23-Aug-27	03-Sep-27
OFF.1830	Admin / Lvl 2 - Overhead Inspections	1	1	30-Aug-27	30-Aug-27
OFF.1870	Admin / Lvl 2 - Fire Protection Heads	2	2	31-Aug-27	01-Sep-27
OFF.1850	Admin / Lvl 2 - Light Fixtures	5	5	31-Aug-27	07-Sep-27
CN6970	Admin / Lvl 2 - Fire Alarm Devices	4	4	31-Aug-27	03-Sep-27
OFF.1940	Admin / Lvl 2 - Carpet Flooring & Resilient Base	3	3	02-Sep-27	07-Sep-27
CN6990	Admin / Lvl 2 - Toilet Partitions	5	5	08-Sep-27	14-Sep-27
CN7000	Admin / Lvl 2 - Install Plumbing Fixtures	10	10	15-Sep-27	28-Sep-27
CN6890	Admin / Lvl 2 - Final Plumbing Inspection	1	1	29-Sep-27	29-Sep-27
Phase 1 (ROMP01 & 03)		205	205	08-Feb-27	24-Nov-27
Phase 1 - Gen Yard		96	96	13-Apr-27	26-Aug-27
P1EX.1230	Phase 1 / Gen Yard - Pour Sidewalk	5	5	14-Jun-27	18-Jun-27
P1EX.1240	Phase 1 / Gen Yard - Install Foundations & Fencing	4	4	13-Aug-27	18-Aug-27
Electrical		96	96	13-Apr-27	26-Aug-27
P1EX.1030	Phase 1 / Gen Yard - Set Transformers	2	2	13-Apr-27	14-Apr-27
P1EX.1280	Phase 1 / Gen Yard - Install Fuel System Control Conduit	10	10	04-Jun-27	17-Jun-27
P1EX.1050	Phase 1 / Gen Yard - Pull, Term & Test MV through XFMRs	7	7	22-Jun-27	30-Jun-27
P1EX.1110	Phase 1 / Gen Yard - Pull In DLB Loop (FLORES)	5	5	01-Jul-27	08-Jul-27
P1EX.1190	Phase 1 / Gen Yard - Pull, Test & Term Mech Gen Feeder Wire	2	2	13-Jul-27	14-Jul-27
P1EX.1200	Phase 1 / Gen Yard - Pull & Term Mech Gen Controls	4	4	15-Jul-27	20-Jul-27
P1EX.1040	Phase 1 / Gen Yard - Install Cable Bus Structure	5	5	16-Jul-27	22-Jul-27
P1EX.1210	Phase 1 / Gen Yard - Install Power & Conduit Inside Mech Gen	2	2	21-Jul-27	22-Jul-27
P1EX.1070	Phase 1 / Gen Yard - LV Cable Bus and Feeders - XFMRs to USBs	10	10	23-Jul-27	05-Aug-27
P1EX.1290	Phase 1 / Gen Yard - Grounding / Lightning Protection	2	2	28-Jul-27	29-Jul-27
P1EX.1250	Phase 1 / Gen Yard - Energize Electrical - Site to Phase	0	0		05-Aug-27
P1EX.1300	Phase 1 / Gen Yard - LV Cable Bus and Feeders - Gens to USBs	15	15	06-Aug-27	26-Aug-27
Mechanical		60	60	19-May-27	12-Aug-27

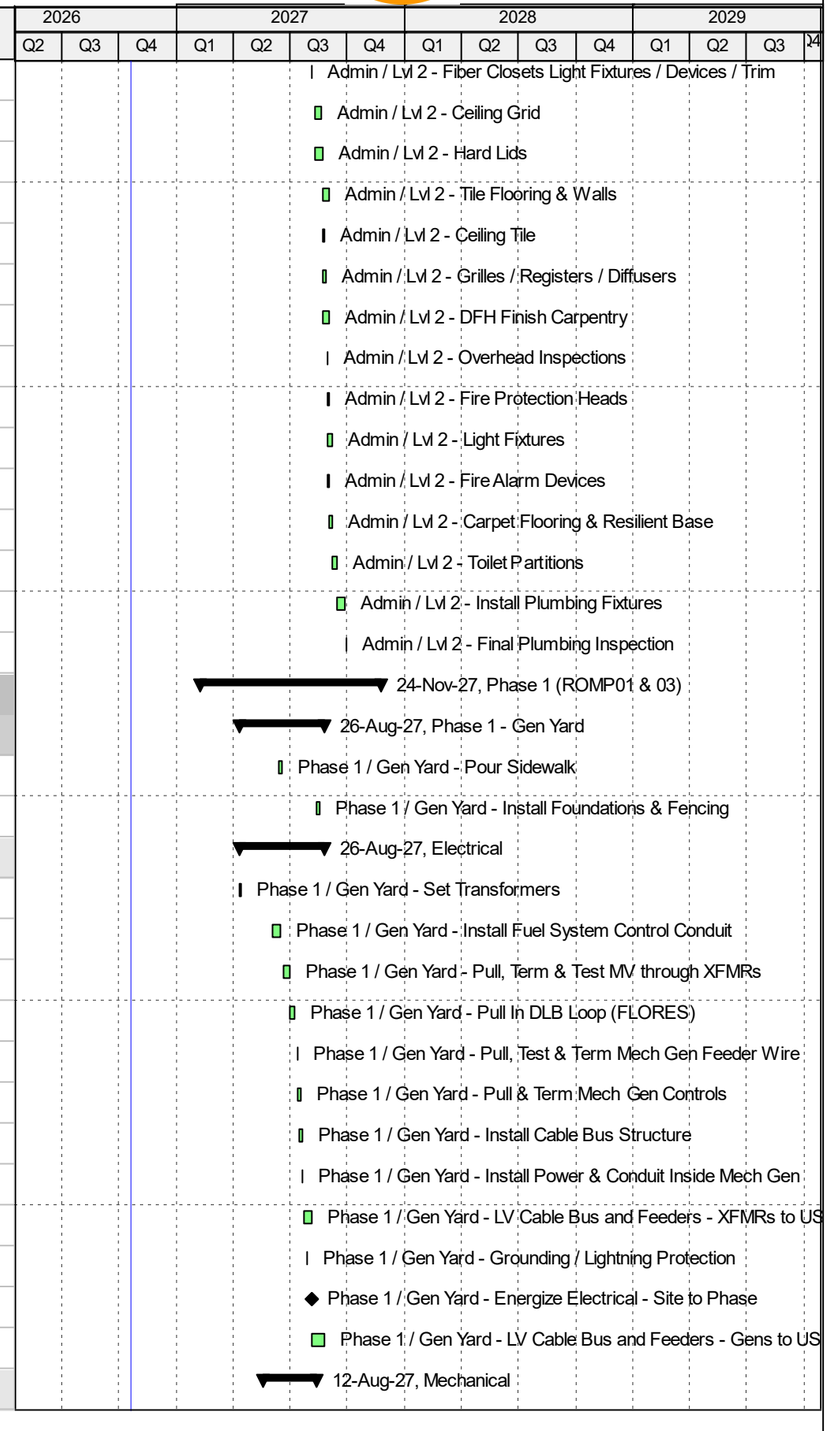

Activity ID	Activity Name	OD	RD	Start	Finish
P1EX.1260	Phase 1 / Gen Yard - Set Fuel Tank	1	1	19-May-27	19-May-27
P1EX.1270	Phase 1 / Gen Yard - Install Fuel Piping	30	30	20-May-27	01-Jul-27
P1EX.1160	Phase 1 / Gen Yard - Set Mechanical Generator	1	1	08-Jul-27	08-Jul-27
P1EX.1060	Phase 1 / Gen Yard - Set Main Service Generators	2	2	08-Jul-27	09-Jul-27
P1EX.1170	Phase 1 / Gen Yard - Set Exhaust For Mechanical Generator	3	3	09-Jul-27	13-Jul-27
P1EX.1220	Phase 1 / Gen Yard - CAT Load Banking	2	2	09-Jul-27	12-Jul-27
P1EX.1090	Phase 1 / Gen Yard - Set Exhaust Stack and Shroud	12	12	12-Jul-27	27-Jul-27
P1EX.1080	Phase 1 / Gen Yard - Install Generator Platforms	5	5	06-Aug-27	12-Aug-27
Phase 1 - Tank Yard		84	84	13-May-27	10-Sep-27
P1EX.1100	Phase 1 / Tank Yard - Build/Set IW Storage Tanks	15	15	13-May-27	03-Jun-27
P1EX.1330	Phase 1 / Tank Yard - Install Fence	14	14	04-Jun-27	23-Jun-27
P1EX.1310	Phase 1 / Tank Yard - Install Fence Foundations	6	6	04-Jun-27	11-Jun-27
P1EX.1320	Phase 1 / Tank Yard - Leak Test	6	6	04-Jun-27	11-Jun-27
P1EX.1340	Phase 1 / Tank Yard - Pipe IW Storage Tanks	50	50	11-Jun-27	20-Aug-27
P1EX.1350	Phase 1 / Tank Yard - Install Control Conduit	14	14	23-Aug-27	10-Sep-27
P1EX.1360	Phase 1 / Tank Yard - Install Lighting	8	8	24-Aug-27	03-Sep-27
Phase 1 - Electrical Room		120	120	09-Apr-27	28-Sep-27
P1ER.1320	Phase 1 / Elec Rm - Layout	1	1	09-Apr-27	09-Apr-27
P1ER.1130	Phase 1 / Elec Rm - Install DriClad	10	10	12-Apr-27	23-Apr-27
P1ER.1000	Phase 1 / Elec Rm - Pull TAHU Feeders	5	5	15-Apr-27	21-Apr-27
P1ER.1010	Phase 1 / Elec Rm - Pull Lighting Control Wiring	7	7	22-Apr-27	30-Apr-27
P1ER.1040	Phase 1 / Elec Rm - Wall Electric & Fire Alarm Rough-in	5	5	26-Apr-27	30-Apr-27
P1ER.1020	Phase 1 / Elec Rm - Stud Framing	4	4	27-Apr-27	30-Apr-27
P1ER.1170	Phase 1 / Elec Rm - Hangers	3	3	03-May-27	05-May-27
P1ER.1260	Phase 1 / Elec Rm - Fire Protection Rough In	3	3	06-May-27	10-May-27
P1ER.1240	Phase 1 / Elec Rm - Install OH Conduit / Mechanical Feeders	5	5	06-May-27	12-May-27
P1ER.1070	Phase 1 / Elec Rm - Set USB (LV Gear)	5	5	13-May-27	19-May-27
P1ER.1100	Phase 1 / Elec Rm - Breaker Testing USB	5	5	20-May-27	26-May-27
P1ER.1330	Phase 1 / Elec Rm - Fill Buck Out	4	4	20-May-27	25-May-27
P1ER.1340	Phase 1 / Elec Rm - Install Cable Tray	7	7	20-May-27	28-May-27
P1ER.1390	Phase 1 / Elec Rm - Pull / Term HUPPs	2	2	20-May-27	21-May-27
P1ER.1210	Phase 1 / Elec Rm - Set SCCS Setting for Breakers	1	1	27-May-27	27-May-27
P1ER.1140	Phase 1 / Elec Rm - Fire Alarm / VESDA	5	5	01-Jun-27	07-Jun-27



Activity ID	Activity Name	OD	RD	Start	Finish
P1ER.1350	Phase 1 / Elec Rm - Install Bus Duct	7	7	01-Jun-27	09-Jun-27
P1ER.1090	Phase 1 / Elec Rm - Install Control Conduit	5	5	01-Jun-27	07-Jun-27
P1ER.1060	Phase 1 / Elec Rm - Hang Drywall & Finish	5	5	16-Jun-27	22-Jun-27
P1ER.1080	Phase 1 / Elec Rm - Prime & First Coat Paint	1	1	23-Jun-27	23-Jun-27
P1ER.1190	Phase 1 / Elec Rm - Doors & Hardware	5	5	24-Jun-27	30-Jun-27
P1ER.1110	Phase 1 / Elec Rm - Set OFCI Electrical Panels	5	5	24-Jun-27	30-Jun-27
P1ER.1120	Phase 1 / Elec Rm - Install AMCOP Panels	1	1	24-Jun-27	24-Jun-27
P1ER.1300	Phase 1 / Elec Rm - Install Electrical Raceways (Branch Conduits)	10	10	01-Jul-27	15-Jul-27
P1ER.1380	Phase 1 / Elec Rm - Pull & Term DLB Fiber	5	5	01-Jul-27	08-Jul-27
P1ER.1400	Phase 1 / Elec Rm - Install UPS	4	4	01-Jul-27	07-Jul-27
P1ER.1150	Phase 1 / Elec Rm - Pull PDC Feeders	5	5	02-Jul-27	09-Jul-27
P1ER.1160	Phase 1 / Elec Rm - Terminate LV Electrical Panels	5	5	07-Jul-27	13-Jul-27
P1ER.1200	Phase 1 / Elec Rm - Manufacturer Inspection USB	1	1	09-Jul-27	09-Jul-27
P1ER.1050	Phase 1 / Elec Rm - Seismic Install	1	1	12-Jul-27	12-Jul-27
P1ER.1230	Phase 1 / Elec Rm - Test & Terminate PDC Feeders	5	5	12-Jul-27	16-Jul-27
P1ER.1220	Phase 1 / Elec Rm - Install Lighting	3	3	12-Jul-27	14-Jul-27
P1ER.1270	Phase 1 / Elec Rm - Egress Lighting	3	3	12-Jul-27	14-Jul-27
P1ER.1180	Phase 1 / Elec Rm - BMS System	10	10	14-Jul-27	27-Jul-27
P1ER.1290	Phase 1 / Elec Rm - Trade Repair	3	3	16-Jul-27	20-Jul-27
P1ER.1280	Phase 1 / Elec Rm - Final Paint / Touch Up	1	1	21-Jul-27	21-Jul-27
P1ER.1030	Phase 1 / Elec Rm - Cable Bus Termination	4	4	23-Jul-27	28-Jul-27
P1ER.1310	Phase 1 / Elec Rm - Energize BMS Panels	1	1	29-Jul-27	29-Jul-27
P1ER.1360	Phase 1 / Elec Rm - Install CRAC Unit & Exhaust Fan	5	5	15-Sep-27	21-Sep-27
P1ER.1370	Phase 1 / Elec Rm - OA Reference Piping	5	5	22-Sep-27	28-Sep-27
Phase 1 - Data Hall		156	156	23-Mar-27	29-Oct-27
P1RP.1590	Phase 1 / Data Hall - Fire Protection Rough In	5	5	23-Mar-27	29-Mar-27
P1RP.1510	Phase 1 / Data Hall - Install Temp Wall Bulkhead	5	5	22-Apr-27	28-Apr-27
P1RP.1430	Phase 1 / Data Hall - Stud Framing (Data Hall / Elec Rm Wall)	5	5	27-Apr-27	03-May-27
P1RP.1100	Phase 1 / Data Hall - Wall Elec & FA Rough-In (IMP)	4	4	29-Apr-27	04-May-27
P1RP.1360	Phase 1 / Data Hall - Above Ceiling Cable Tray	3	3	03-May-27	05-May-27
P1RP.1040	Phase 1 / Data Hall - Stud Framing (Equipment Platform)	5	5	03-May-27	07-May-27
P1RP.1500	Phase 1 / Data Hall - Wall Elec & FA Rough-In (Data Hall / Elec Rm)	4	4	04-May-27	07-May-27
P1RP.1350	Phase 1 / Data Hall - Seismic Install	2	2	06-May-27	07-May-27

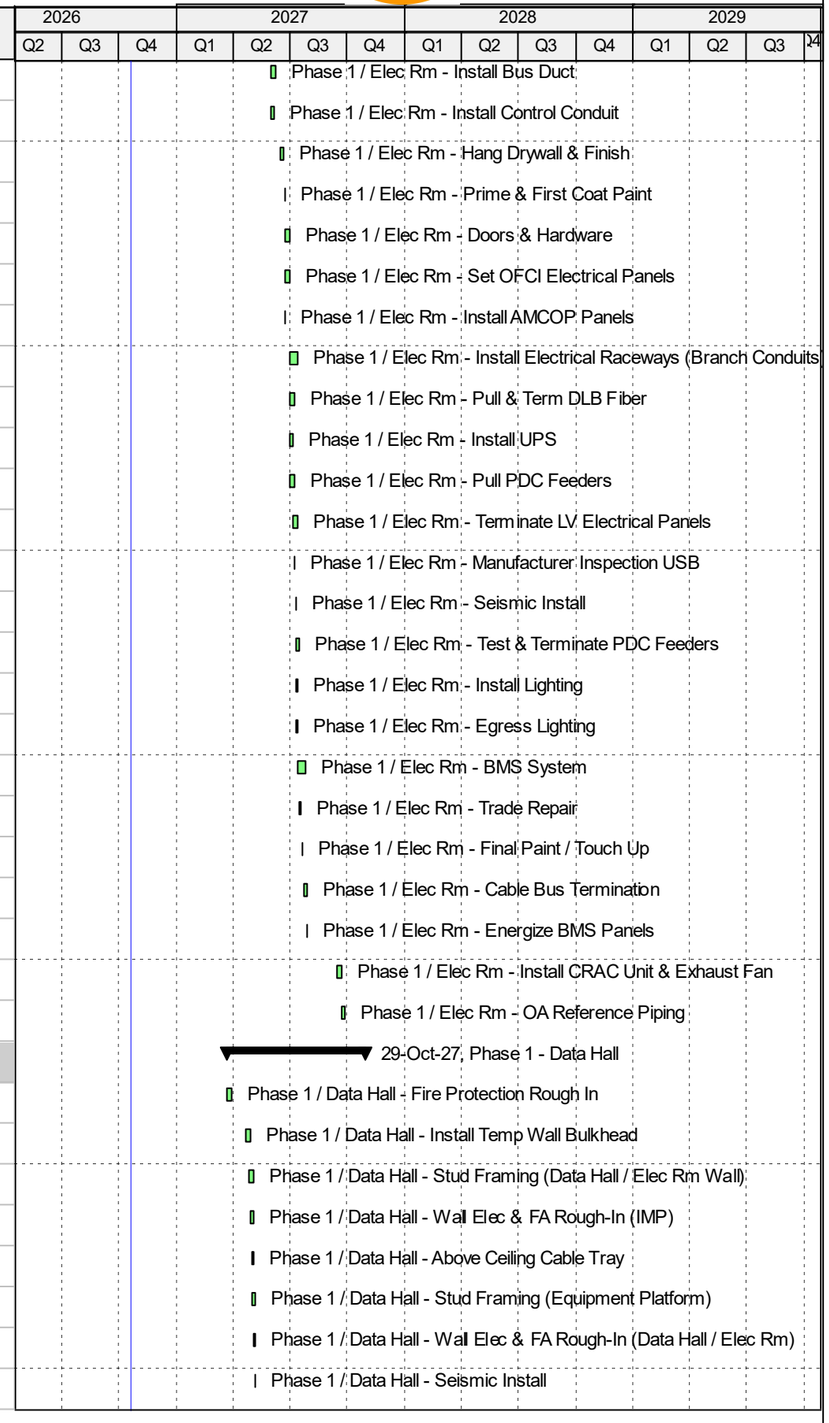


Gray

CMH139
Preliminary Schedule

aws


Activity ID	Activity Name	OD	RD	Start	Finish
P1RP.1570	Phase 1 / Data Hall - OH Electric Rough In	5	5	10-May-27	14-May-27
P1RP.1130	Phase 1 / Data Hall - In Wall Rough In Inspection (Electrical / FA)	1	1	20-May-27	20-May-27
P1RP.1460	Phase 1 / Data Hall - Hang Drywall & Finish (Data Hall / Elec Rm)	5	5	21-May-27	27-May-27
P1RP.1190	Phase 1 / Data Hall - Prime & First Coat Paint	3	3	28-May-27	02-Jun-27
P1RP.1420	Phase 1 / Data Hall - Install Backdraft Dampers	5	5	03-Jun-27	09-Jun-27
P1RP.1050	Phase 1 / Data Hall - Fire Protection Drops	5	5	03-Jun-27	09-Jun-27
P1RP.1020	Phase 1 / Data Hall - MARS Racking	7	7	08-Jun-27	16-Jun-27
P1RP.1070	Phase 1 / Data Hall - Install Lighting Wiring & Fixtures	5	5	17-Jun-27	23-Jun-27
P1RP.1200	Phase 1 / Data Hall - Temp Wall Install	5	5	17-Jun-27	23-Jun-27
P1RP.1060	Phase 1 / Data Hall - Upper Polycarbonate Panels and Cold Aisle Cable Tray Arms	3	3	17-Jun-27	21-Jun-27
P1RP.1090	Phase 1 / Data Hall - Power PDC Whips	10	10	17-Jun-27	30-Jun-27
P1RP.1150	Phase 1 / Data Hall - PDC Feeders Drops & Supports	10	10	17-Jun-27	30-Jun-27
P1RP.1520	Phase 1 / Data Hall - ACT Grid Corridors	4	4	17-Jun-27	22-Jun-27
P1RP.1030	Phase 1 / Data Hall - Install Snubbers	5	5	17-Jun-27	23-Jun-27
P1RP.1230	Phase 1 / Data Hall - Install Control Dampers (PRD)	5	5	21-Jun-27	25-Jun-27
P1RP.1210	Phase 1 / Data Hall - Fire Alarm VESDA	10	10	21-Jun-27	02-Jul-27
P1RP.1530	Phase 1 / Data Hall - ACT Grid Cold Aisles	5	5	21-Jun-27	25-Jun-27
P1RP.1260	Phase 1 / Data Hall - Perfect Position	4	4	22-Jun-27	25-Jun-27
P1RP.1250	Phase 1 / Data Hall - Doors and Hardware	2	2	24-Jun-27	25-Jun-27
P1RP.1490	Phase 1 / Data Hall - Avenue Basket/Cable Tray (South)	2	2	28-Jun-27	29-Jun-27
P1RP.1380	Phase 1 / Data Hall - Install Fire Protection Heads Avenue	2	2	28-Jun-27	29-Jun-27
P1RP.1280	Phase 1 / Data Hall - Install Fire Protection Heads Cold Aisle	2	2	28-Jun-27	29-Jun-27
P1RP.1160	Phase 1 / Data Hall - Cold Aisle Basket/Cable Tray	3	3	28-Jun-27	30-Jun-27
P1RP.1540	Phase 1 / Data Hall - ACT Borders For Corridors	1	1	28-Jun-27	28-Jun-27
P1RP.1580	Phase 1 / Data Hall - Install Control Wiring	5	5	28-Jun-27	02-Jul-27
P1RP.1550	Phase 1 / Data Hall - ACT Borders For Cold Aisles	1	1	29-Jun-27	29-Jun-27
P1RP.1390	Phase 1 / Data Hall - Structural Overhead Inspection (Avenue)	1	1	30-Jun-27	30-Jun-27
P1RP.1290	Phase 1 / Data Hall - Avenue Basket/Cable Tray (North)	2	2	30-Jun-27	01-Jul-27
P1RP.1560	Phase 1 / Data Hall - ACT Remaining Tile Drops Post Inspection	3	3	01-Jul-27	06-Jul-27
P1RP.1340	Phase 1 / Data Hall - CAT6 Cable Install	3	3	02-Jul-27	07-Jul-27
P1RP.1220	Phase 1 / Data Hall - Touch Up Paint	4	4	06-Jul-27	09-Jul-27
P1RP.1080	Phase 1 / Data Hall - Set PDC Cabinets	3	3	07-Jul-27	09-Jul-27
P1RP.1120	Phase 1 / Data Hall - EPMS	15	15	12-Jul-27	30-Jul-27

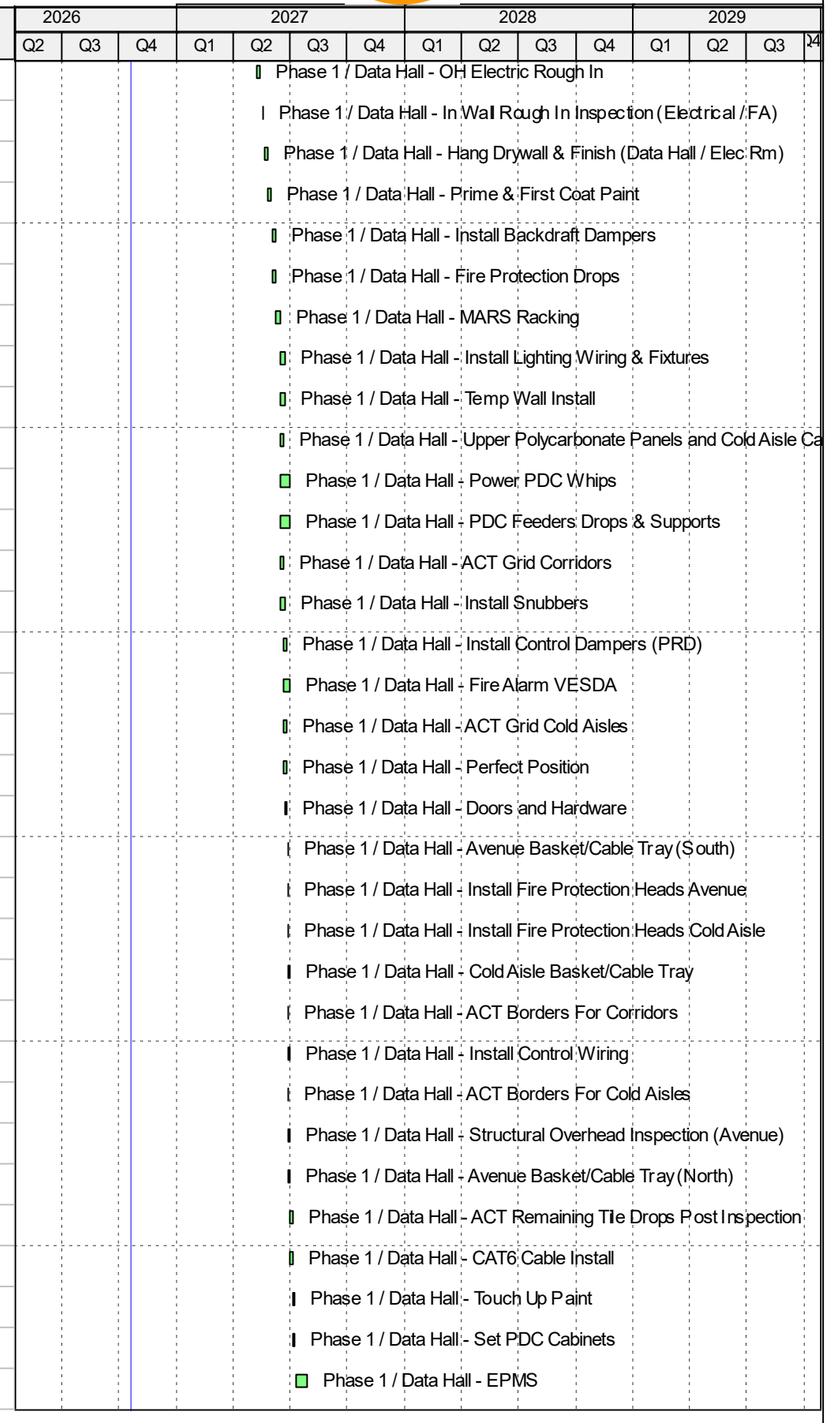

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary


Run Date: 15-Oct-26 14:16
Data Date: 19-Oct-26

Activity ID	Activity Name	OD	RD	Start	Finish
P1RP.1110	Phase 1 / Data Hall - BMS	15	15	12-Jul-27	30-Jul-27
P1RP.1270	Phase 1 / Data Hall - PDC Feeders Test & Terminate	10	10	12-Jul-27	23-Jul-27
P1RP.1180	Phase 1 / Data Hall - Lower Polycarbonate Panels	5	5	02-Aug-27	06-Aug-27
P1RP.1240	Phase 1 / Data Hall - NEA Finalization	10	10	28-Sep-27	11-Oct-27
P1RP.1300	Phase 1 / Data Hall - H2C Readiness Coordination	14	14	12-Oct-27	29-Oct-27
Phase 1 - TAHU Gallery		100	100	19-Mar-27	09-Aug-27
P1DG.1330	Phase 1 / TAHU - Fire Protection Rough In	2	2	19-Mar-27	22-Mar-27
P1DG.1170	Phase 1 / TAHU - Seismic Install	2	2	20-May-27	21-May-27
P1DG.1320	Phase 1 / TAHU - Sound Attenuator	10	10	20-May-27	03-Jun-27
P1DG.1110	Phase 1 / TAHU - Install CFMF IMP Support	10	10	20-May-27	03-Jun-27
P1DG.1200	Phase 1 / TAHU - Hang Outside Stairwell / Lobby Drywall	4	4	20-May-27	25-May-27
P1DG.1040	Phase 1 / TAHU - Install IMP Panels	6	6	04-Jun-27	11-Jun-27
P1DG.1080	Phase 1 / TAHU - Prime & Paint Drywall	3	3	14-Jun-27	16-Jun-27
P1DG.1010	Phase 1 / TAHU - BMS Controls Rough In	10	10	14-Jun-27	25-Jun-27
P1DG.1030	Phase 1 / TAHU - Wall Elec & Fire Alarm Rough-In	5	5	14-Jun-27	18-Jun-27
P1DG.1090	Phase 1 / TAHU - Fire Alarm (VESDA)	5	5	14-Jun-27	18-Jun-27
P1DG.1190	Phase 1 / TAHU - Control Dampers	5	5	17-Jun-27	23-Jun-27
P1DG.1050	Phase 1 / TAHU - Pull & Terminate Fire Alarm Cable	5	5	21-Jun-27	25-Jun-27
P1DG.1070	Phase 1 / TAHU - Set TAHUs	2	2	28-Jun-27	29-Jun-27
P1DG.1140	Phase 1 / TAHU - Doors and Hardware	3	3	30-Jun-27	02-Jul-27
P1DG.1060	Phase 1 / TAHU - IW Supply Piping at TAHUs	10	10	30-Jun-27	14-Jul-27
P1DG.1150	Phase 1 / TAHU - Lighting	5	5	30-Jun-27	07-Jul-27
P1DG.1100	Phase 1 / TAHU - TAHU Trim	10	10	30-Jun-27	14-Jul-27
P1DG.1160	Phase 1 / TAHU - Paint Doors & Frames	2	2	06-Jul-27	07-Jul-27
P1DG.1000	Phase 1 / TAHU - Tie In TAHUs	10	10	15-Jul-27	28-Jul-27
P1DG.1130	Phase 1 / TAHU - BMS Tie In	2	2	27-Jul-27	28-Jul-27
P1DG.1120	Phase 1 / TAHU - IW Drain Piping at TAHUs	5	5	29-Jul-27	04-Aug-27
P1DG.1180	Phase 1 / TAHU - Terminate Power To TAHUs	3	3	05-Aug-27	09-Aug-27
Phase 1 - Catcher C1		142	142	08-Feb-27	26-Aug-27
P1C1.1220	Phase 1 / C1 - Intumescent Paint on Structural Steel	4	4	08-Feb-27	11-Feb-27
P1C1.1120	Phase 1 / C1 - Install AMCOP Panels	5	5	13-Apr-27	19-Apr-27
P1C1.1000	Phase 1 / C1 - Pull Lighting Control Wiring	7	7	03-May-27	11-May-27
P1C1.1240	Phase 1 / C1 - Seismic Install	1	1	20-May-27	20-May-27

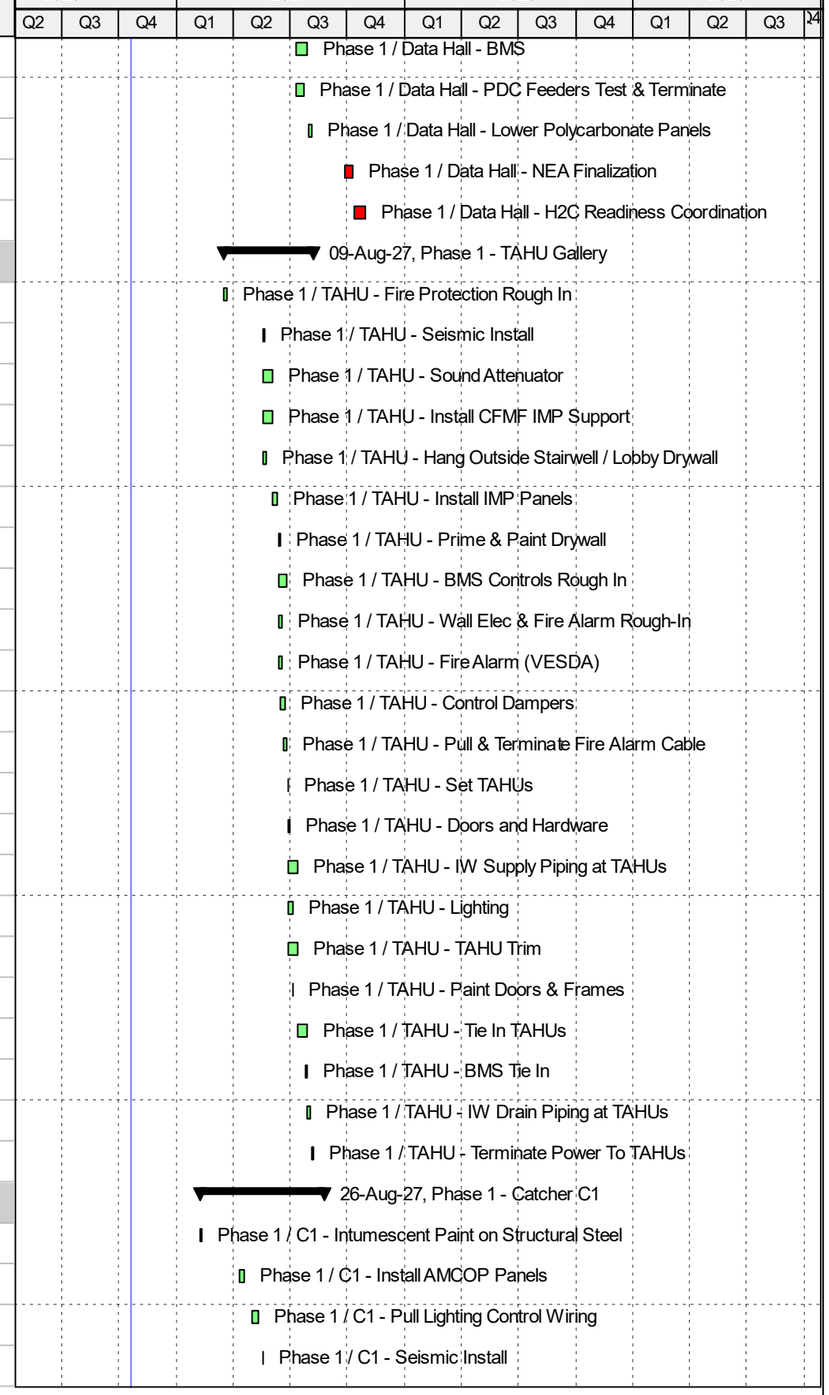

CMH139
Preliminary Schedule


Activity ID	Activity Name	OD	RD	Start	Finish
P1C1.1010	Phase 1 / C1 - Stud Framing	5	5	21-May-27	27-May-27
P1C1.1030	Phase 1 / C1 - Wall Electric & Fire Alarm Rough-in	2	2	26-May-27	27-May-27
P1C1.1050	Phase 1 / C1 - Hang Drywall & Finish	5	5	28-May-27	04-Jun-27
P1C1.1060	Phase 1 / C1 - Set USB	2	2	02-Jun-27	03-Jun-27
P1C1.1140	Phase 1 / C1 - Set SCCS Setting for Breakers	1	1	04-Jun-27	04-Jun-27
P1C1.1090	Phase 1 / C1 - Breaker Testing USB	5	5	04-Jun-27	10-Jun-27
P1C1.1080	Phase 1 / C1 - Install Busway C1 & C2	5	5	04-Jun-27	10-Jun-27
P1C1.1190	Phase 1 / C1 - Doors and Hardware	5	5	07-Jun-27	11-Jun-27
P1C1.1070	Phase 1 / C1 - Prime & First Coat Paint	2	2	07-Jun-27	08-Jun-27
P1C1.1110	Phase 1 / C1 - Install Split Systems & ERV	10	10	09-Jun-27	22-Jun-27
P1C1.1100	Phase 1 / C1 - Set OFCI Electrical Panels	5	5	09-Jun-27	15-Jun-27
P1C1.1130	Phase 1 / C1 - Manufacturer Inspection USB	1	1	11-Jun-27	11-Jun-27
P1C1.1150	Phase 1 / C1 - Install Lighting	10	10	16-Jun-27	29-Jun-27
P1C1.1160	Phase 1 / C1 - Terminate LV Electrical Panels	5	5	07-Jul-27	13-Jul-27
P1C1.1180	Phase 1 / C1 - BMS System	10	10	14-Jul-27	27-Jul-27
P1C1.1210	Phase 1 / C1 - LV Panelboards Energized	0	0		26-Aug-27
Phase 1 - Catcher C2		142	142	08-Feb-27	26-Aug-27
P1C2.1220	Phase 1 / C2 - Intumescent Paint Structural Steel	4	4	08-Feb-27	11-Feb-27
P1C2.1120	Phase 1 / C2 - Install AMCOP Panels	5	5	13-Apr-27	19-Apr-27
P1C2.1030	Phase 1 / C2 - Wall Electric & Fire Alarm Rough-in	5	5	26-Apr-27	30-Apr-27
P1C2.1010	Phase 1 / C2 - Stud Framing	4	4	27-Apr-27	30-Apr-27
P1C2.1240	Phase 1 / C2 - Hang Drywall & Finish	6	6	03-May-27	10-May-27
P1C2.1050	Phase 1 / C2 - Hang Drywall & Finish (One Side)	6	6	03-May-27	10-May-27
P1C2.1000	Phase 1 / C2 - Pull Lighting Control Wiring	7	7	03-May-27	11-May-27
P1C2.1070	Phase 1 / C2 - Prime & First Coat Paint	1	1	11-May-27	11-May-27
P1C2.1110	Phase 1 / C2 - Install Split Systems & ERV	10	10	12-May-27	25-May-27
P1C2.1230	Phase 1 / C2 - Seismic Install	1	1	21-May-27	21-May-27
P1C2.1020	Phase 1 / C2 - OSA Ductwork	3	3	07-Jun-27	09-Jun-27
P1C2.1060	Phase 1 / C2 - Set USB	2	2	10-Jun-27	11-Jun-27
P1C2.1140	Phase 1 / C2 - Set SCCS Setting for Breakers	1	1	14-Jun-27	14-Jun-27
P1C2.1190	Phase 1 / C2 - Doors and Hardware	5	5	14-Jun-27	18-Jun-27
P1C2.1090	Phase 1 / C2 - Breaker Testing USB	5	5	14-Jun-27	18-Jun-27
P1C2.1100	Phase 1 / C2 - Set OFCI Electrical Panels	1	1	14-Jun-27	14-Jun-27

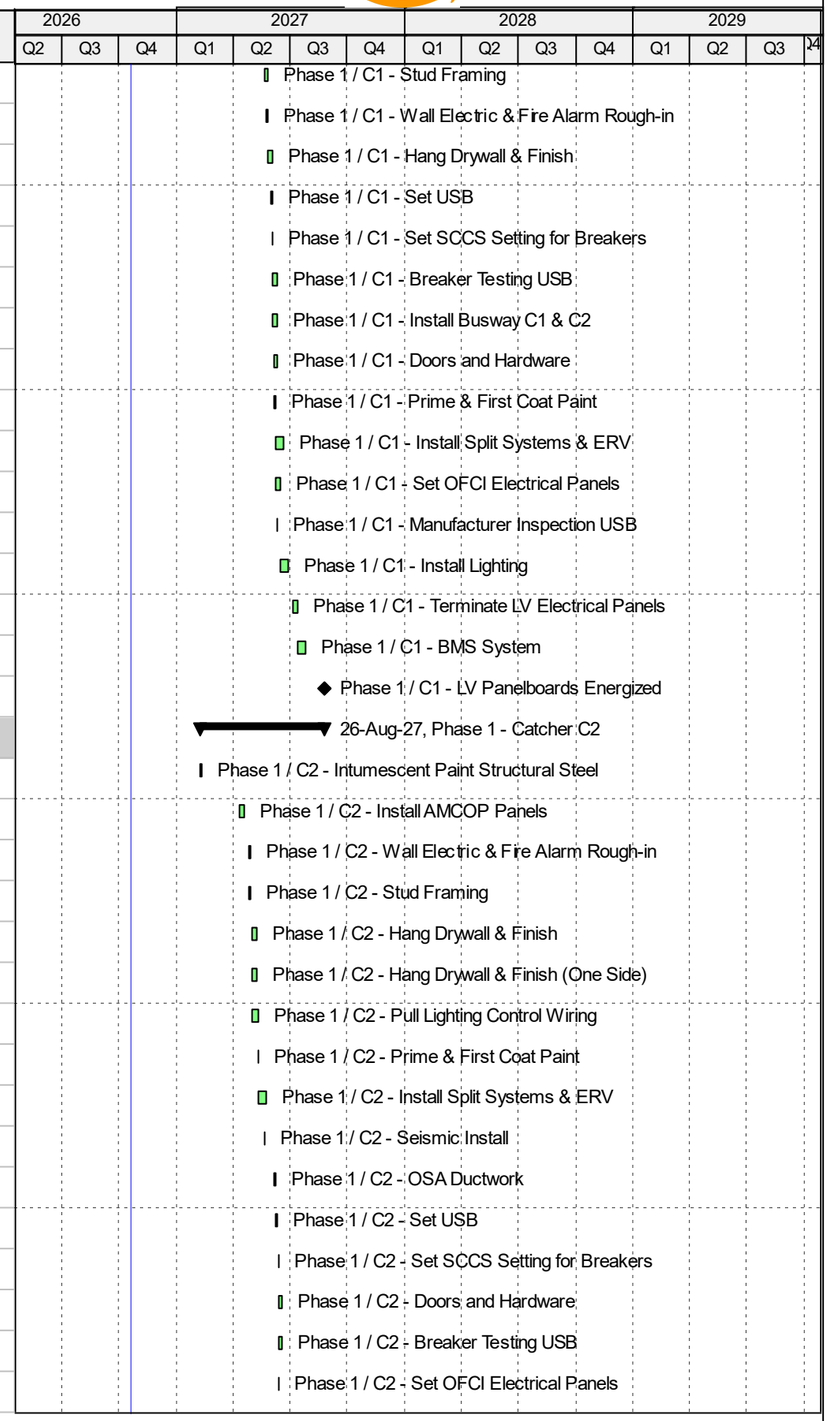

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary


Run Date: 15-Oct-26 14:16
Data Date: 19-Oct-26

Activity ID	Activity Name	OD	RD	Start	Finish
P1C2.1080	Phase 1 / C2 - Install Busway C1 & C2	5	5	14-Jun-27	18-Jun-27
P1C2.1150	Phase 1 / C2 - Install Lighting	10	10	15-Jun-27	28-Jun-27
P1C2.1130	Phase 1 / C2 - Manufacturer Inspection USB	1	1	21-Jun-27	21-Jun-27
P1C2.1160	Phase 1 / C2 - Terminate LV Electrical Panels	3	3	07-Jul-27	09-Jul-27
P1C2.1180	Phase 1 / C2 - BMS System	10	10	12-Jul-27	23-Jul-27
P1C2.1210	Phase 1 / C2 - LV Panelboards Energized	0	0		26-Aug-27
Phase 1 - Cx		118	118	10-Jun-27	24-Nov-27
P1CX.1020	Phase 1 / Cx - EC 3rd Party Busway Bus Plug Testing (L2)	2	2	10-Jun-27	11-Jun-27
P1CX.1050	Phase 1 / Cx - EC 3rd Party Testing & Inspection USB (L2)	3	3	14-Jun-27	16-Jun-27
P1CX.1180	Phase 1 / Cx - Tie In MOP C1	2	2	14-Jun-27	15-Jun-27
P1CX.2020	Phase 1 / Cx - Tie In MOP C2	2	2	16-Jun-27	17-Jun-27
P1CX.1140	Phase 1 / Cx - EC 3rd Party Busway C1 / C2 Testing	2	2	21-Jun-27	22-Jun-27
P1CX.1170	Phase 1 / Cx - EC Busway C1 / C2 L2 Cx Review	1	1	23-Jun-27	23-Jun-27
P1CX.1220	Phase 1 / Cx - EC Busway C1 L3 Cx	2	2	24-Jun-27	25-Jun-27
P1CX.1320	Phase 1 / Cx - AMCOP / BACOP Start Up & Cx	5	5	25-Jun-27	01-Jul-27
P1CX.2010	Phase 1 / Cx - EC Busway C2 L3 Cx	2	2	28-Jun-27	29-Jun-27
P1CX.1000	Phase 1 / Cx - EC 3rd Party LV Panelboard Testing (L2)	3	3	01-Jul-27	06-Jul-27
P1CX.1100	Phase 1 / Cx - EC L2 Cx Review for MV Switchgear	1	1	01-Jul-27	01-Jul-27
P1CX.1080	Phase 1 / Cx - EC L2 CX Review for MV XFMRs	1	1	02-Jul-27	02-Jul-27
P1CX.1200	Phase 1 / Cx - Fuel System Cx	7	7	02-Jul-27	13-Jul-27
P1CX.1090	Phase 1 / Cx - EC L3 Cx for MV XFMRs	5	5	06-Jul-27	12-Jul-27
P1CX.1430	Phase 1 / Cx - Eaton XFMR Testing	3	3	06-Jul-27	08-Jul-27
P1CX.2000	Phase 1 / Cx - Fire Alarm Programming & Pretest	2	2	06-Jul-27	07-Jul-27
P1CX.1130	Phase 1 / Cx - EC L3 Cx for MV	3	3	09-Jul-27	13-Jul-27
P1CX.1420	Phase 1 / Cx - Eaton DLB Programming & Test (FLORES)	5	5	09-Jul-27	15-Jul-27
P1CX.1120	Phase 1 / Cx - Construction Power To Generator	3	3	12-Jul-27	14-Jul-27
P1CX.1160	Phase 1 / Cx - HUPPS Panelboards Energized	1	1	14-Jul-27	14-Jul-27
P1CX.1340	Phase 1 / Cx - Energize Control Network Arch	1	1	15-Jul-27	15-Jul-27
P1CX.1030	Phase 1 / Cx - CAT L2 Cx Generators	2	2	15-Jul-27	16-Jul-27
P1CX.1350	Phase 1 / Cx - Office HVAC / Mechanical Startup	5	5	16-Jul-27	22-Jul-27
P1CX.2050	Phase 1 / Cx - EPMS Point to Point (USB)	4	4	16-Jul-27	21-Jul-27
P1CX.2070	Phase 1 / Cx - EPMS Point to Point (PDC)	4	4	19-Jul-27	22-Jul-27
P1CX.2060	Phase 1 / Cx - BMS Point to Point (TAHUs)	5	5	28-Jul-27	03-Aug-27

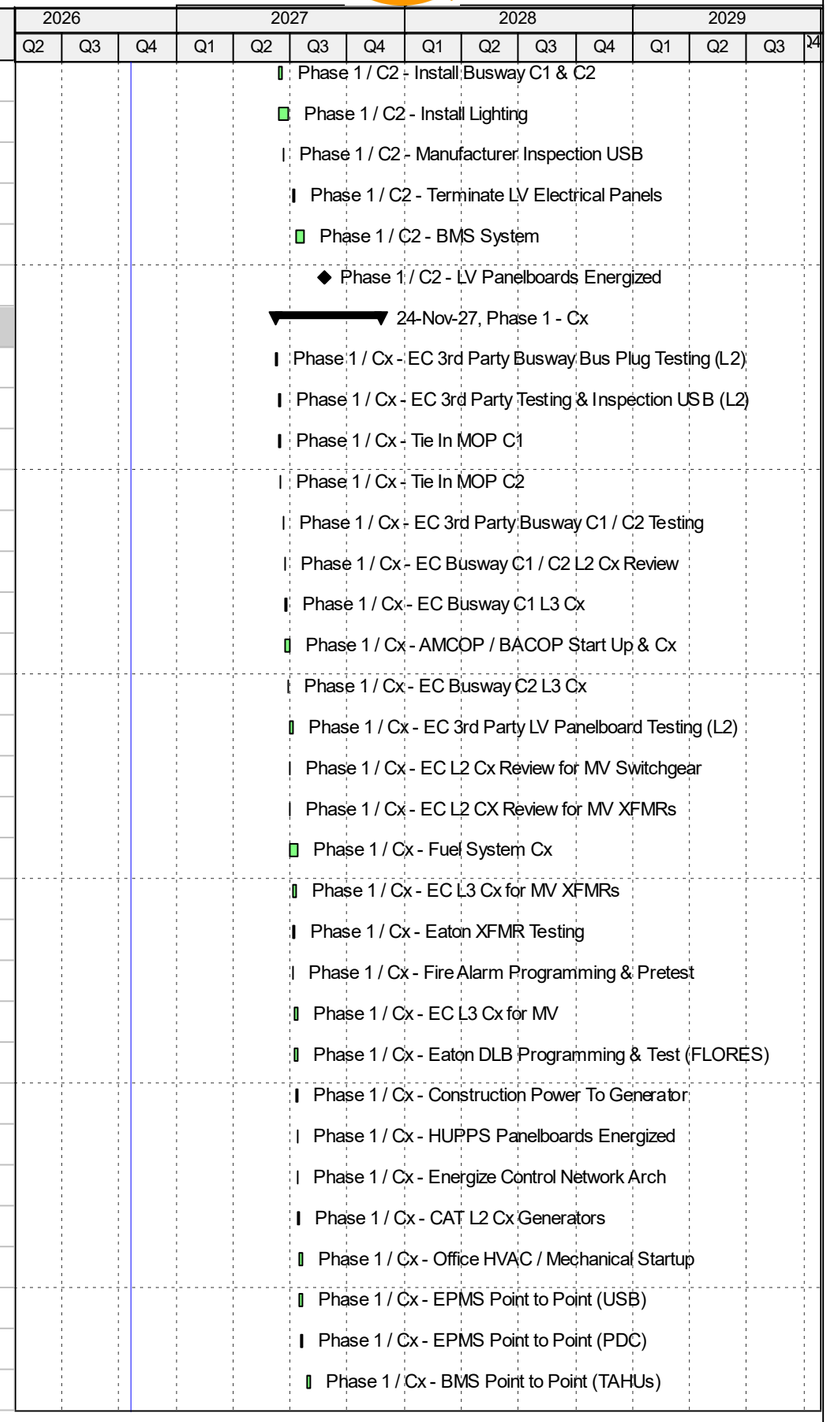


CMH139
Preliminary Schedule


Activity ID	Activity Name	OD	RD	Start	Finish
P1CX.1150	Phase 1 / Cx - EC L3 Cx USBs	2	2	06-Aug-27	09-Aug-27
P1CX.1250	Phase 1 / Cx - Vendor UPS Start Up & Cx	9	9	10-Aug-27	20-Aug-27
P1CX.1310	Phase 1 / Cx - ATS L3 Cx	1	1	10-Aug-27	10-Aug-27
P1CX.1210	Phase 1 / Cx - MC TAHU L2 Cx	5	5	10-Aug-27	16-Aug-27
P1CX.1440	Phase 1 / Cx - Eaton DLB Testing	2	2	10-Aug-27	11-Aug-27
OFCX.1400	Phase 1 / Cx - Admin VRF L2 Cx Review	2	2	11-Aug-27	12-Aug-27
P1CX.1370	Phase 1 / Cx - Energize MSDBs	1	1	11-Aug-27	11-Aug-27
OFCX.1220	Phase 1 / Cx - Admin VRF L3 Cx	5	5	13-Aug-27	19-Aug-27
P1CX.1410	Phase 1 / Cx - IW System L2 Cx	2	2	23-Aug-27	24-Aug-27
P1EX.1130	Phase 1 / Cx - Pull / Term / Test Fire Riser	5	5	25-Aug-27	31-Aug-27
P1CX.1400	Phase 1 / Cx - IW System L3 Cx	10	10	25-Aug-27	08-Sep-27
P1CX.1190	Phase 1 / Cx - EC L2 CX Review for LV Panelboard	2	2	25-Aug-27	26-Aug-27
P1CX.1040	Phase 1 / Cx - EC L2 Cx Review for Generator	1	1	27-Aug-27	27-Aug-27
P1CX.1260	Phase 1 / Cx - EC L3 Cx LV Panelboard	1	1	27-Aug-27	27-Aug-27
P1CX.1070	Phase 1 / Cx - EC L3 Cx Generators	3	3	30-Aug-27	01-Sep-27
P1CX.1060	Phase 1 / Cx - CAT L3 Cx Generators Testing	5	5	30-Aug-27	03-Sep-27
P1CX.1290	Phase 1 / Cx - Split System Startup & Commissioning	5	5	30-Aug-27	03-Sep-27
P1CX.1280	Phase 1 / Cx - ERV Startup & Commissioning	5	5	30-Aug-27	03-Sep-27
P1CX.1270	Phase 1 / Cx - EDH Startup & Commissioning	4	4	30-Aug-27	02-Sep-27
P1CX.1240	Phase 1 / Cx - Vendor TAHU L3 Cx	10	10	09-Sep-27	22-Sep-27
OFCX.1330	Phase 1 / Cx - Office Test & Balance	3	3	13-Sep-27	15-Sep-27
P1CX.1330	Phase 1 / Cx - Test & Balance	5	5	23-Sep-27	29-Sep-27
P1CX.1360	Phase 1 / Cx - Life Safety Walkthrough	1	1	28-Oct-27	28-Oct-27
P1CX.1380	Phase 1 / Cx - L4 / L5 Cx	18	18	01-Nov-27	24-Nov-27
Phase 2 (ROMP02 & 04)		204	204	19-Mar-27	07-Jan-28
Phase 2 - Gen Yard		94	94	15-Apr-27	26-Aug-27
P2EX.1030	Phase 2 / Gen Yard - Set Transformers	2	2	15-Apr-27	16-Apr-27
P2EX.1050	Phase 2 / Gen Yard - Pull, Term & Test MV through XFMRs	7	7	19-Apr-27	27-Apr-27
P2EX.1100	Phase 2 / Gen Yard - Pull In FLORES Loop	5	5	28-Apr-27	04-May-27
P2EX.1370	Phase 2 / Gen Yard - Install Fuel Piping	30	30	20-May-27	01-Jul-27
P2EX.1380	Phase 2 / Gen Yard - Install Fuel System Control Conduit	10	10	04-Jun-27	17-Jun-27
P2EX.1160	Phase 2 / Gen Yard - Pour Sidewalk	5	5	14-Jun-27	18-Jun-27
P2EX.1060	Phase 2 / Gen Yard - Set Generators	2	2	08-Jul-27	09-Jul-27

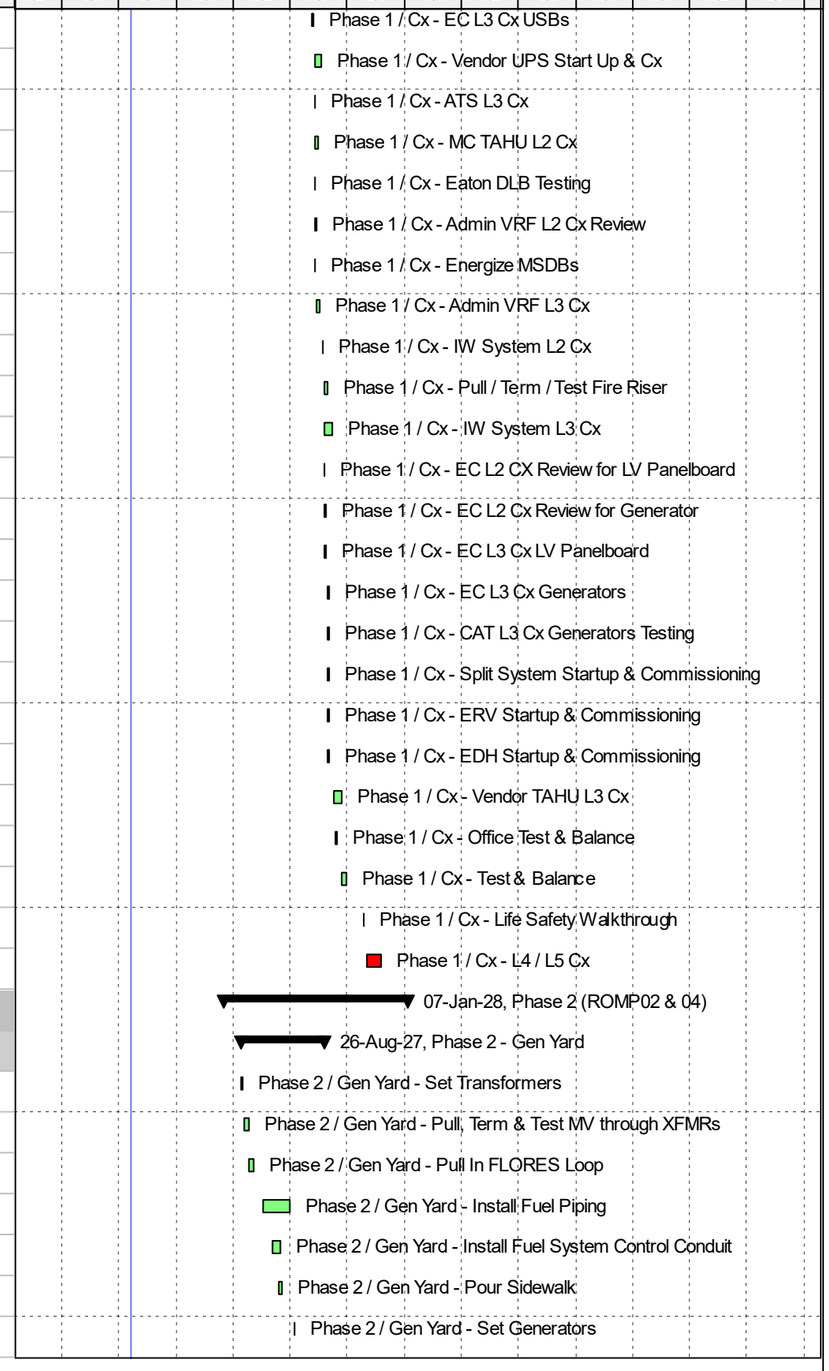

Activity ID	Activity Name	OD	RD	Start	Finish
P2EX.1090	Phase 2 / Gen Yard - Set Exhaust Stack and Shroud	12	12	12-Jul-27	27-Jul-27
P2EX.1040	Phase 2 / Gen Yard - Install Cable Bus Structure	5	5	16-Jul-27	22-Jul-27
P2EX.1070	Phase 2 / Gen Yard - LV Cable Bus and Feeders - XFMRs to USBs	10	10	23-Jul-27	05-Aug-27
P2EX.1140	Phase 2 / Gen Yard - Grounding / Lightning Protection	2	2	28-Jul-27	29-Jul-27
P2EX.1110	Phase 2 / Gen Yard - Energize Electrical - Site To Phase	0	0		05-Aug-27
P2EX.1130	Phase 2 / Gen Yard - LV Cable Bus and Feeders - Gens to USBs	15	15	06-Aug-27	26-Aug-27
P2EX.1080	Phase 2 / Gen Yard - Install Generator Platforms	5	5	09-Aug-27	13-Aug-27
P2EX.1120	Phase 2 / Gen Yard - Install Foundations & Fencing	4	4	16-Aug-27	19-Aug-27
Phase 2 - Electrical Room		128	128	14-Apr-27	13-Oct-27
P2ER.1380	Phase 2 / Elec Rm - Layout	1	1	14-Apr-27	14-Apr-27
P2ER.1620	Phase 2 / Elec Rm - Install DriClad	10	10	15-Apr-27	28-Apr-27
P2ER.1000	Phase 2 / Elec Rm - Pull TAHU Feeders	5	5	22-Apr-27	28-Apr-27
P2ER.1040	Phase 2 / Elec Rm - Wall Electric & Fire Alarm Rough-in	5	5	28-Apr-27	04-May-27
P2ER.1020	Phase 2 / Elec Rm - Stud Framing	4	4	29-Apr-27	04-May-27
P2ER.1010	Phase 2 / Elec Rm - Pull Lighting Control Wiring	7	7	29-Apr-27	07-May-27
P2ER.1050	Phase 2 / Elec Rm - Hangers	3	3	05-May-27	07-May-27
P2ER.1400	Phase 2 / Elec Rm - Install OH Conduit / Mechanical Feeders	5	5	10-May-27	14-May-27
P2ER.1060	Phase 2 / Elec Rm - Hang Drywall & Finish	5	5	01-Jun-27	07-Jun-27
P2ER.1390	Phase 2 / Elec Rm - Fire Protection Rough In	3	3	01-Jun-27	03-Jun-27
P2ER.1590	Phase 2 / Elec Rm - Pull / Term HUPPs	2	2	04-Jun-27	07-Jun-27
P2ER.1080	Phase 2 / Elec Rm - Prime & First Coat Paint	1	1	08-Jun-27	08-Jun-27
P2ER.1120	Phase 2 / Elec Rm - Install Split Systems & ERV	10	10	09-Jun-27	22-Jun-27
P2ER.1410	Phase 2 / Elec Rm - Set USB (LV Gear)	5	5	15-Jun-27	21-Jun-27
P2ER.1140	Phase 2 / Elec Rm - Install AMCOP Panels	1	1	22-Jun-27	22-Jun-27
P2ER.1430	Phase 2 / Elec Rm - Doors & Hardware	5	5	22-Jun-27	28-Jun-27
P2ER.1440	Phase 2 / Elec Rm - Breaker Testing USB	5	5	22-Jun-27	28-Jun-27
P2ER.1420	Phase 2 / Elec Rm - Fill Buck Out	4	4	22-Jun-27	25-Jun-27
P2ER.1450	Phase 2 / Elec Rm - Install Cable Tray	7	7	22-Jun-27	30-Jun-27
P2ER.1210	Phase 2 / Elec Rm - Set SCCS Setting for Breakers	1	1	29-Jun-27	29-Jun-27
P2ER.1110	Phase 2 / Elec Rm - Set OFCI Electrical Panels	5	5	01-Jul-27	08-Jul-27
P2ER.1470	Phase 2 / Elec Rm - Fire Alarm / VESDA	5	5	01-Jul-27	08-Jul-27
P2ER.1490	Phase 2 / Elec Rm - Install Bus Duct	7	7	01-Jul-27	12-Jul-27
P2ER.1600	Phase 2 / Elec Rm - Install Control Conduit	5	5	01-Jul-27	08-Jul-27

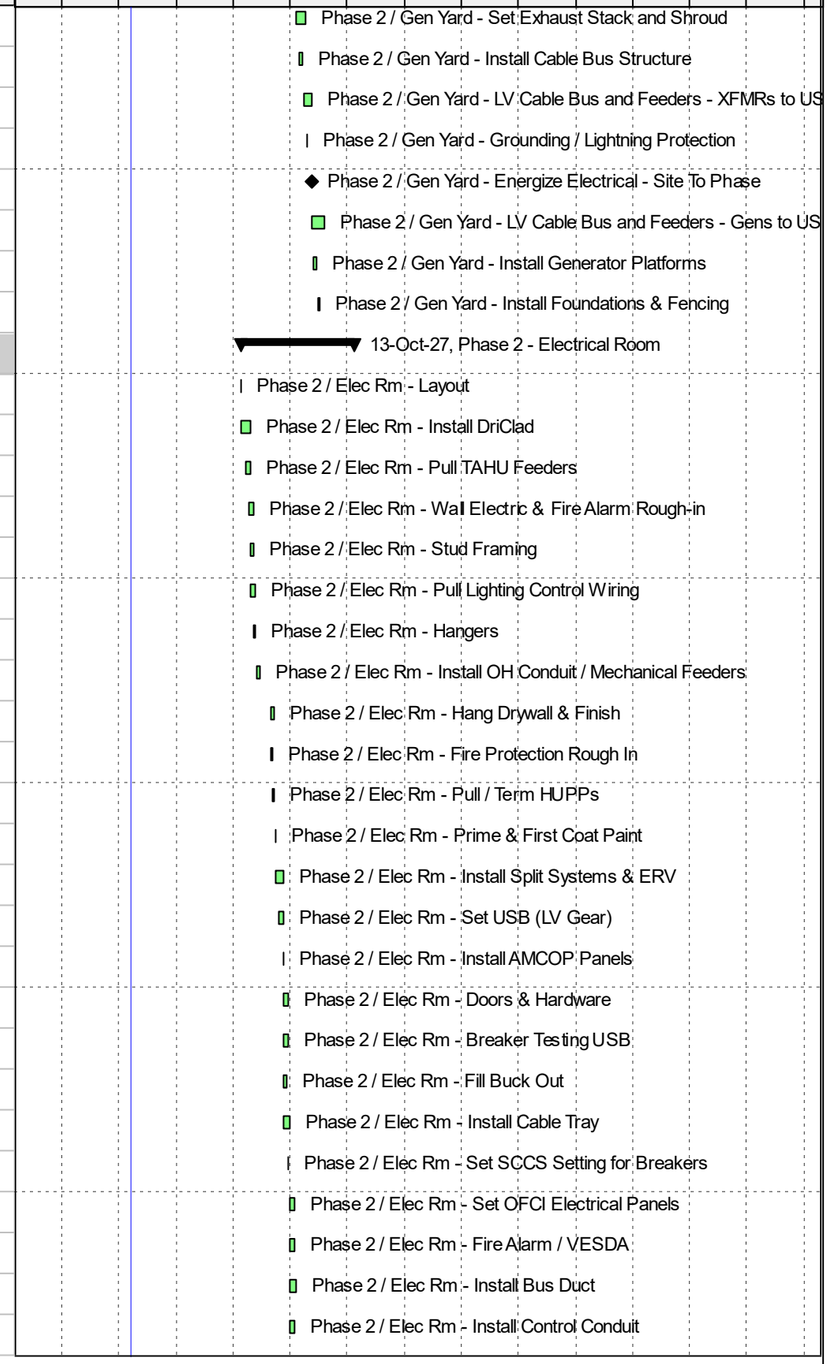

Activity ID	Activity Name	OD	RD	Start	Finish
P2ER.1500	Phase 2 / Elec Rm - Install Electrical Raceways (Branch Conduits)	10	10	09-Jul-27	22-Jul-27
P2ER.1610	Phase 2 / Elec Rm - Install UPS	4	4	09-Jul-27	14-Jul-27
P2ER.1160	Phase 2 / Elec Rm - Terminate LV Electrical Panels	5	5	14-Jul-27	20-Jul-27
P2ER.1530	Phase 2 / Elec Rm - Pull & Term DLB Fiber	5	5	19-Jul-27	23-Jul-27
P2ER.1385	Phase 2 / Elec Rm - Pull PDC Feeders	5	5	20-Jul-27	26-Jul-27
P2ER.1460	Phase 2 / Elec Rm - Cable Bus Termination	4	4	23-Jul-27	28-Jul-27
P2ER.1520	Phase 2 / Elec Rm - Manufacturer Inspection USB	1	1	26-Jul-27	26-Jul-27
P2ER.1540	Phase 2 / Elec Rm - Seismic Install	1	1	27-Jul-27	27-Jul-27
P2ER.1570	Phase 2 / Elec Rm - Test & Terminate PDC Feeders	5	5	27-Jul-27	02-Aug-27
P2ER.1550	Phase 2 / Elec Rm - Egress Lighting	3	3	27-Jul-27	29-Jul-27
P2ER.1560	Phase 2 / Elec Rm - Trade Repair	3	3	27-Jul-27	29-Jul-27
P2ER.1310	Phase 2 / Elec Rm - Install Lighting	3	3	27-Jul-27	29-Jul-27
P2ER.1580	Phase 2 / Elec Rm - Final Paint / Touch Up	1	1	30-Jul-27	30-Jul-27
P2ER.1480	Phase 2 / Elec Rm - Install CRAC Unit & Exhaust Fan	5	5	15-Sep-27	21-Sep-27
P2ER.1510	Phase 2 / Elec Rm - OA Reference Piping	5	5	22-Sep-27	28-Sep-27
P2ER.1180	Phase 2 / Elec Rm - BMS System	10	10	29-Sep-27	12-Oct-27
P2ER.1290	Phase 2 / Elec Rm - Energize BMS Panels	1	1	13-Oct-27	13-Oct-27
Phase 2 - Data Hall		186	186	26-Mar-27	17-Dec-27
P2RP.1750	Phase 2 / Data Hall - Fire Protection Rough In	5	5	26-Mar-27	01-Apr-27
P2RP.1040	Phase 2 / Data Hall - Stud Framing (Data Hall / Elec Rm Wall)	5	5	29-Apr-27	05-May-27
P2RP.1590	Phase 2 / Data Hall - Install Temp Wall Bulkhead	5	5	29-Apr-27	05-May-27
P2RP.1700	Phase 2 / Data Hall - Stud Framing (Equipment Platform)	5	5	05-May-27	11-May-27
P2RP.1720	Phase 2 / Data Hall - Above Ceiling Cable Tray	3	3	06-May-27	10-May-27
P2RP.1730	Phase 2 / Data Hall - Seismic Install	2	2	11-May-27	12-May-27
P2RP.1600	Phase 2 / Data Hall - OH Electric Rough In	5	5	12-May-27	18-May-27
P2RP.1100	Phase 2 / Data Hall - Wall Elec & FA Rough-In (IMP)	4	4	01-Jun-27	04-Jun-27
P2RP.1710	Phase 2 / Data Hall - Wall Elec & FA Rough-In (Data Hall / Elec Rm)	4	4	01-Jun-27	04-Jun-27
P2RP.1610	Phase 2 / Data Hall - In Wall Rough In Inspection (Electrical / FA)	1	1	07-Jun-27	07-Jun-27
P2RP.1350	Phase 2 / Data Hall - Hang Drywall & Finish (Data Hall / Elec Rm)	5	5	08-Jun-27	14-Jun-27
P2RP.1370	Phase 2 / Data Hall - Prime & First Coat Paint	3	3	15-Jun-27	17-Jun-27
P2RP.1050	Phase 2 / Data Hall - Fire Protection Drops	5	5	18-Jun-27	24-Jun-27
P2RP.1230	Phase 2 / Data Hall - Install Backdraft Dampers	5	5	18-Jun-27	24-Jun-27
P2RP.1020	Phase 2 / Data Hall - MARS Racking	7	7	23-Jun-27	01-Jul-27

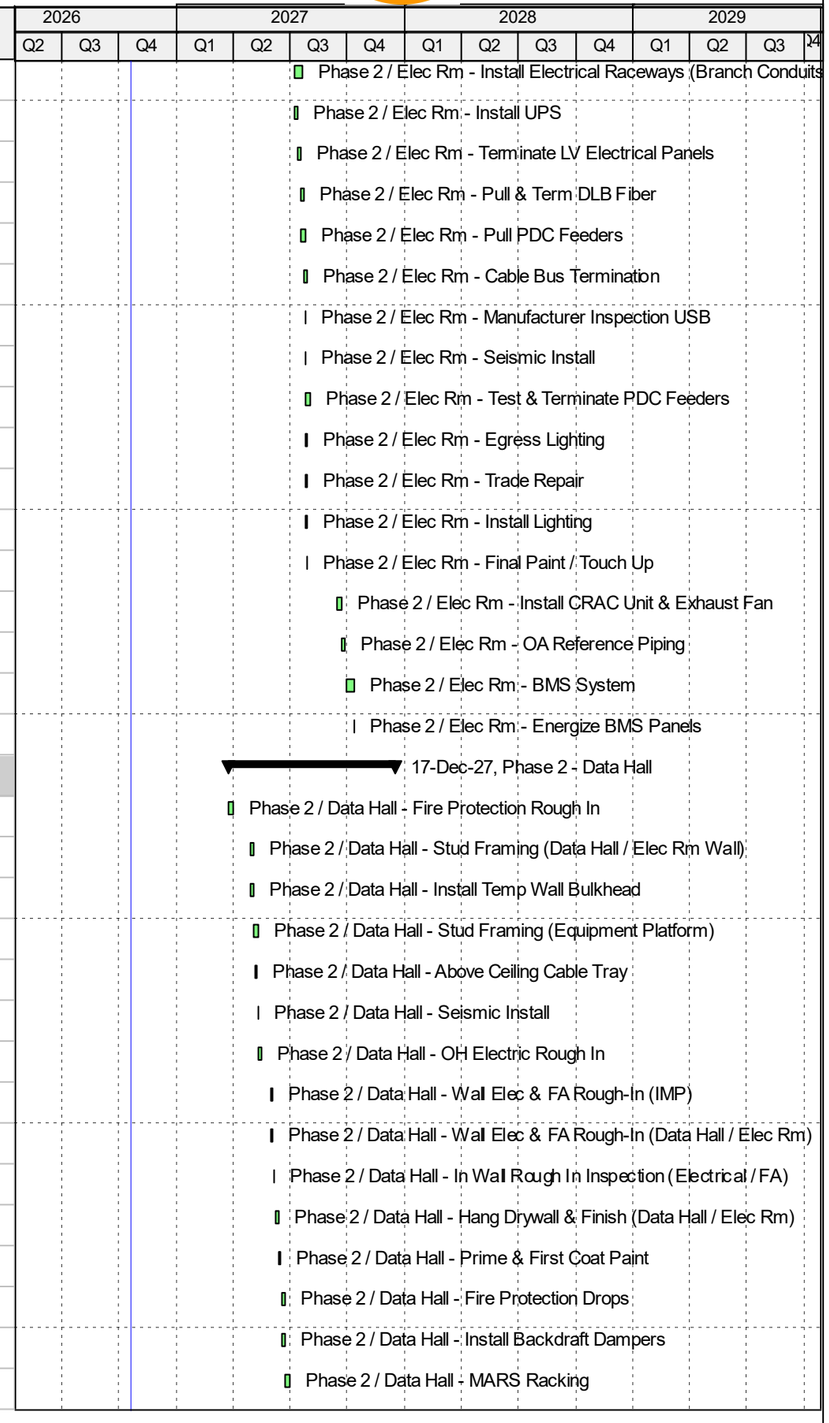


Gray

CMH139
Preliminary Schedule

aws


Activity ID	Activity Name	OD	RD	Start	Finish
P2RP.1200	Phase 2 / Data Hall - Temp Wall Install	5	5	02-Jul-27	09-Jul-27
P2RP.1060	Phase 2 / Data Hall - Upper Polycarbonate Panels and Cold Aisle Cable Tray Arms	3	3	02-Jul-27	07-Jul-27
P2RP.1220	Phase 2 / Data Hall - Install Lighting Wiring & Fixtures	5	5	02-Jul-27	09-Jul-27
P2RP.1420	Phase 2 / Data Hall - Power PDC Whips	10	10	02-Jul-27	16-Jul-27
P2RP.1440	Phase 2 / Data Hall - Install Control Dampers (PRD)	5	5	02-Jul-27	09-Jul-27
P2RP.1620	Phase 2 / Data Hall - ACT Grid Corridors	4	4	02-Jul-27	08-Jul-27
P2RP.1630	Phase 2 / Data Hall - Install Snubbers	5	5	02-Jul-27	09-Jul-27
P2RP.1030	Phase 2 / Data Hall - PDC Feeders Drops & Supports	10	10	02-Jul-27	16-Jul-27
P2RP.1210	Phase 2 / Data Hall - Fire Alarm VESDA	10	10	07-Jul-27	20-Jul-27
P2RP.1640	Phase 2 / Data Hall - ACT Grid Cold Aisles	5	5	07-Jul-27	13-Jul-27
P2RP.1260	Phase 2 / Data Hall - Perfect Position	4	4	08-Jul-27	13-Jul-27
P2RP.1250	Phase 2 / Data Hall - Doors and Hardware	2	2	12-Jul-27	13-Jul-27
P2RP.1650	Phase 2 / Data Hall - Install Control Wiring	5	5	12-Jul-27	16-Jul-27
P2RP.1280	Phase 2 / Data Hall - Install Fire Protection Heads Avenue	2	2	14-Jul-27	15-Jul-27
P2RP.1160	Phase 2 / Data Hall - Cold Aisle Basket/Cable Tray	3	3	14-Jul-27	16-Jul-27
P2RP.1400	Phase 2 / Data Hall - Avenue Basket/Cable Tray (South)	2	2	14-Jul-27	15-Jul-27
P2RP.1660	Phase 2 / Data Hall - ACT Borders For Corridors	1	1	14-Jul-27	14-Jul-27
P2RP.1740	Phase 2 / Data Hall - Install Fire Protection Heads Cold Aisle	2	2	14-Jul-27	15-Jul-27
P2RP.1670	Phase 2 / Data Hall - ACT Borders For Cold Aisles	1	1	15-Jul-27	15-Jul-27
P2RP.1290	Phase 2 / Data Hall - Avenue Basket/Cable Tray (North)	2	2	16-Jul-27	19-Jul-27
P2RP.1310	Phase 2 / Data Hall - Structural Overhead Inspection (Avenue)	1	1	16-Jul-27	16-Jul-27
P2RP.1690	Phase 2 / Data Hall - ACT Remaining Tile Drops Post Inspection	3	3	19-Jul-27	21-Jul-27
P2RP.1680	Phase 2 / Data Hall - Touch Up Paint	4	4	19-Jul-27	22-Jul-27
P2RP.1430	Phase 2 / Data Hall - CAT6 Cable Install	3	3	20-Jul-27	22-Jul-27
P2RP.1080	Phase 2 / Data Hall - Set PDC Cabinets	3	3	22-Jul-27	26-Jul-27
P2RP.1120	Phase 2 / Data Hall - EPMS	15	15	27-Jul-27	16-Aug-27
P2RP.1110	Phase 2 / Data Hall - BMS	15	15	27-Jul-27	16-Aug-27
P2RP.1270	Phase 2 / Data Hall - PDC Feeders Test & Terminate	10	10	27-Jul-27	09-Aug-27
P2RP.1180	Phase 2 / Data Hall - Lower Polycarbonate Panels	5	5	17-Aug-27	23-Aug-27
P2RP.1070	Phase 2 / Data Hall - NEA Finalization	33	33	12-Oct-27	29-Nov-27
P2RP.1090	Phase 2 / Data Hall - H2C Readiness Coordination	14	14	30-Nov-27	17-Dec-27
Phase 2 - TAHU Gallery		107	107	19-Mar-27	18-Aug-27
P2DG.1270	Phase 2 / TAHU - Fire Protection Rough In	5	5	19-Mar-27	25-Mar-27

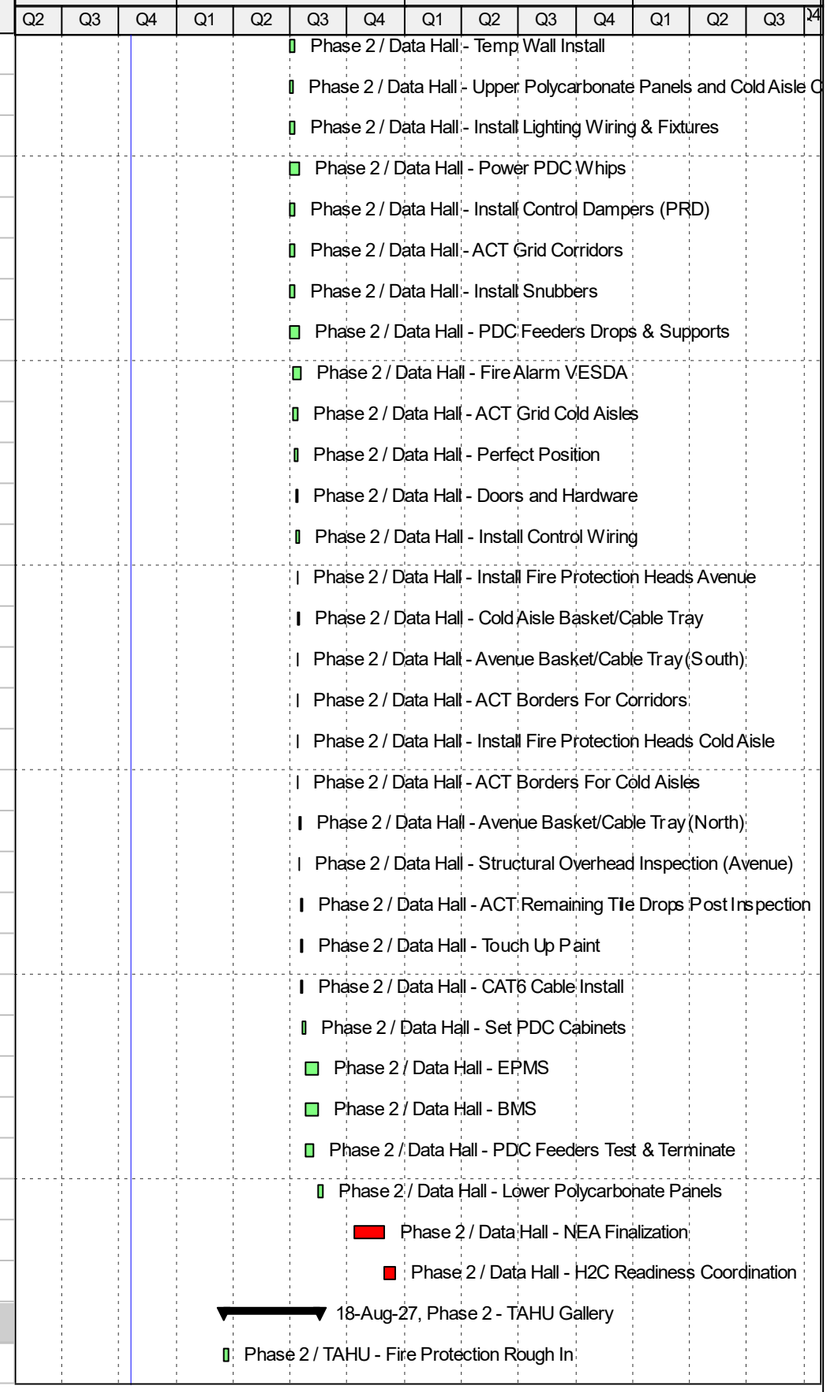

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

Run Date: 15-Oct-26 14:16
Data Date: 19-Oct-26

Activity ID	Activity Name	OD	RD	Start	Finish
P2DG.1200	Phase 2 / TAHU - Seismic Install	2	2	01-Jun-27	02-Jun-27
P2DG.1100	Phase 2 / TAHU - Sound Attenuator	10	10	01-Jun-27	14-Jun-27
P2DG.1250	Phase 2 / TAHU - Hang Outside Stairwell / Lobby Drywall	4	4	01-Jun-27	04-Jun-27
P2DG.1260	Phase 2 / TAHU - Install CFMF IMP Support	10	10	01-Jun-27	14-Jun-27
P2DG.1170	Phase 2 / TAHU - Install IMP Panels	6	6	15-Jun-27	22-Jun-27
P2DG.1050	Phase 2 / TAHU - Fire Alarm (VESDA)	5	5	23-Jun-27	29-Jun-27
P2DG.1080	Phase 2 / TAHU - Prime & Paint Drywall	3	3	23-Jun-27	25-Jun-27
P2DG.1010	Phase 2 / TAHU - BMS Controls Rough In	10	10	23-Jun-27	07-Jul-27
P2DG.1030	Phase 2 / TAHU - Wall Elec & Fire Alarm Rough-In	5	5	23-Jun-27	29-Jun-27
P2DG.1130	Phase 2 / TAHU - Control Dampers	5	5	28-Jun-27	02-Jul-27
P2DG.1110	Phase 2 / TAHU - Pull & Terminate Fire Alarm Cable	5	5	30-Jun-27	07-Jul-27
P2DG.1070	Phase 2 / TAHU - Set TAHUs	2	2	08-Jul-27	09-Jul-27
P2DG.1140	Phase 2 / TAHU - Doors and Hardware	3	3	12-Jul-27	14-Jul-27
P2DG.1150	Phase 2 / TAHU - Lighting	5	5	12-Jul-27	16-Jul-27
P2DG.1220	Phase 2 / TAHU - IW Supply Piping at TAHUs	10	10	12-Jul-27	23-Jul-27
P2DG.1180	Phase 2 / TAHU - TAHU Trim	10	10	12-Jul-27	23-Jul-27
P2DG.1190	Phase 2 / TAHU - Paint Doors & Frames	2	2	15-Jul-27	16-Jul-27
P2DG.1230	Phase 2 / TAHU - Tie In TAHUs	10	10	26-Jul-27	06-Aug-27
P2DG.1020	Phase 2 / TAHU - BMS Tie In	2	2	05-Aug-27	06-Aug-27
P2DG.1120	Phase 2 / TAHU - IW Drain Piping at TAHUs	5	5	09-Aug-27	13-Aug-27
P2DG.1240	Phase 2 / TAHU - Terminate Power To TAHUs	3	3	16-Aug-27	18-Aug-27
Phase 2 - Cx		176	176	28-Apr-27	07-Jan-28
P2CX.1110	Phase 2 / Cx - EC L2 Cx Review for MV Switchgear	1	1	28-Apr-27	28-Apr-27
P2CX.1080	Phase 2 / Cx - EC L2 Cx Review for MV XFMRs	1	1	29-Apr-27	29-Apr-27
P2CX.1090	Phase 2 / Cx - EC L3 Cx for MV XFMRs	5	5	30-Apr-27	06-May-27
P2CX.1370	Phase 2 / Cx - Eaton XFMR Testing	3	3	30-Apr-27	04-May-27
P2CX.1130	Phase 2 / Cx - EC L3 Cx for MV	3	3	05-May-27	07-May-27
P2CX.1120	Phase 2 / Cx - EC 3rd Party Testing & Inspection USB (L2)	3	3	22-Jun-27	24-Jun-27
P2CX.1200	Phase 2 / Cx - Fuel System Cx	7	7	02-Jul-27	13-Jul-27
P2CX.1160	Phase 2 / Cx - HUPPS Panelboards Energized	1	1	09-Jul-27	09-Jul-27
P2CX.1000	Phase 2 / Cx - EC 3rd Party LV Panelboard Testing (L2)	3	3	09-Jul-27	13-Jul-27
P2CX.1320	Phase 2 / Cx - AMCOP / BACOP Start Up & Cx	5	5	09-Jul-27	15-Jul-27
P2CX.1100	Phase 2 / Cx - Construction Power To Generator	3	3	12-Jul-27	14-Jul-27

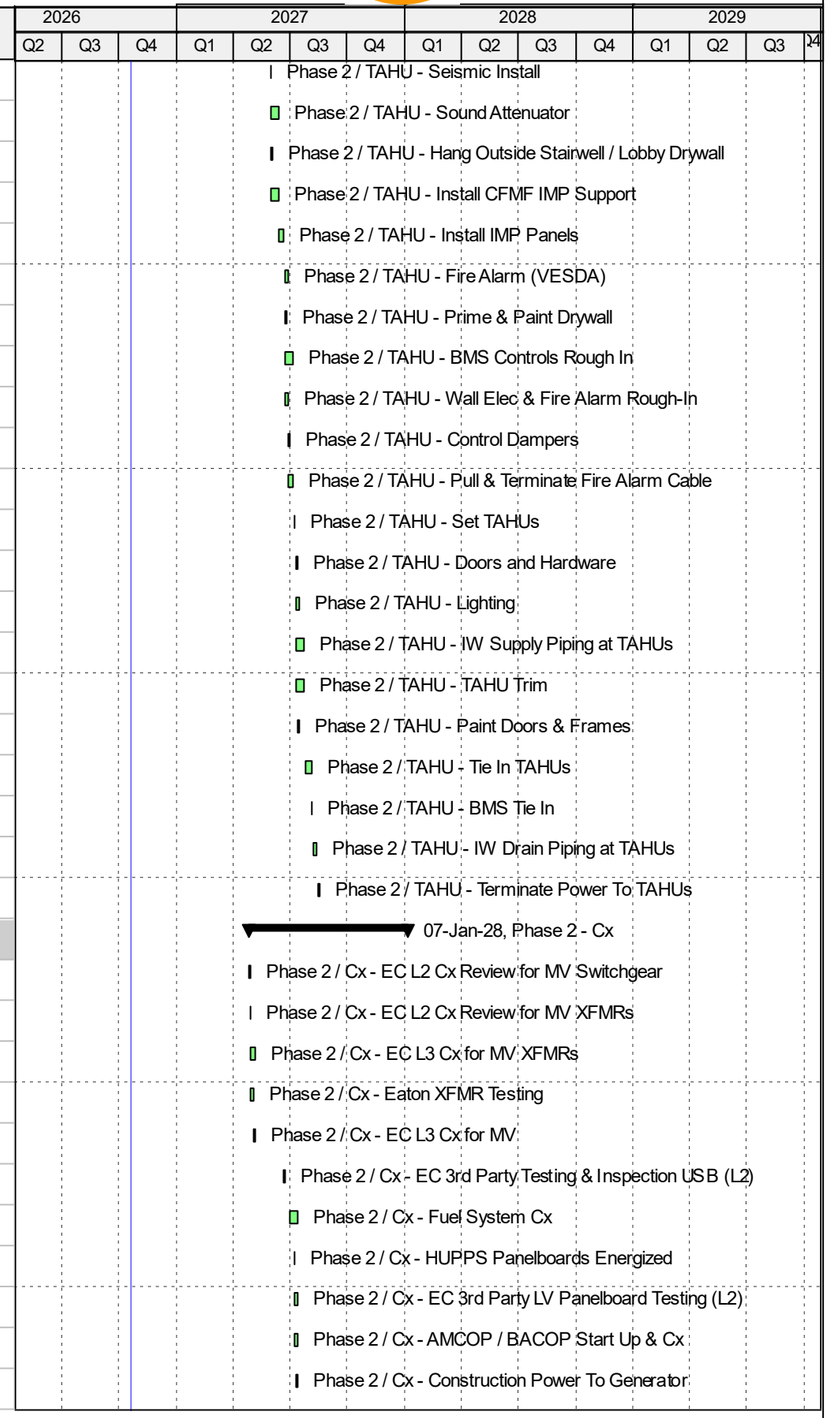


Gray


CMH139
Preliminary Schedule

aws

Activity ID	Activity Name	OD	RD	Start	Finish
P2CX.1380	Phase 2 / Cx - Energize Control Network Arch	1	1	12-Jul-27	12-Jul-27
P2CX.1020	Phase 2 / Cx - EC 3rd Party Busway Bus Plug Testing (L2)	2	2	13-Jul-27	14-Jul-27
P2CX.1340	Phase 2 / Cx - EPMS Point to Point (USB)	4	4	13-Jul-27	16-Jul-27
P2CX.1030	Phase 2 / Cx - CAT L2 Cx Generators	2	2	15-Jul-27	16-Jul-27
P2CX.2030	Phase 2 / Cx - Tie In MOP C1	2	2	15-Jul-27	16-Jul-27
P2CX.2040	Phase 2 / Cx - Tie In MOP C2	2	2	19-Jul-27	20-Jul-27
P2CX.1140	Phase 2 / Cx - EC 3rd Party Busway C1 / C2 Testing	2	2	21-Jul-27	22-Jul-27
P2CX.1190	Phase 2 / Cx - EC L2 Cx Review for LV Panelboard	2	2	21-Jul-27	22-Jul-27
P2CX.2010	Phase 2 / Cx - Fire Alarm Programming & Pretest	2	2	21-Jul-27	22-Jul-27
P2CX.1260	Phase 2 / Cx - EC L3 Cx LV Panelboard	1	1	23-Jul-27	23-Jul-27
P2CX.1170	Phase 2 / Cx - EC Busway C1 / C2 L2 Cx Review	1	1	23-Jul-27	23-Jul-27
P2CX.1220	Phase 2 / Cx - EC Busway C1 L3 Cx	2	2	26-Jul-27	27-Jul-27
P2CX.1010	Phase 2 / Cx - Eaton DLB Programming & Test (FLORES)	5	5	26-Jul-27	30-Jul-27
P2CX.2020	Phase 2 / Cx - EC Busway C2 L3 Cx	2	2	28-Jul-27	29-Jul-27
P2MS.180	Phase 2 / Cx - Life Safety Walkthrough	1	1	30-Jul-27	30-Jul-27
P2CX.1350	Phase 2 / Cx - EPMS Point to Point (PDC)	4	4	03-Aug-27	06-Aug-27
P2CX.1150	Phase 2 / Cx - EC L3 Cx USBs	2	2	06-Aug-27	09-Aug-27
P2CX.1250	Phase 2 / Cx - Vendor UPS Start Up & Cx	9	9	10-Aug-27	20-Aug-27
P2CX.1310	Phase 2 / Cx - ATS L3 Cx	1	1	10-Aug-27	10-Aug-27
P2CX.1180	Phase 2 / Cx - Eaton DLB Testing	2	2	10-Aug-27	11-Aug-27
P2CX.1390	Phase 2 / Cx - Energize MSDBs	1	1	11-Aug-27	11-Aug-27
P2CX.1290	Phase 2 / Cx - Split System Startup & Commissioning	10	10	12-Aug-27	25-Aug-27
P2CX.1280	Phase 2 / Cx - ERV Startup & Commissioning	10	10	12-Aug-27	25-Aug-27
P2CX.1270	Phase 2 / Cx - EDH Startup & Commissioning	4	4	12-Aug-27	17-Aug-27
P2CX.1300	Phase 2 / Cx - IW System L2 Cx	2	2	16-Aug-27	17-Aug-27
P2CX.1400	Phase 2 / Cx - IW System L3 Cx	10	10	18-Aug-27	31-Aug-27
P2CX.1210	Phase 2 / Cx - MC TAHU L2 Cx	5	5	19-Aug-27	25-Aug-27
P2CX.1040	Phase 2 / Cx - EC L2 Cx Review for Generator	1	1	27-Aug-27	27-Aug-27
P2CX.1070	Phase 2 / Cx - EC L3 Cx Generators	3	3	30-Aug-27	01-Sep-27
P2CX.1060	Phase 2 / Cx - CAT L3 Cx Generators Testing	5	5	30-Aug-27	03-Sep-27
P2CX.1240	Phase 2 / Cx - Vendor TAHU L3 Cx	10	10	01-Sep-27	15-Sep-27
P2CX.1330	Phase 2 / Cx - Test & Balance	5	5	16-Sep-27	22-Sep-27
P2CX.1360	Phase 2 / Cx - BMS Point to Point (TAHUs)	5	5	13-Oct-27	19-Oct-27

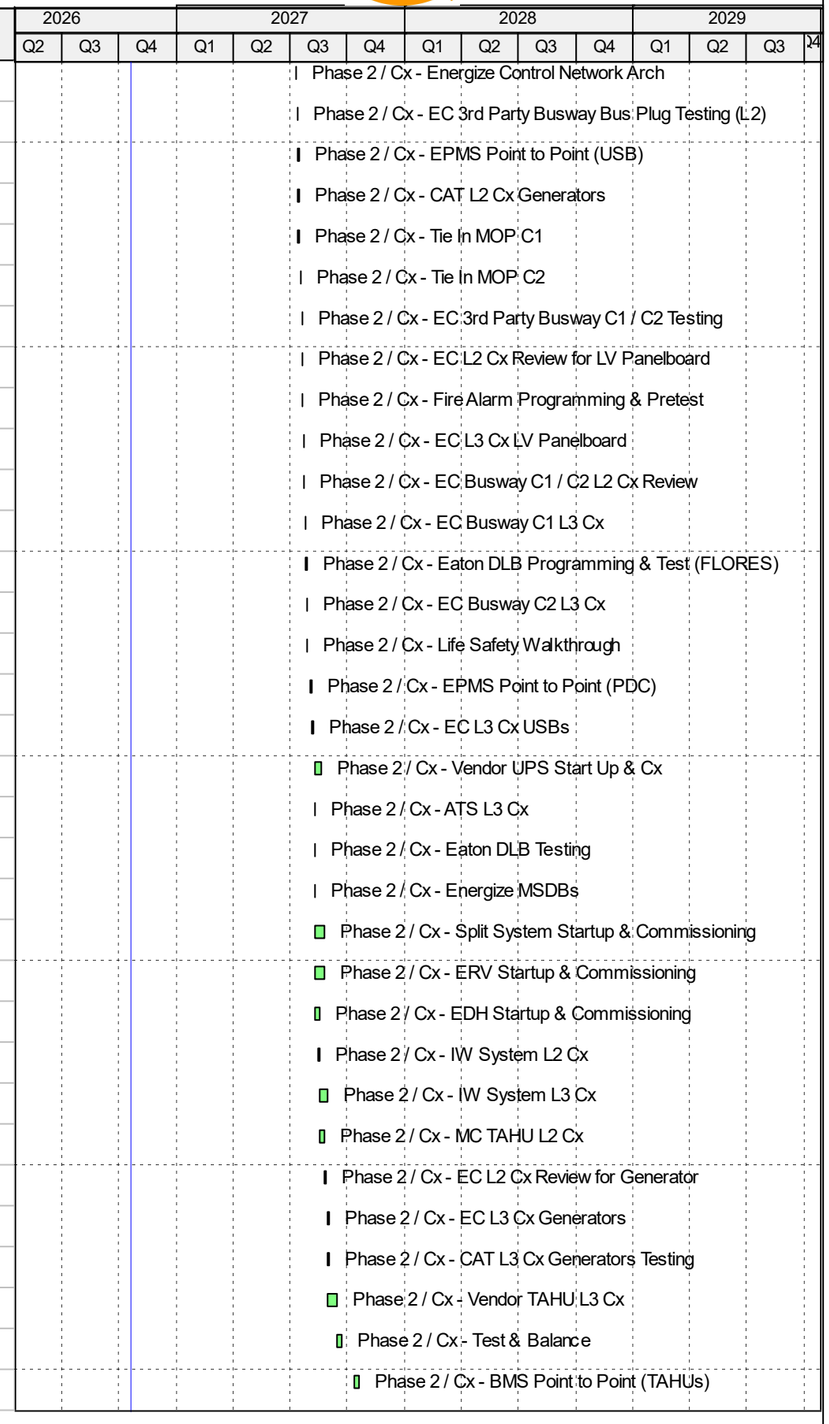


Activity ID	Activity Name	OD	RD	Start	Finish
P2CX.1230	Phase 2 / Cx - L4 / L5 Cx	13	13	20-Dec-27	07-Jan-28
Phase 3 (ROMP05 & 07)		222	222	23-Mar-27	04-Feb-28
Phase 3 - Gen Yard		92	92	19-Apr-27	26-Aug-27
P5EX.1030	Phase 3 / Gen Yard - Set Transformers	2	2	19-Apr-27	20-Apr-27
P5EX.1050	Phase 3 / Gen Yard - Pull, Term & Test MV through XFMRs	7	7	21-Apr-27	29-Apr-27
P5EX.1100	Phase 3 / Gen Yard - Pull In FLORES Loop	5	5	30-Apr-27	06-May-27
P5EX.1370	Phase 3 / Gen Yard - Install Fuel Piping	30	30	20-May-27	01-Jul-27
P5EX.1380	Phase 3 / Gen Yard - Install Fuel System Control Conduit	10	10	04-Jun-27	17-Jun-27
P5EX.1120	Phase 3 / Gen Yard - Pour Sidewalk	5	5	18-Jun-27	24-Jun-27
P5EX.1060	Phase 3 / Gen Yard - Set Generators	2	2	15-Jul-27	16-Jul-27
P5EX.1040	Phase 3 / Gen Yard - Install Cable Bus Structure	5	5	16-Jul-27	22-Jul-27
P5EX.1090	Phase 3 / Gen Yard - Set Exhaust Stack and Shroud	12	12	19-Jul-27	03-Aug-27
P5EX.1070	Phase 3 / Gen Yard - LV Cable Bus and Feeders - XFMRs to USBs	10	10	23-Jul-27	05-Aug-27
P5EX.1140	Phase 3 / Gen Yard - Grounding / Lightning Protection	2	2	04-Aug-27	05-Aug-27
P5EX.1110	Phase 3 / Gen Yard - Energize Electrical - Site To Phase	0	0		05-Aug-27
P4EX.1190	Phase 3 / Gen Yard - LV Cable Bus and Feeders - Gens to USBs	15	15	06-Aug-27	26-Aug-27
P5EX.1080	Phase 3 / Gen Yard - Install Generator Platforms	5	5	16-Aug-27	20-Aug-27
P5EX.1130	Phase 3 / Gen Yard - Install Foundations & Fencing	4	4	23-Aug-27	26-Aug-27
Phase 3 - Electrical Room		125	125	19-Apr-27	13-Oct-27
P5ER.1590	Phase 3 / Elec Rm - Layout	1	1	19-Apr-27	19-Apr-27
P5ER.1820	Phase 3 / Elec Rm - Install DriClad	10	10	20-Apr-27	03-May-27
P5ER.1000	Phase 3 / Elec Rm - Pull TAHU Feeders	5	5	29-Apr-27	05-May-27
P5ER.1040	Phase 3 / Elec Rm - Wall Electric & Fire Alarm Rough-in	5	5	04-May-27	10-May-27
P5ER.1020	Phase 3 / Elec Rm - Stud Framing	4	4	05-May-27	10-May-27
P5ER.1010	Phase 3 / Elec Rm - Pull Lighting Control Wiring	7	7	06-May-27	14-May-27
P5ER.1380	Phase 3 / Elec Rm - Hangers	3	3	11-May-27	13-May-27
P5ER.1610	Phase 3 / Elec Rm - Install OH Conduit / Mechanical Feeders	5	5	14-May-27	20-May-27
P5ER.1060	Phase 3 / Elec Rm - Hang Drywall & Finish	5	5	01-Jun-27	07-Jun-27
P5ER.1600	Phase 3 / Elec Rm - Fire Protection Rough In	3	3	04-Jun-27	08-Jun-27
P5ER.1080	Phase 3 / Elec Rm - Prime & First Coat Paint	1	1	08-Jun-27	08-Jun-27
P5ER.1120	Phase 3 / Elec Rm - Install Split Systems & ERV	10	10	09-Jun-27	22-Jun-27
P5ER.1800	Phase 3 / Elec Rm - Pull / Term HUPPs	2	2	09-Jun-27	10-Jun-27
P5ER.1620	Phase 3 / Elec Rm - Set USB (LV Gear)	5	5	13-Jul-27	19-Jul-27

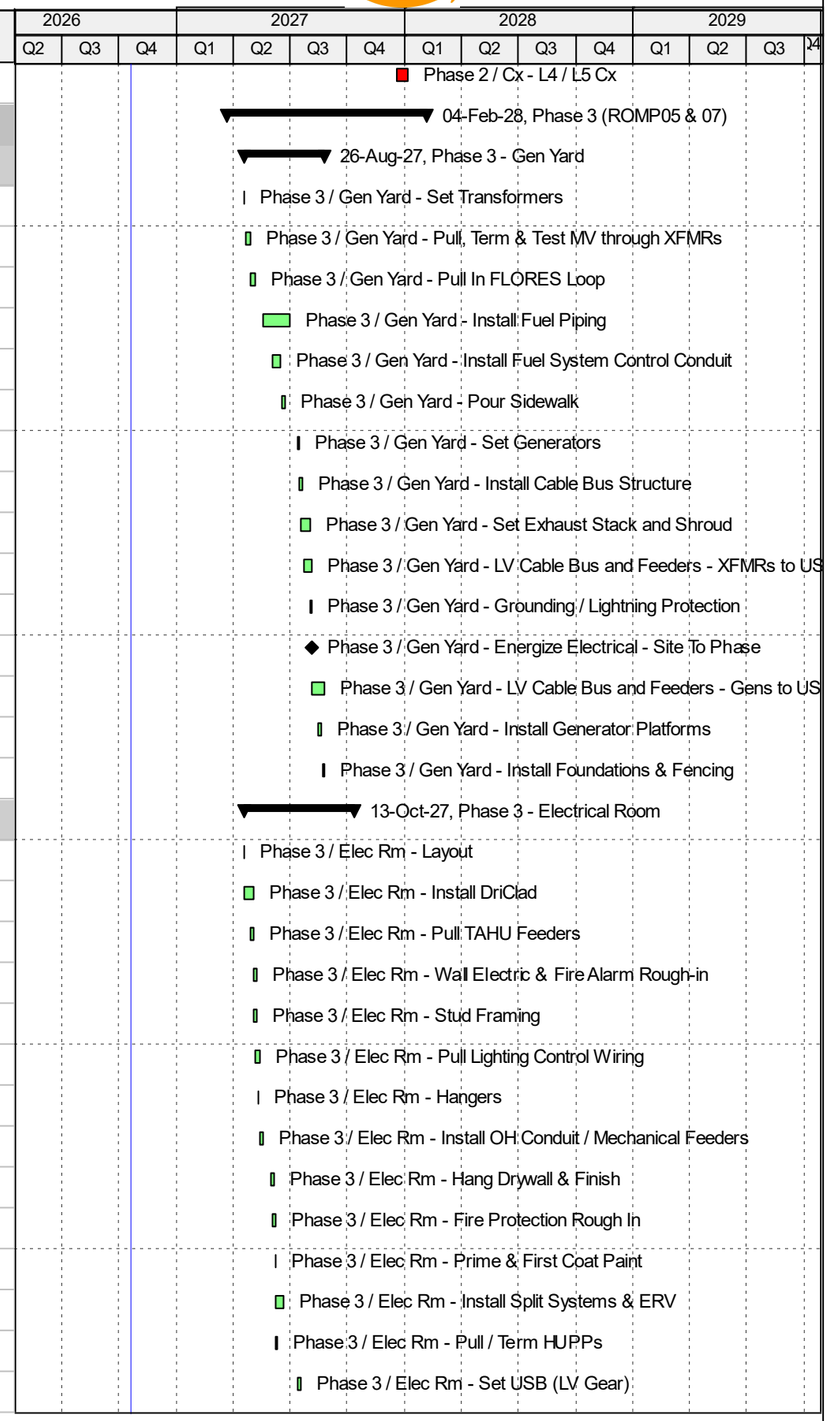

CMH139
Preliminary Schedule

Activity ID	Activity Name	OD	RD	Start	Finish
P5ER.1140	Phase 3 / Elec Rm - Install AMCOP Panels	1	1	20-Jul-27	20-Jul-27
P5ER.1640	Phase 3 / Elec Rm - Doors & Hardware	5	5	20-Jul-27	26-Jul-27
P5ER.1650	Phase 3 / Elec Rm - Breaker Testing USB	5	5	20-Jul-27	26-Jul-27
P5ER.1630	Phase 3 / Elec Rm - Fill Buck Out	4	4	20-Jul-27	23-Jul-27
P5ER.1660	Phase 3 / Elec Rm - Install Cable Tray	7	7	20-Jul-27	28-Jul-27
P5ER.1670	Phase 3 / Elec Rm - Cable Bus Termination	4	4	23-Jul-27	28-Jul-27
P5ER.1210	Phase 3 / Elec Rm - Set SCCS Setting for Breakers	1	1	27-Jul-27	27-Jul-27
P5ER.1110	Phase 3 / Elec Rm - Set OFCI Electrical Panels	5	5	29-Jul-27	04-Aug-27
P5ER.1680	Phase 3 / Elec Rm - Fire Alarm / VESDA	5	5	29-Jul-27	04-Aug-27
P5ER.1700	Phase 3 / Elec Rm - Install Bus Duct	7	7	29-Jul-27	06-Aug-27
P5ER.1810	Phase 3 / Elec Rm - Install Control Conduit	5	5	29-Jul-27	04-Aug-27
P5ER.1330	Phase 3 / Elec Rm - Pull & Term DLB Fiber	5	5	05-Aug-27	11-Aug-27
P5ER.1710	Phase 3 / Elec Rm - Install Electrical Raceways (Branch Conduits)	10	10	05-Aug-27	18-Aug-27
P3ER.1820	Phase 3 / Elec Rm - Install UPS	4	4	05-Aug-27	10-Aug-27
P5ER.1150	Phase 3 / Elec Rm - Pull PDC Feeders	5	5	06-Aug-27	12-Aug-27
P5ER.1160	Phase 3 / Elec Rm - Terminate LV Electrical Panels	5	5	10-Aug-27	16-Aug-27
P5ER.1730	Phase 3 / Elec Rm - Manufacturer Inspection USB	1	1	12-Aug-27	12-Aug-27
P5ER.1220	Phase 3 / Elec Rm - Install Lighting	3	3	13-Aug-27	17-Aug-27
P5ER.1750	Phase 3 / Elec Rm - Seismic Install	1	1	13-Aug-27	13-Aug-27
P5ER.1780	Phase 3 / Elec Rm - Test & Terminate PDC Feeders	5	5	13-Aug-27	19-Aug-27
P5ER.1760	Phase 3 / Elec Rm - Egress Lighting	3	3	13-Aug-27	17-Aug-27
P5ER.1770	Phase 3 / Elec Rm - Trade Repair	3	3	19-Aug-27	23-Aug-27
P5ER.1790	Phase 3 / Elec Rm - Final Paint / Touch Up	1	1	24-Aug-27	24-Aug-27
P5ER.1690	Phase 3 / Elec Rm - Install CRAC Unit & Exhaust Fan	5	5	15-Sep-27	21-Sep-27
P5ER.1720	Phase 3 / Elec Rm - OA Reference Piping	5	5	22-Sep-27	28-Sep-27
P5ER.1180	Phase 3 / Elec Rm - BMS System	10	10	29-Sep-27	12-Oct-27
P5ER.1740	Phase 3 / Elec Rm - Energize BMS Panels	1	1	13-Oct-27	13-Oct-27
Phase 3 - Data Hall		202	202	30-Mar-27	14-Jan-28
P3RP.1730	Phase 3 / Data Hall - Fire Protection Rough In	5	5	30-Mar-27	05-Apr-27
P5RP.1040	Phase 3 / Data Hall - Stud Framing (Data Hall / Elec Rm Wall)	5	5	05-May-27	11-May-27
P3RP.1590	Phase 3 / Data Hall - Install Temp Wall Bulkhead	5	5	06-May-27	12-May-27
P5RP.1700	Phase 3 / Data Hall - Stud Framing (Equipment Platform)	5	5	11-May-27	17-May-27
P3RP.1700	Phase 3 / Data Hall - Above Ceiling Cable Tray	3	3	13-May-27	17-May-27

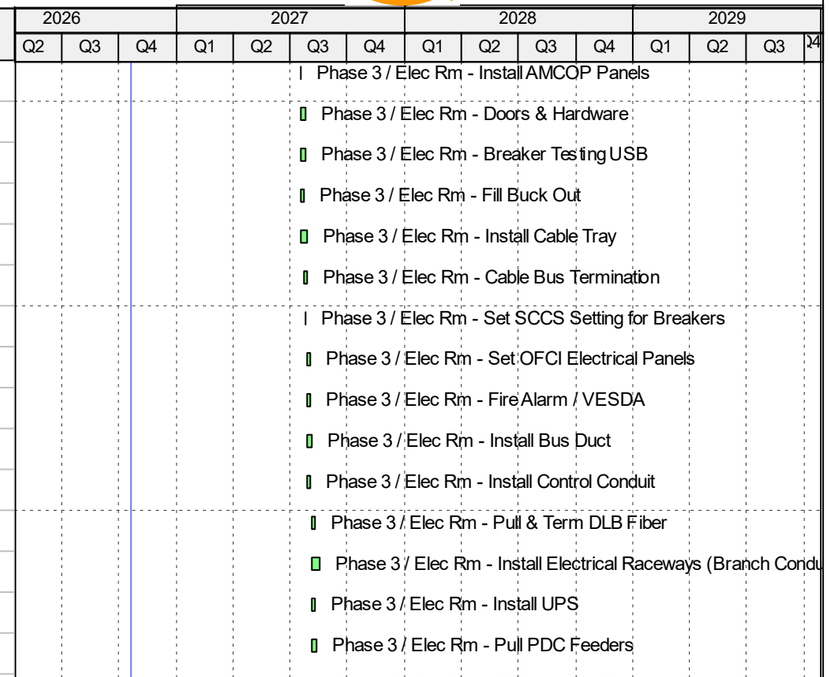


Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

Run Date: 15-Oct-26 14:16
Data Date: 19-Oct-26

CMH139
Preliminary Schedule


Activity ID	Activity Name	OD	RD	Start	Finish
P3RP.1600	Phase 3 / Data Hall - OH Electric Rough In	5	5	18-May-27	24-May-27
P3RP.1710	Phase 3 / Data Hall - Seismic Install	2	2	18-May-27	19-May-27
P5RP.1100	Phase 3 / Data Hall - Wall Elec & FA Rough-In (IMP)	4	4	01-Jun-27	04-Jun-27
P5RP.1710	Phase 3 / Data Hall - Wall Elec & FA Rough-In (Data Hall / Elec Rm)	4	4	01-Jun-27	04-Jun-27
P3RP.1610	Phase 3 / Data Hall - In Wall Rough In Inspection (Electrical / FA)	1	1	07-Jun-27	07-Jun-27
P5RP.1130	Phase 3 / Data Hall - Hang Drywall & Finish (Data Hall / Elec Rm)	5	5	08-Jun-27	14-Jun-27
P5RP.1190	Phase 3 / Data Hall - Prime & First Coat Paint	3	3	15-Jun-27	17-Jun-27
P5RP.1050	Phase 3 / Data Hall - Fire Protection Drops	5	5	18-Jun-27	24-Jun-27
P5RP.1350	Phase 3 / Data Hall - Install Backdraft Dampers	5	5	18-Jun-27	24-Jun-27
P5RP.1020	Phase 3 / Data Hall - MARS Racking	7	7	13-Jul-27	21-Jul-27
P5RP.1070	Phase 3 / Data Hall - Install Lighting Wiring & Fixtures	5	5	22-Jul-27	28-Jul-27
P5RP.1200	Phase 3 / Data Hall - Temp Wall Install	5	5	22-Jul-27	28-Jul-27
P5RP.1060	Phase 3 / Data Hall - Upper Polycarbonate Panels and Cold Aisle Cable Tray Arms	3	3	22-Jul-27	26-Jul-27
P5RP.1230	Phase 3 / Data Hall - Install Control Dampers (PRD)	5	5	22-Jul-27	28-Jul-27
P5RP.1410	Phase 3 / Data Hall - Power PDC Whips	10	10	22-Jul-27	04-Aug-27
P3RP.1620	Phase 3 / Data Hall - ACT Grid Corridors	4	4	22-Jul-27	27-Jul-27
P3RP.1630	Phase 3 / Data Hall - Install Snubbers	5	5	22-Jul-27	28-Jul-27
P5RP.1030	Phase 3 / Data Hall - PDC Feeders Drops & Supports	10	10	22-Jul-27	04-Aug-27
P5RP.1210	Phase 3 / Data Hall - Fire Alarm VESDA	10	10	26-Jul-27	06-Aug-27
P3RP.1640	Phase 3 / Data Hall - ACT Grid Cold Aisles	5	5	26-Jul-27	30-Jul-27
P5RP.1340	Phase 3 / Data Hall - Perfect Position	4	4	27-Jul-27	30-Jul-27
P5RP.1250	Phase 3 / Data Hall - Doors and Hardware	2	2	29-Jul-27	30-Jul-27
P3RP.1650	Phase 3 / Data Hall - Install Control Wiring	5	5	29-Jul-27	04-Aug-27
P5RP.1280	Phase 3 / Data Hall - Install Fire Protection Heads Avenue	2	2	02-Aug-27	03-Aug-27
P5RP.1160	Phase 3 / Data Hall - Cold Aisle Basket/Cable Tray	3	3	02-Aug-27	04-Aug-27
P5RP.1360	Phase 3 / Data Hall - Avenue Basket/Cable Tray (South)	2	2	02-Aug-27	03-Aug-27
P3RP.1660	Phase 3 / Data Hall - ACT Borders For Corridors	1	1	02-Aug-27	02-Aug-27
P3RP.1720	Phase 3 / Data Hall - Install Fire Protection Heads Cold Aisle	2	2	02-Aug-27	03-Aug-27
P3RP.1670	Phase 3 / Data Hall - ACT Borders For Cold Aisles	1	1	03-Aug-27	03-Aug-27
P5RP.1290	Phase 3 / Data Hall - Avenue Basket/Cable Tray (North)	2	2	04-Aug-27	05-Aug-27
P5RP.1310	Phase 3 / Data Hall - Structural Overhead Inspection (Avenue)	1	1	04-Aug-27	04-Aug-27
P3RP.1690	Phase 3 / Data Hall - ACT Remaining Tile Drops Post Inspection	3	3	05-Aug-27	09-Aug-27
P3RP.1680	Phase 3 / Data Hall - Touch Up Paint	4	4	05-Aug-27	10-Aug-27

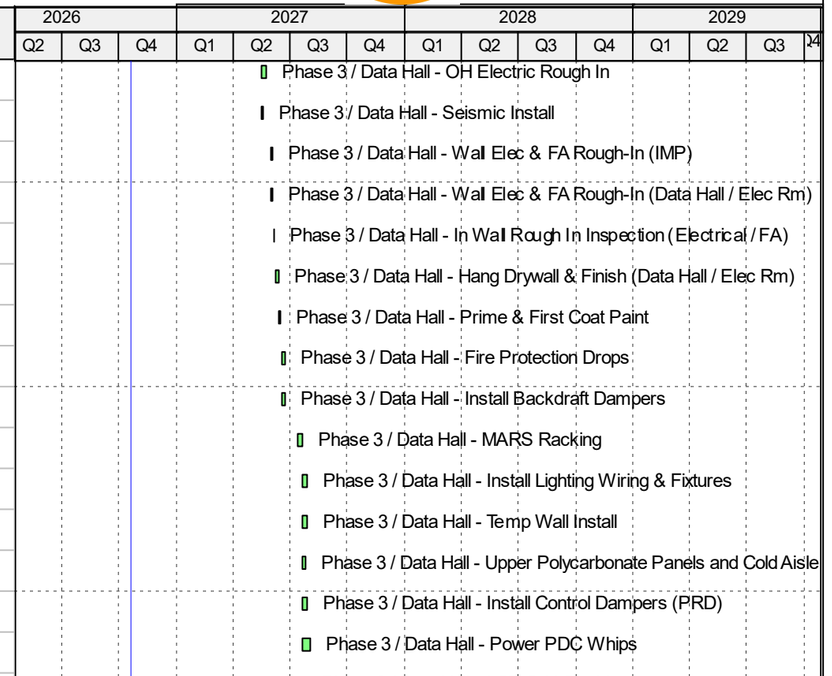

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

Run Date: 15-Oct-26 14:16
Data Date: 19-Oct-26

Activity ID	Activity Name	OD	RD	Start	Finish
P5RP.1420	Phase 3 / Data Hall - CAT6 Cable Install	3	3	06-Aug-27	10-Aug-27
P5RP.1080	Phase 3 / Data Hall - Set PDC Cabinets	3	3	10-Aug-27	12-Aug-27
P5RP.1110	Phase 3 / Data Hall - BMS	15	15	13-Aug-27	02-Sep-27
P5RP.1270	Phase 3 / Data Hall - PDC Feeders Test & Terminate	10	10	13-Aug-27	26-Aug-27
P5RP.1430	Phase 3 / Data Hall - EPMS	15	15	13-Aug-27	02-Sep-27
P5RP.1180	Phase 3 / Data Hall - Lower Polycarbonate Panels	5	5	03-Sep-27	10-Sep-27
P5RP.1090	Phase 3 / Data Hall - NEA Finalization	19	19	30-Nov-27	27-Dec-27
P5RP.1140	Phase 3 / Data Hall - H2C Readiness Coordination	13	13	28-Dec-27	14-Jan-28
Phase 3 - TAHU Gallery		108	108	23-Mar-27	23-Aug-27
P5DG.1230	Phase 3 / TAHU - Fire Protection Rough In	5	5	23-Mar-27	29-Mar-27
P5DG.1170	Phase 3 / TAHU - Sound Attenuator	10	10	01-Jun-27	14-Jun-27
P5DG.1180	Phase 3 / TAHU - Seismic Install	2	2	01-Jun-27	02-Jun-27
P5DG.1190	Phase 3 / TAHU - Hang Outside Stairwell / Lobby Drywall	4	4	01-Jun-27	04-Jun-27
P5DG.1200	Phase 3 / TAHU - Install CFMF IMP Support	10	10	01-Jun-27	14-Jun-27
P5DG.1040	Phase 3 / TAHU - Install IMP Panels	6	6	15-Jun-27	22-Jun-27
P5DG.1080	Phase 3 / TAHU - Prime & Paint Drywall	3	3	23-Jun-27	25-Jun-27
P5DG.1010	Phase 3 / TAHU - BMS Controls Rough In	10	10	23-Jun-27	07-Jul-27
P5DG.1030	Phase 3 / TAHU - Wall Elec & Fire Alarm Rough-In	5	5	23-Jun-27	29-Jun-27
P5DG.1130	Phase 3 / TAHU - Fire Alarm (VESDA)	5	5	23-Jun-27	29-Jun-27
P5DG.1090	Phase 3 / TAHU - Control Dampers	5	5	28-Jun-27	02-Jul-27
P5DG.1050	Phase 3 / TAHU - Pull & Terminate Fire Alarm Cable	5	5	30-Jun-27	07-Jul-27
P5DG.1070	Phase 3 / TAHU - Set TAHUs	2	2	13-Jul-27	14-Jul-27
P5DG.1140	Phase 3 / TAHU - Doors and Hardware	3	3	15-Jul-27	19-Jul-27
P5DG.1060	Phase 3 / TAHU - IW Supply Piping at TAHUs	10	10	15-Jul-27	28-Jul-27
P5DG.1110	Phase 3 / TAHU - TAHU Trim	10	10	15-Jul-27	28-Jul-27
P5DG.1210	Phase 3 / TAHU - Paint Doors & Frames	2	2	20-Jul-27	21-Jul-27
P5DG.1150	Phase 3 / TAHU - Lighting	5	5	29-Jul-27	04-Aug-27
P5DG.1100	Phase 3 / TAHU - Tie In TAHUs	10	10	29-Jul-27	11-Aug-27
P5DG.1020	Phase 3 / TAHU - BMS Tie In	2	2	10-Aug-27	11-Aug-27
P5DG.1120	Phase 3 / TAHU - IW Drain Piping at TAHUs	5	5	12-Aug-27	18-Aug-27
P5DG.1220	Phase 3 / TAHU - Terminate Power To TAHUs	3	3	19-Aug-27	23-Aug-27
Phase 3 - Cx		194	194	30-Apr-27	04-Feb-28
P5CX.1100	Phase 3 / Cx - EC L2 Cx Review for MV Switchgear	1	1	30-Apr-27	30-Apr-27

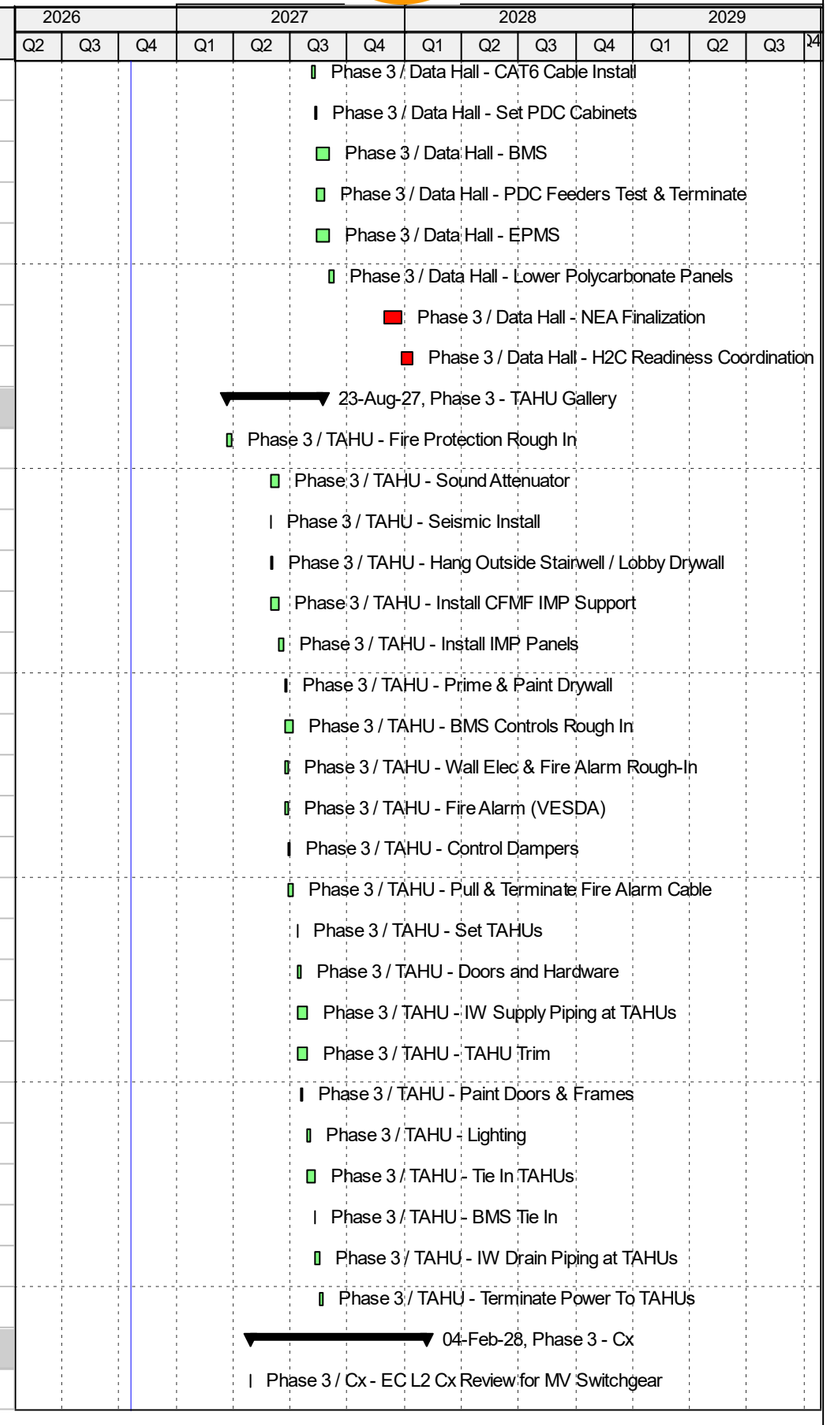


Gray


CMH139
Preliminary Schedule

aws

Activity ID	Activity Name	OD	RD	Start	Finish
P5CX.1080	Phase 3 / Cx - EC L2 Cx Review for MV XFMRs	1	1	03-May-27	03-May-27
P5CX.1090	Phase 3 / Cx - EC L3 Cx for MV XFMRs	5	5	04-May-27	10-May-27
P5CX.1350	Phase 3 / Cx - Eaton XFMR Testing	3	3	04-May-27	06-May-27
P5CX.1130	Phase 3 / Cx - EC L3 Cx for MV	3	3	07-May-27	11-May-27
P5CX.1200	Phase 3 / Cx - Fuel System Cx	7	7	02-Jul-27	13-Jul-27
P5CX.1180	Phase 3 / Cx - Construction Power To Generator	3	3	19-Jul-27	21-Jul-27
P5CX.1120	Phase 3 / Cx - EC 3rd Party Testing & Inspection USB (L2)	3	3	20-Jul-27	22-Jul-27
P5CX.1030	Phase 3 / Cx - CAT L2 Cx Generators	2	2	22-Jul-27	23-Jul-27
P5CX.1160	Phase 3 / Cx - HUPPS Panelboards Energized	1	1	05-Aug-27	05-Aug-27
P5CX.1000	Phase 3 / Cx - EC 3rd Party LV Panelboard Testing (L2)	3	3	05-Aug-27	09-Aug-27
P5CX.1320	Phase 3 / Cx - AMCOP / BACOP Start Up & Cx	5	5	05-Aug-27	11-Aug-27
P5CX.1360	Phase 3 / Cx - Energize Control Network Arch	1	1	06-Aug-27	06-Aug-27
P5CX.1390	Phase 3 / Cx - EPMS Point to Point (USB)	4	4	09-Aug-27	12-Aug-27
P5CX.1470	Phase 3 / Cx - Fire Alarm Programming & Pretest	2	2	09-Aug-27	10-Aug-27
P5CX.1230	Phase 3 / Cx - EC 3rd Party Busway Bus Plug Testing (L2)	2	2	09-Aug-27	10-Aug-27
P5MCM.5010	Phase 3 / Cx - Tie in MOP C1	2	2	11-Aug-27	12-Aug-27
P5MCM.5020	Phase 3 / Cx - Eaton DLB Programming & Test (FLORES)	5	5	12-Aug-27	18-Aug-27
P5MCM.5050	Phase 3 / Cx - Tie in MOP C2	2	2	13-Aug-27	16-Aug-27
P5CX.1140	Phase 3 / Cx - EC 3rd Party Busway C1 / C2 Testing	2	2	17-Aug-27	18-Aug-27
P5CX.1190	Phase 3 / Cx - EC L2 Cx Review for LV Panelboard	2	2	17-Aug-27	18-Aug-27
P5MS.180	Phase 3 / Cx - Life Safety Walkthrough	1	1	18-Aug-27	18-Aug-27
P5CX.1260	Phase 3 / Cx - EC L3 Cx LV Panelboard	1	1	19-Aug-27	19-Aug-27
P5CX.1170	Phase 3 / Cx - EC Busway C1 / C2 L2 Cx Review	1	1	19-Aug-27	19-Aug-27
P5CX.1220	Phase 3 / Cx - EC Busway C1 L3 Cx	2	2	20-Aug-27	23-Aug-27
P5CX.1380	Phase 3 / Cx - EPMS Point to Point (PDC)	4	4	20-Aug-27	25-Aug-27
P5CX.1210	Phase 3 / Cx - MC TAHU L2 Cx	5	5	24-Aug-27	30-Aug-27
P5CX.1480	Phase 3 / Cx - EC Busway C2 L3 Cx	2	2	24-Aug-27	25-Aug-27
P5CX.1150	Phase 3 / Cx - EC L3 Cx USBs	2	2	26-Aug-27	27-Aug-27
P5CX.1040	Phase 3 / Cx - EC L2 Cx Review for Generator	1	1	27-Aug-27	27-Aug-27
P5CX.1070	Phase 3 / Cx - EC L3 Cx Generators	3	3	30-Aug-27	01-Sep-27
P5CX.1060	Phase 3 / Cx - CAT L3 Cx Generators Testing	5	5	30-Aug-27	03-Sep-27
P5CX.1250	Phase 3 / Cx - Vendor UPS Start Up & Cx	9	9	30-Aug-27	10-Sep-27
P5CX.1310	Phase 3 / Cx - ATS L3 Cx	1	1	30-Aug-27	30-Aug-27

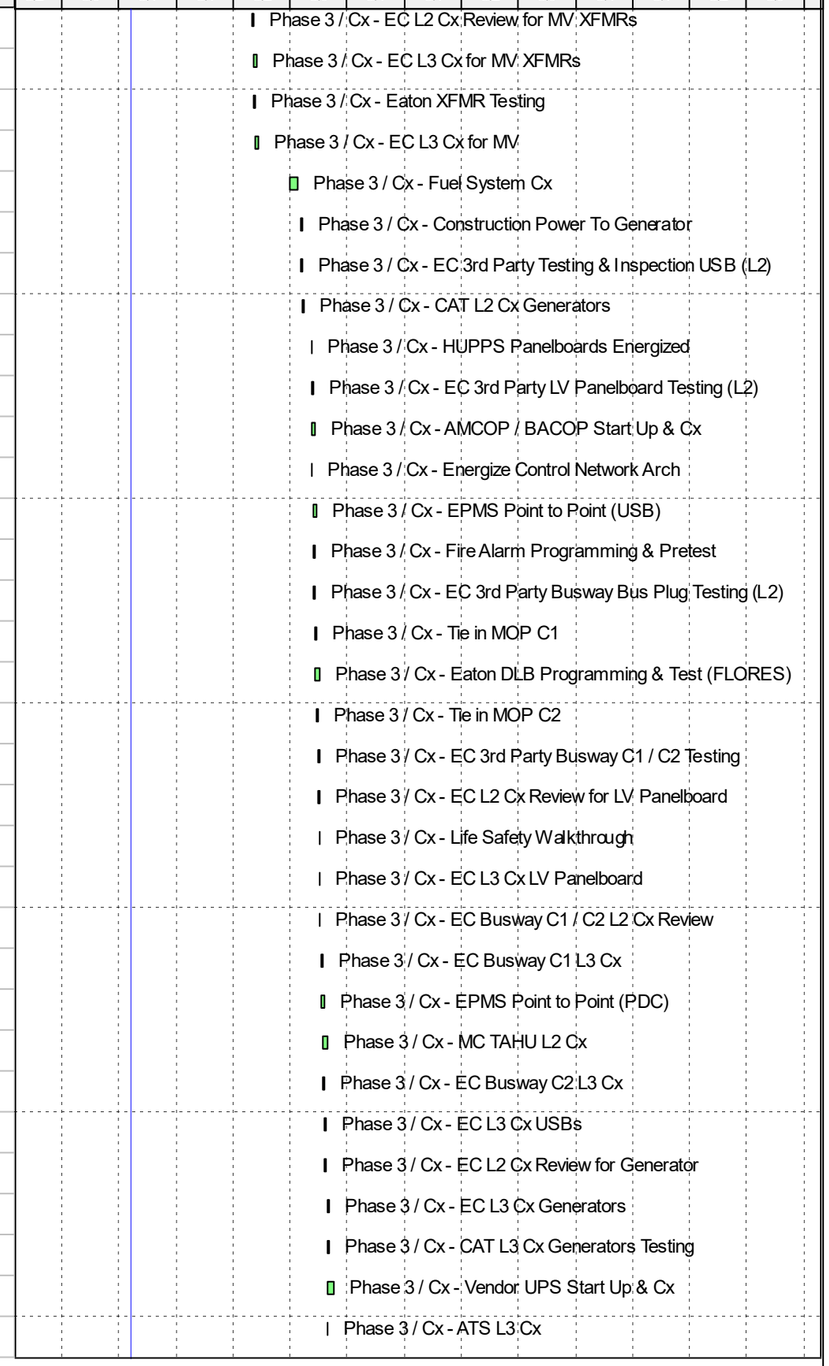

Activity ID	Activity Name	OD	RD	Start	Finish
P5CX.1420	Phase 3 / Cx - Eaton DLB Testing	2	2	30-Aug-27	31-Aug-27
P5CX.1400	Phase 3 / Cx - Energize MSDBs	1	1	31-Aug-27	31-Aug-27
P5CX.1290	Phase 3 / Cx - Split System Startup & Commissioning	10	10	01-Sep-27	15-Sep-27
P5CX.1280	Phase 3 / Cx - ERV Startup & Commissioning	10	10	01-Sep-27	15-Sep-27
P5CX.1270	Phase 3 / Cx - EDH Startup & Commissioning	4	4	01-Sep-27	07-Sep-27
P5MCM.5030	Phase 3 / Cx - IW System L2 Cx	2	2	01-Sep-27	02-Sep-27
P5MCM.5040	Phase 3 / Cx - IW System L3 Cx	10	10	03-Sep-27	17-Sep-27
P5CX.1240	Phase 3 / Cx - Vendor TAHU L3 Cx	10	10	20-Sep-27	01-Oct-27
P5CX.1330	Phase 3 / Cx - Test & Balance	5	5	04-Oct-27	08-Oct-27
P5CX.1370	Phase 3 / Cx - BMS Point to Point (TAHUs)	5	5	13-Oct-27	19-Oct-27
P5CX.1430	Phase 3 / Cx - L4 / L5 Cx	15	15	17-Jan-28	04-Feb-28
Phase 4 (ROMP06 & 08)		221	221	21-Apr-27	03-Mar-28
Phase 4 - Gen Yard		157	157	21-Apr-27	02-Dec-27
P6EX.1030	Phase 4 / Gen Yard - Set Transformers	2	2	21-Apr-27	22-Apr-27
P6EX.1050	Phase 4 / Gen Yard - Pull, Term & Test MV through XFMRs	7	7	23-Apr-27	03-May-27
P6EX.1100	Phase 4 / Gen Yard - Pull In FLORES Loop	5	5	04-May-27	10-May-27
P6EX.1370	Phase 4 / Gen Yard - Install Fuel Piping	30	30	20-May-27	01-Jul-27
P6EX.1380	Phase 4 / Gen Yard - Install Fuel System Control Conduit	10	10	04-Jun-27	17-Jun-27
P6EX.1120	Phase 4 / Gen Yard - Pour Sidewalk	5	5	18-Jun-27	24-Jun-27
P6EX.1060	Phase 4 / Gen Yard - Set Generators	2	2	10-Aug-27	11-Aug-27
P6EX.1090	Phase 4 / Gen Yard - Set Exhaust Stack and Shroud	12	12	12-Aug-27	27-Aug-27
P6EX.1390	Phase 4 / Gen Yard - Grounding / Lightning Protection	2	2	30-Aug-27	31-Aug-27
P6EX.1080	Phase 4 / Gen Yard - Install Generator Platforms	5	5	10-Sep-27	16-Sep-27
P6EX.1130	Phase 4 / Gen Yard - Install Foundations & Fencing	4	4	17-Sep-27	22-Sep-27
P6EX.1040	Phase 4 / Gen Yard - Install Cable Bus Structure	5	5	20-Oct-27	26-Oct-27
P6EX.1070	Phase 4 / Gen Yard - LV Cable Bus and Feeders - XFMRs to USBs	10	10	27-Oct-27	09-Nov-27
P6EX.1110	Phase 4 / Gen Yard - Energize Electrical - Site To Phase	0	0		09-Nov-27
P6EX.1140	Phase 4 / Gen Yard - LV Cable Bus and Feeders - Gens to USBs	15	15	10-Nov-27	02-Dec-27
Phase 4 - Electrical Room		129	129	30-Apr-27	01-Nov-27
P6ER.1800	Phase 4 / Elec Rm - Layout	1	1	30-Apr-27	30-Apr-27
P6ER.2020	Phase 4 / Elec Rm - Install DriClad	10	10	03-May-27	14-May-27
P6ER.1040	Phase 4 / Elec Rm - Wall Electric & Fire Alarm Rough-in	5	5	14-May-27	20-May-27
P6ER.1020	Phase 4 / Elec Rm - Stud Framing	4	4	17-May-27	20-May-27

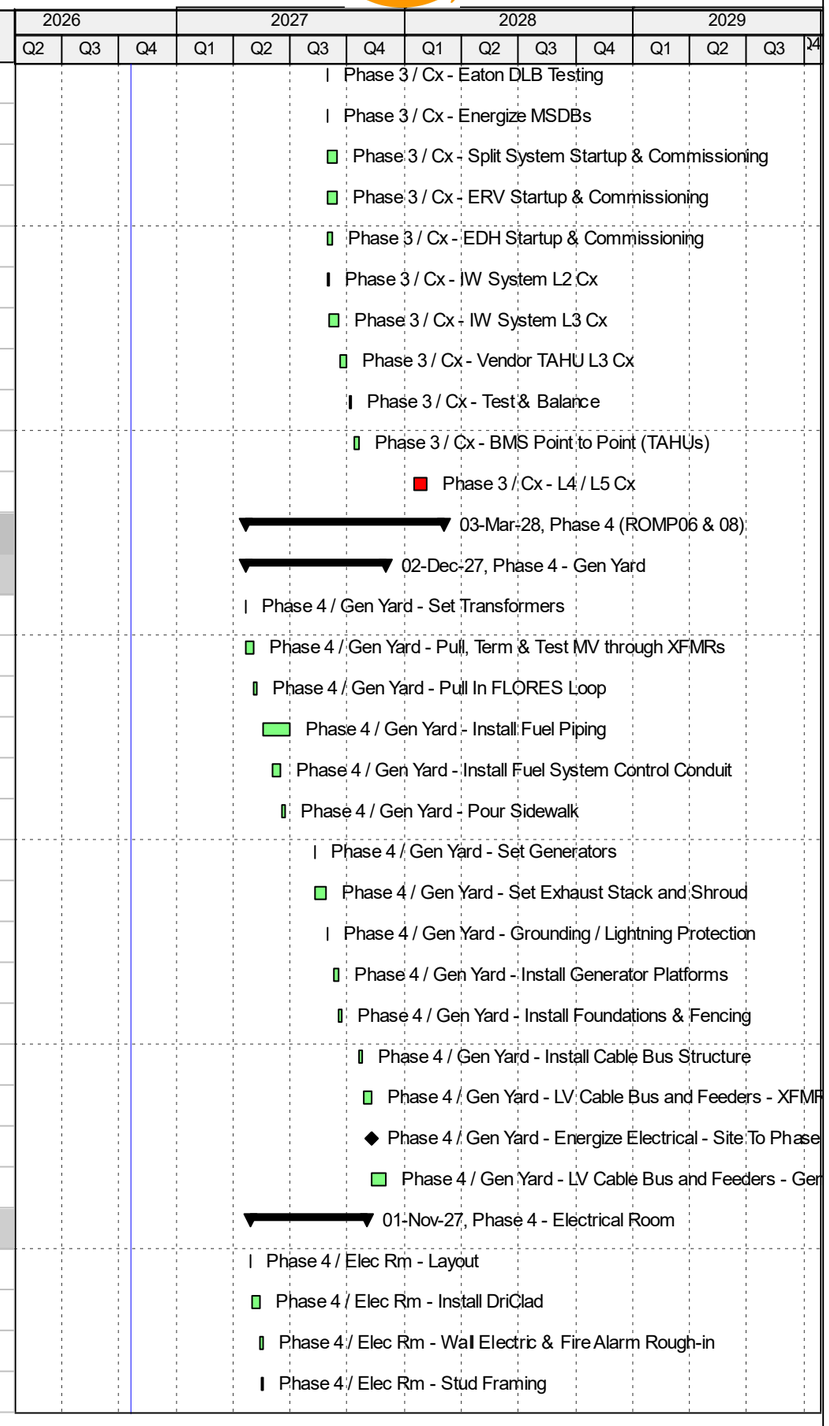


Gray

CMH139
Preliminary Schedule

aws


Activity ID	Activity Name	OD	RD	Start	Finish
P6ER.1060	Phase 4 / Elec Rm - Hang Drywall & Finish	5	5	21-May-27	27-May-27
P6ER.1380	Phase 4 / Elec Rm - Hangers	3	3	21-May-27	25-May-27
P6ER.1080	Phase 4 / Elec Rm - Prime & First Coat Paint	1	1	28-May-27	28-May-27
P6ER.1000	Phase 4 / Elec Rm - Pull TAHU Feeders	5	5	28-May-27	04-Jun-27
P6ER.1010	Phase 4 / Elec Rm - Pull Lighting Control Wiring	7	7	07-Jun-27	15-Jun-27
P6ER.1120	Phase 4 / Elec Rm - Install Split Systems & ERV	10	10	18-Jun-27	01-Jul-27
P6ER.1810	Phase 4 / Elec Rm - Fire Protection Rough In	3	3	18-Jun-27	22-Jun-27
P6ER.1820	Phase 4 / Elec Rm - Install OH Conduit / Mechanical Feeders	5	5	18-Jun-27	24-Jun-27
P6ER.1390	Phase 4 / Elec Rm - Pull / Term HUPPs	2	2	23-Jun-27	24-Jun-27
P6ER.1830	Phase 4 / Elec Rm - Set USB (LV Gear)	5	5	10-Aug-27	16-Aug-27
P6ER.1140	Phase 4 / Elec Rm - Install AMCOP Panels	1	1	17-Aug-27	17-Aug-27
P6ER.1850	Phase 4 / Elec Rm - Doors & Hardware	5	5	17-Aug-27	23-Aug-27
P6ER.1860	Phase 4 / Elec Rm - Breaker Testing USB	5	5	17-Aug-27	23-Aug-27
P6ER.1840	Phase 4 / Elec Rm - Fill Buck Out	4	4	17-Aug-27	20-Aug-27
P6ER.1870	Phase 4 / Elec Rm - Install Cable Tray	7	7	17-Aug-27	25-Aug-27
P6ER.1210	Phase 4 / Elec Rm - Set SCCS Setting for Breakers	1	1	24-Aug-27	24-Aug-27
P6ER.1110	Phase 4 / Elec Rm - Set OFCI Electrical Panels	5	5	26-Aug-27	01-Sep-27
P6ER.1890	Phase 4 / Elec Rm - Fire Alarm / VESDA	5	5	26-Aug-27	01-Sep-27
P6ER.1910	Phase 4 / Elec Rm - Install Bus Duct	7	7	26-Aug-27	03-Sep-27
P6ER.2010	Phase 4 / Elec Rm - Install Control Conduit	5	5	26-Aug-27	01-Sep-27
P6ER.1920	Phase 4 / Elec Rm - Install Electrical Raceways (Branch Conduits)	10	10	02-Sep-27	16-Sep-27
P6ER.1190	Phase 4 / Elec Rm - Pull & Term DLB Fiber	5	5	02-Sep-27	09-Sep-27
P4ER.2020	Phase 4 / Elec Rm - Install UPS	4	4	02-Sep-27	08-Sep-27
P6ER.1150	Phase 4 / Elec Rm - Pull PDC Feeders	5	5	03-Sep-27	10-Sep-27
P6ER.1160	Phase 4 / Elec Rm - Terminate LV Electrical Panels	5	5	08-Sep-27	14-Sep-27
P6ER.1940	Phase 4 / Elec Rm - Manufacturer Inspection USB	1	1	10-Sep-27	10-Sep-27
P6ER.1220	Phase 4 / Elec Rm - Install Lighting	3	3	13-Sep-27	15-Sep-27
P6ER.1960	Phase 4 / Elec Rm - Seismic Install	1	1	13-Sep-27	13-Sep-27
P6ER.1990	Phase 4 / Elec Rm - Test & Terminate PDC Feeders	5	5	13-Sep-27	17-Sep-27
P6ER.1970	Phase 4 / Elec Rm - Egress Lighting	3	3	13-Sep-27	15-Sep-27
P6ER.1900	Phase 4 / Elec Rm - Install CRAC Unit & Exhaust Fan	5	5	15-Sep-27	21-Sep-27
P6ER.1980	Phase 4 / Elec Rm - Trade Repair	3	3	17-Sep-27	21-Sep-27
P6ER.2000	Phase 4 / Elec Rm - Final Paint / Touch Up	1	1	22-Sep-27	22-Sep-27

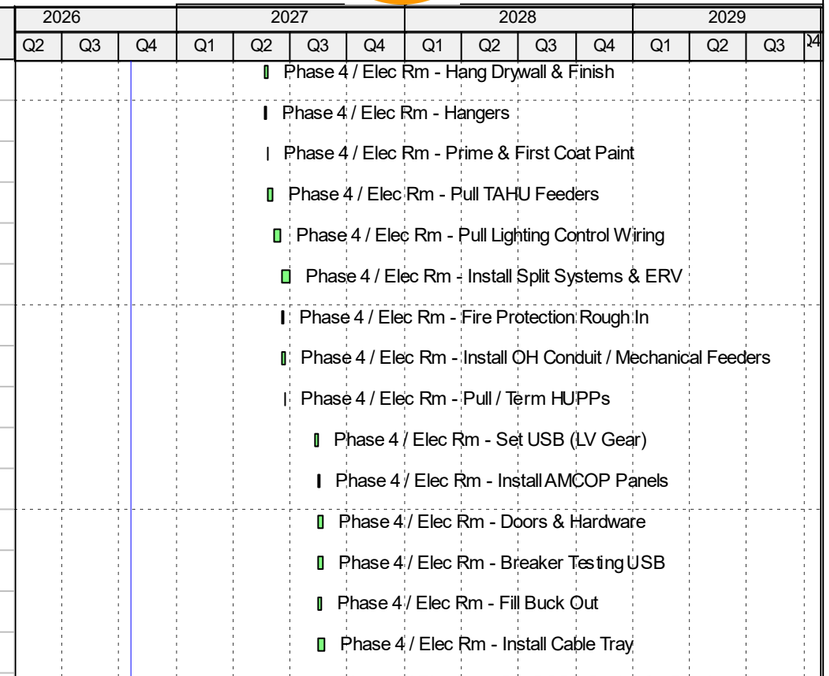


Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

Run Date: 15-Oct-26 14:16
Data Date: 19-Oct-26


Activity ID	Activity Name	OD	RD	Start	Finish
P6ER.1930	Phase 4 / Elec Rm - OA Reference Piping	5	5	22-Sep-27	28-Sep-27
P6ER.1180	Phase 4 / Elec Rm - BMS System	10	10	29-Sep-27	12-Oct-27
P6ER.1950	Phase 4 / Elec Rm - Energize BMS Panels	1	1	13-Oct-27	13-Oct-27
P6ER.1880	Phase 4 / Elec Rm - Cable Bus Termination	4	4	27-Oct-27	01-Nov-27
Phase 4 - Data Hall		188	188	17-May-27	11-Feb-28
P6RP.1040	Phase 4 / Data Hall - Stud Framing (Data Hall / Elec Rm Wall)	5	5	17-May-27	21-May-27
P6RP.1370	Phase 4 / Data Hall - Stud Framing (Equipment Platform)	5	5	21-May-27	27-May-27
P4RP.1600	Phase 4 / Data Hall - OH Electric Rough In	5	5	28-May-27	04-Jun-27
P4RP.1590	Phase 4 / Data Hall - Install Temp Wall Bulkhead	5	5	07-Jun-27	11-Jun-27
P4RP.1730	Phase 4 / Data Hall - Fire Protection Rough In	5	5	11-Jun-27	17-Jun-27
P4RP.1700	Phase 4 / Data Hall - Above Ceiling Cable Tray	3	3	14-Jun-27	16-Jun-27
P4RP.1710	Phase 4 / Data Hall - Seismic Install	2	2	17-Jun-27	18-Jun-27
P6RP.1100	Phase 4 / Data Hall - Wall Elec & FA Rough-In (IMP)	4	4	18-Jun-27	23-Jun-27
P6RP.1380	Phase 4 / Data Hall - Wall Elec & FA Rough-In (Data Hall / Elec Rm)	4	4	18-Jun-27	23-Jun-27
P4RP.1610	Phase 4 / Data Hall - In Wall Rough In Inspection (Electrical / FA)	1	1	24-Jun-27	24-Jun-27
P6RP.1130	Phase 4 / Data Hall - Hang Drywall & Finish (Data Hall / Elec Rm)	5	5	25-Jun-27	01-Jul-27
P6RP.1190	Phase 4 / Data Hall - Prime & First Coat Paint	3	3	02-Jul-27	07-Jul-27
P6RP.1050	Phase 4 / Data Hall - Fire Protection Drops	5	5	08-Jul-27	14-Jul-27
P4RP.1390	Phase 4 / Data Hall - Install Backdraft Dampers	5	5	08-Jul-27	14-Jul-27
P6RP.1020	Phase 4 / Data Hall - MARS Racking	7	7	10-Aug-27	18-Aug-27
P6RP.1070	Phase 4 / Data Hall - Install Lighting Wiring & Fixtures	5	5	19-Aug-27	25-Aug-27
P6RP.1060	Phase 4 / Data Hall - Upper Polycarbonate Panels and Cold Aisle Cable Tray Arms	3	3	19-Aug-27	23-Aug-27
P6RP.1230	Phase 4 / Data Hall - Install Control Dampers (PRD)	5	5	19-Aug-27	25-Aug-27
P6RP.1200	Phase 4 / Data Hall - Power PDC Whips	10	10	19-Aug-27	01-Sep-27
P6RP.1360	Phase 4 / Data Hall - Temp Wall Install	5	5	19-Aug-27	25-Aug-27
P4RP.1620	Phase 4 / Data Hall - ACT Grid Corridors	4	4	19-Aug-27	24-Aug-27
P4RP.1630	Phase 4 / Data Hall - Install Snubbers	5	5	19-Aug-27	25-Aug-27
P6RP.1030	Phase 4 / Data Hall - PDC Feeders Drops & Supports	10	10	19-Aug-27	01-Sep-27
P6RP.1210	Phase 4 / Data Hall - Fire Alarm VESDA	10	10	23-Aug-27	03-Sep-27
P4RP.1640	Phase 4 / Data Hall - ACT Grid Cold Aisles	5	5	23-Aug-27	27-Aug-27
P6RP.1260	Phase 4 / Data Hall - Perfect Position	4	4	24-Aug-27	27-Aug-27
P6RP.1250	Phase 4 / Data Hall - Doors and Hardware	2	2	26-Aug-27	27-Aug-27
P4RP.1650	Phase 4 / Data Hall - Install Control Wiring	5	5	26-Aug-27	01-Sep-27

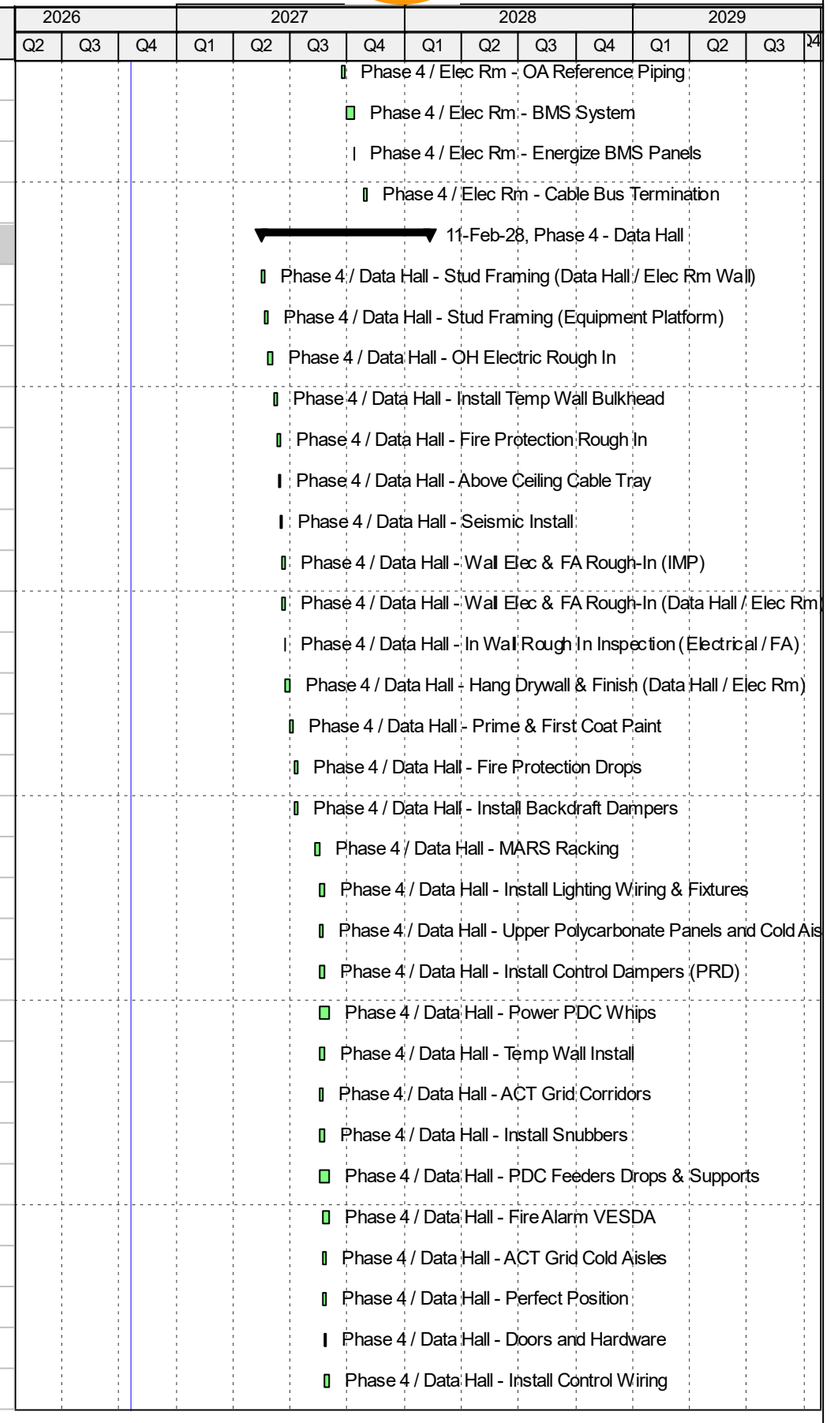

Activity ID	Activity Name	OD	RD	Start	Finish
P6RP.1290	Phase 4 / Data Hall - Avenue Basket/Cable Tray (South)	2	2	30-Aug-27	31-Aug-27
P6RP.1280	Phase 4 / Data Hall - Install Fire Protection Heads Avenue	2	2	30-Aug-27	31-Aug-27
P6RP.1160	Phase 4 / Data Hall - Cold Aisle Basket/Cable Tray	3	3	30-Aug-27	01-Sep-27
P4RP.1660	Phase 4 / Data Hall - ACT Borders For Corridors	1	1	30-Aug-27	30-Aug-27
P4RP.1720	Phase 4 / Data Hall - Install Fire Protection Heads Cold Aisle	2	2	30-Aug-27	31-Aug-27
P4RP.1670	Phase 4 / Data Hall - ACT Borders For Cold Aisles	1	1	31-Aug-27	31-Aug-27
P6RP.1310	Phase 4 / Data Hall - Structural Overhead Inspection (Avenue)	1	1	01-Sep-27	01-Sep-27
P6RP.1390	Phase 4 / Data Hall - Avenue Basket/Cable Tray (North)	2	2	01-Sep-27	02-Sep-27
P4RP.1690	Phase 4 / Data Hall - ACT Remaining Tile Drops Post Inspection	3	3	02-Sep-27	07-Sep-27
P4RP.1680	Phase 4 / Data Hall - Touch Up Paint	4	4	02-Sep-27	08-Sep-27
P6RP.1340	Phase 4 / Data Hall - CAT6 Cable Install	3	3	03-Sep-27	08-Sep-27
P6RP.1080	Phase 4 / Data Hall - Set PDC Cabinets	3	3	08-Sep-27	10-Sep-27
P6RP.1110	Phase 4 / Data Hall - BMS	15	15	13-Sep-27	01-Oct-27
P6RP.1270	Phase 4 / Data Hall - PDC Feeders Test & Terminate	10	10	13-Sep-27	24-Sep-27
P6RP.1350	Phase 4 / Data Hall - EPMS	15	15	13-Sep-27	01-Oct-27
P6RP.1180	Phase 4 / Data Hall - Lower Polycarbonate Panels	5	5	04-Oct-27	08-Oct-27
P6RP.1090	Phase 4 / Data Hall - NEA Finalization	19	19	28-Dec-27	24-Jan-28
P6RP.1120	Phase 4 / Data Hall - H2C Readiness Coordination	14	14	25-Jan-28	11-Feb-28
Phase 4 - TAHU Gallery		76	76	04-Jun-27	21-Sep-27
P6DG.1240	Phase 4 / TAHU - Fire Protection Rough In	5	5	04-Jun-27	10-Jun-27
P6DG.1100	Phase 4 / TAHU - Sound Attenuator	10	10	18-Jun-27	01-Jul-27
P6DG.1130	Phase 4 / TAHU - Seismic Install	2	2	18-Jun-27	21-Jun-27
P6DG.1180	Phase 4 / TAHU - Hang Outside Stairwell / Lobby Drywall	4	4	18-Jun-27	23-Jun-27
P6DG.1190	Phase 4 / TAHU - Install CFMF IMP Support	10	10	18-Jun-27	01-Jul-27
P6DG.1040	Phase 4 / TAHU - Install IMP Panels	6	6	02-Jul-27	12-Jul-27
P6DG.1050	Phase 4 / TAHU - Fire Alarm (VESDA)	5	5	13-Jul-27	19-Jul-27
P6DG.1080	Phase 4 / TAHU - Prime & Paint Drywall	3	3	13-Jul-27	15-Jul-27
P6DG.1010	Phase 4 / TAHU - BMS Controls Rough In	10	10	13-Jul-27	26-Jul-27
P6DG.1030	Phase 4 / TAHU - Wall Elec & Fire Alarm Rough-In	5	5	13-Jul-27	19-Jul-27
P6DG.1090	Phase 4 / TAHU - Control Dampers	5	5	16-Jul-27	22-Jul-27
P6DG.1110	Phase 4 / TAHU - Pull & Terminate Fire Alarm Cable	5	5	20-Jul-27	26-Jul-27
P6DG.1070	Phase 4 / TAHU - Set TAHUs	2	2	10-Aug-27	11-Aug-27
P6DG.1140	Phase 4 / TAHU - Doors and Hardware	3	3	12-Aug-27	16-Aug-27

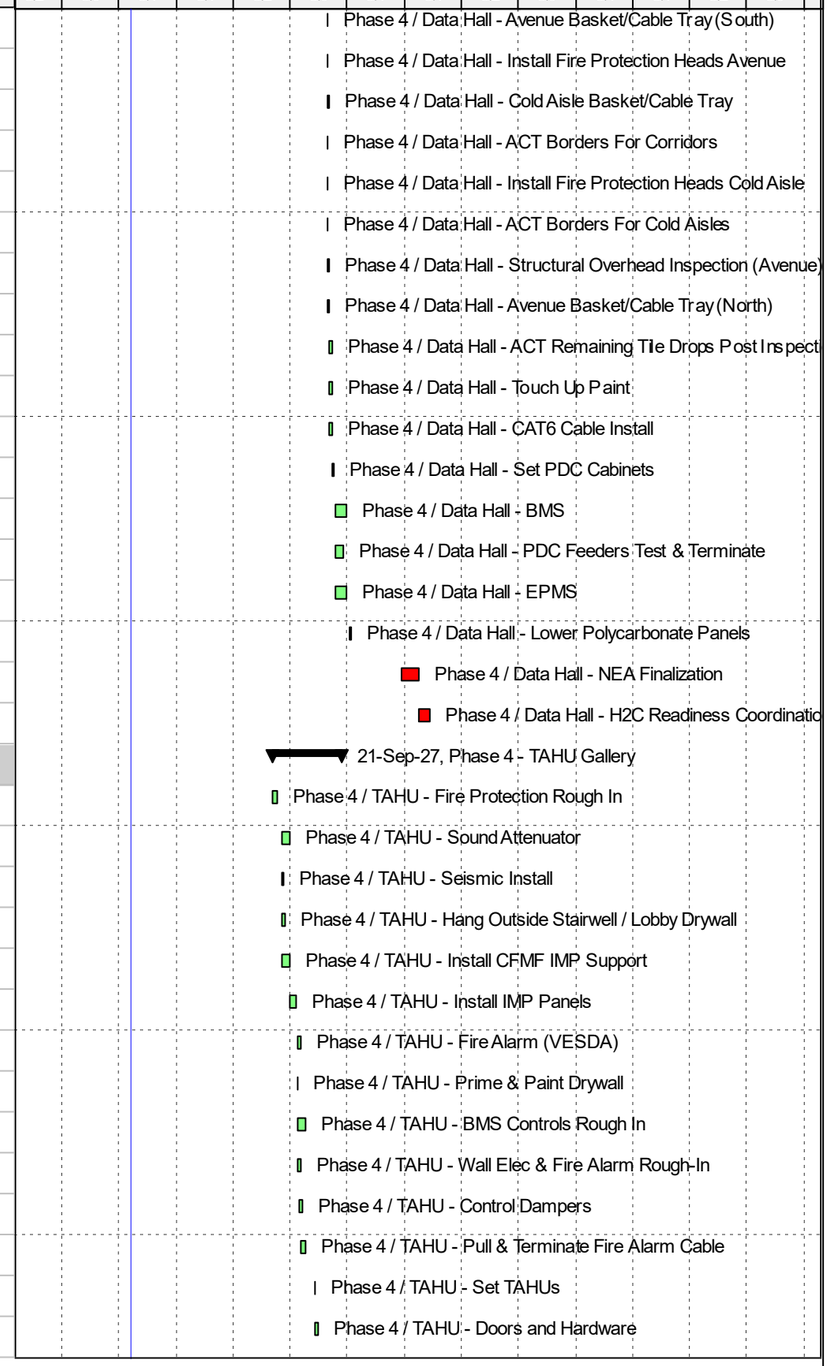


Activity ID	Activity Name	OD	RD	Start	Finish
P6DG.1060	Phase 4 / TAHU - IW Supply Piping at TAHUs	10	10	12-Aug-27	25-Aug-27
P6DG.1210	Phase 4 / TAHU - TAHU Trim	10	10	12-Aug-27	25-Aug-27
P6DG.1220	Phase 4 / TAHU - Paint Doors & Frames	2	2	17-Aug-27	18-Aug-27
P6DG.1150	Phase 4 / TAHU - Lighting	5	5	26-Aug-27	01-Sep-27
P6DG.1160	Phase 4 / TAHU - Tie In TAHUs	10	10	26-Aug-27	09-Sep-27
P6DG.1170	Phase 4 / TAHU - BMS Tie In	2	2	08-Sep-27	09-Sep-27
P6DG.1120	Phase 4 / TAHU - IW Drain Piping at TAHUs	5	5	10-Sep-27	16-Sep-27
P6DG.1230	Phase 4 / TAHU - Terminate Power To TAHUs	3	3	17-Sep-27	21-Sep-27
Phase 4 - Cx		212	212	04-May-27	03-Mar-28
P6CX.1100	Phase 4 / Cx - EC L2 Cx Review for MV Switchgear	1	1	04-May-27	04-May-27
P6CX.1080	Phase 4 / Cx - EC L2 Cx Review for MV XFMRs	1	1	05-May-27	05-May-27
P6CX.1090	Phase 4 / Cx - EC L3 Cx for MV XFMRs	5	5	06-May-27	12-May-27
P6CX.1360	Phase 4 / Cx - Eaton XFMR Testing	3	3	06-May-27	10-May-27
P6CX.1130	Phase 4 / Cx - EC L3 Cx for MV	3	3	11-May-27	13-May-27
P6CX.1200	Phase 4 / Cx - Fuel System Cx	7	7	02-Jul-27	13-Jul-27
P6CX.1180	Phase 4 / Cx - Construction Power To Generator	3	3	12-Aug-27	16-Aug-27
P6CX.1030	Phase 4 / Cx - CAT L2 Cx Generators	2	2	17-Aug-27	18-Aug-27
P6CX.1120	Phase 4 / Cx - EC 3rd Party Testing & Inspection USB (L2)	3	3	17-Aug-27	19-Aug-27
P6CX.1160	Phase 4 / Cx - HUPPS Panelboards Energized	1	1	02-Sep-27	02-Sep-27
P6CX.1000	Phase 4 / Cx - EC 3rd Party LV Panelboard Testing (L2)	3	3	02-Sep-27	07-Sep-27
P6CX.1320	Phase 4 / Cx - AMCOP / BACOP Start Up & Cx	5	5	02-Sep-27	09-Sep-27
P6CX.1370	Phase 4 / Cx - Energize Control Network Arch	1	1	03-Sep-27	03-Sep-27
P6CX.2010	Phase 4 / Cx - Fire Alarm Programming & Pretest	2	2	07-Sep-27	08-Sep-27
P6CX.1230	Phase 4 / Cx - EC 3rd Party Busway Bus Plug Testing (L2)	2	2	07-Sep-27	08-Sep-27
P4CX.2080	Phase 4 / Cx - EPMS Point to Point (USB)	4	4	07-Sep-27	10-Sep-27
P6MCM.6010	Phase 4 / Cx - Tie in MOP C1	2	2	09-Sep-27	10-Sep-27
P6MCM.6020	Phase 4 / Cx - Eaton DLB Programming & Test (FLORES)	5	5	10-Sep-27	16-Sep-27
P6MCM.6030	Phase 4 / Cx - Tie in MOP C2	2	2	13-Sep-27	14-Sep-27
P6CX.1140	Phase 4 / Cx - EC 3rd Party Busway C1 / C2 Testing	2	2	15-Sep-27	16-Sep-27
P6CX.1190	Phase 4 / Cx - EC L2 Cx Review for LV Panelboard	2	2	15-Sep-27	16-Sep-27
P6MS.180	Phase 4 / Cx - Life Safety Walkthrough	1	1	16-Sep-27	16-Sep-27
P6CX.1260	Phase 4 / Cx - EC L3 Cx LV Panelboard	1	1	17-Sep-27	17-Sep-27
P6CX.1170	Phase 4 / Cx - EC Busway C1 / C2 L2 Cx Review	1	1	17-Sep-27	17-Sep-27

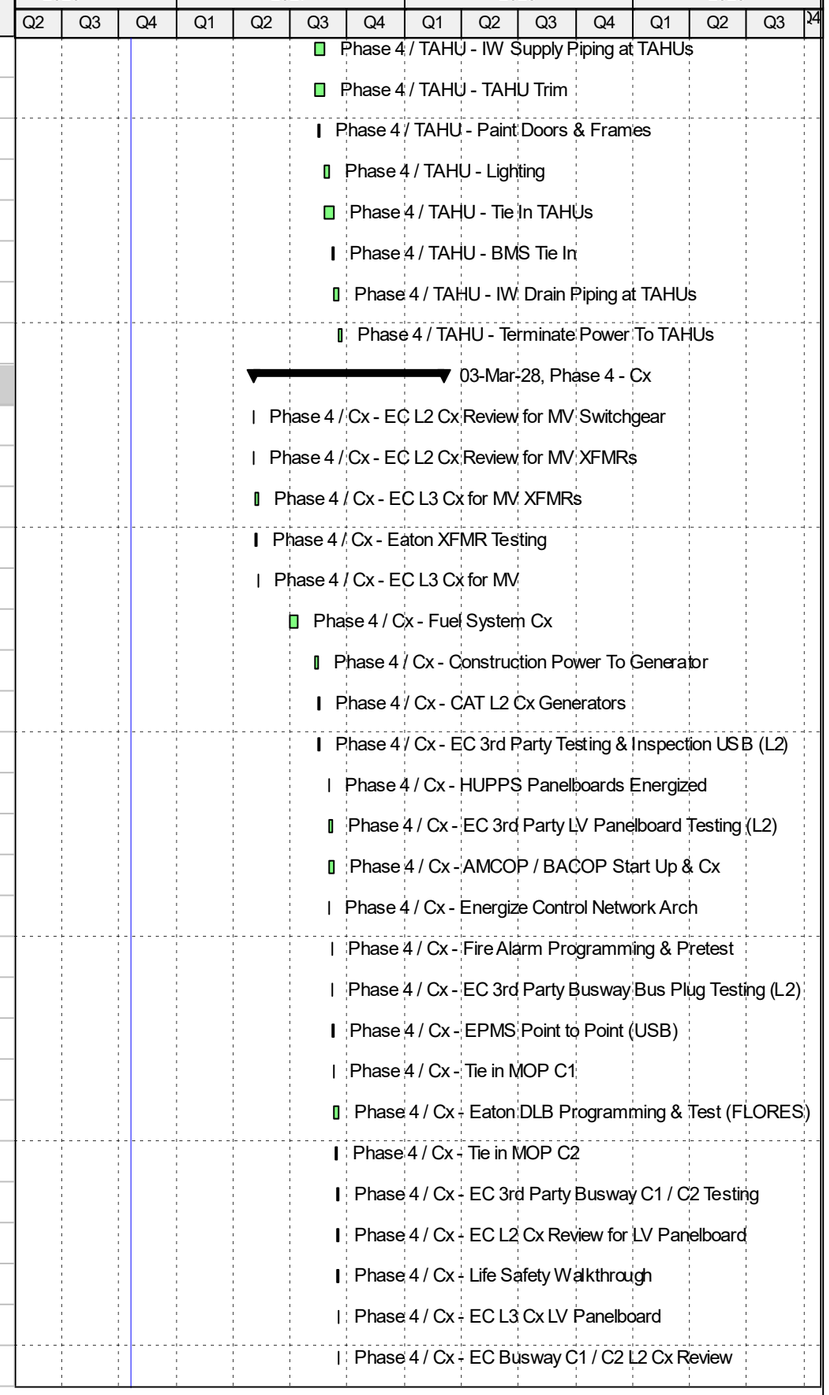

CMH139
Preliminary Schedule


Activity ID	Activity Name	OD	RD	Start	Finish
P6CX.1220	Phase 4 / Cx - EC Busway C1 L3 Cx	2	2	20-Sep-27	21-Sep-27
P4CX.2100	Phase 4 / Cx - EPMS Point to Point (PDC)	4	4	20-Sep-27	23-Sep-27
P6CX.1210	Phase 4 / Cx - MC TAHU L2 Cx	5	5	22-Sep-27	28-Sep-27
P6CX.2020	Phase 4 / Cx - EC Busway C2 L3 Cx	2	2	22-Sep-27	23-Sep-27
P4CX.2090	Phase 4 / Cx - BMS Point to Point (TAHUs)	5	5	13-Oct-27	19-Oct-27
P6CX.1150	Phase 4 / Cx - EC L3 Cx USBs	2	2	10-Nov-27	11-Nov-27
P6CX.1250	Phase 4 / Cx - Vendor UPS Start Up & Cx	9	9	12-Nov-27	24-Nov-27
P6CX.1310	Phase 4 / Cx - ATS L3 Cx	1	1	12-Nov-27	12-Nov-27
P6CX.1340	Phase 4 / Cx - Eaton DLB Testing	2	2	12-Nov-27	15-Nov-27
P6CX.2030	Phase 4 / Cx - Energize MSDBs	1	1	15-Nov-27	15-Nov-27
P6CX.1290	Phase 4 / Cx - Split System Startup & Commissioning	10	10	16-Nov-27	01-Dec-27
P6CX.1280	Phase 4 / Cx - ERV Startup & Commissioning	10	10	16-Nov-27	01-Dec-27
P6CX.1270	Phase 4 / Cx - EDH Startup & Commissioning	4	4	16-Nov-27	19-Nov-27
P6CX.1300	Phase 4 / Cx - IW System L2 Cx	2	2	16-Nov-27	17-Nov-27
P6CX.1380	Phase 4 / Cx - IW System L3 Cx	10	10	18-Nov-27	03-Dec-27
P6CX.1040	Phase 4 / Cx - EC L2 Cx Review for Generator	1	1	03-Dec-27	03-Dec-27
P6CX.1070	Phase 4 / Cx - EC L3 Cx Generators	3	3	06-Dec-27	08-Dec-27
P6CX.1060	Phase 4 / Cx - CAT L3 Cx Generators Testing	5	5	06-Dec-27	10-Dec-27
P6CX.1240	Phase 4 / Cx - Vendor TAHU L3 Cx	10	10	06-Dec-27	17-Dec-27
P6CX.1330	Phase 4 / Cx - Test & Balance	5	5	20-Dec-27	27-Dec-27
P6CX.1350	Phase 4 / Cx - L4 / L5 Cx	15	15	14-Feb-28	03-Mar-28
Phase 5 (ROMP09 & 11)		257	257	30-Mar-27	31-Mar-28
Phase 5 - Gen Yard		155	155	23-Apr-27	02-Dec-27
P9EX.1030	Phase 5 / Gen Yard - Set Transformers	2	2	23-Apr-27	26-Apr-27
P9EX.1050	Phase 5 / Gen Yard - Pull, Term & Test MV through XFMRs	7	7	27-Apr-27	05-May-27
P9EX.1100	Phase 5 / Gen Yard - Pull In FLORES Loop	5	5	06-May-27	12-May-27
P9EX.1370	Phase 5 / Gen Yard - Install Fuel Piping	30	30	20-May-27	01-Jul-27
P9EX.1380	Phase 5 / Gen Yard - Install Fuel System Control Conduit	10	10	04-Jun-27	17-Jun-27
P9EX.1120	Phase 5 / Gen Yard - Pour Sidewalk	5	5	18-Jun-27	24-Jun-27
P9EX.1060	Phase 5 / Gen Yard - Set Generators	2	2	07-Sep-27	08-Sep-27
P9EX.1090	Phase 5 / Gen Yard - Set Exhaust Stack and Shroud	12	12	09-Sep-27	24-Sep-27
P9EX.1390	Phase 5 / Gen Yard - Grounding / Lightning Protection	2	2	27-Sep-27	28-Sep-27
P9EX.1080	Phase 5 / Gen Yard - Install Generator Platforms	5	5	07-Oct-27	13-Oct-27

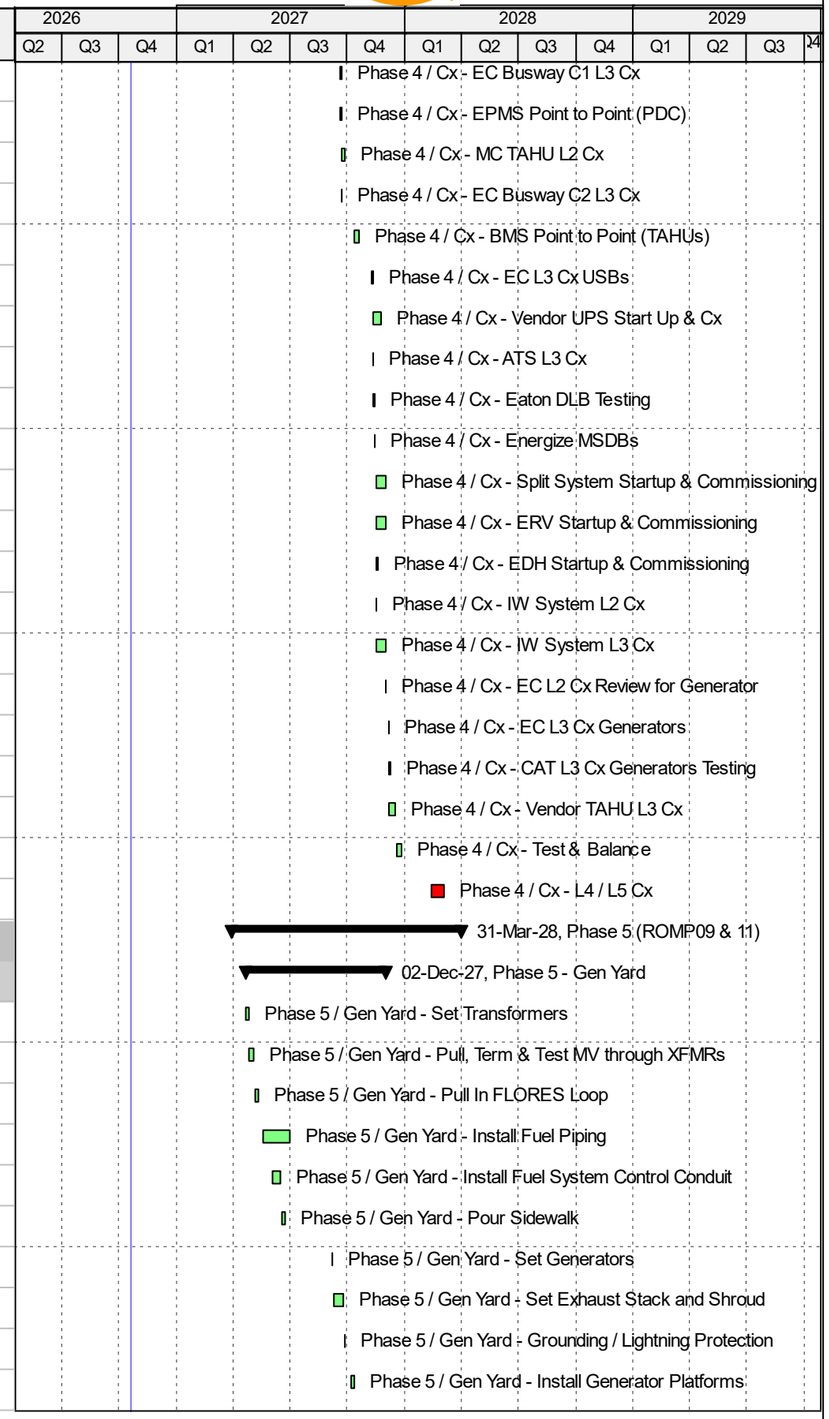


Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

Run Date: 15-Oct-26 14:16
Data Date: 19-Oct-26


Activity ID	Activity Name	OD	RD	Start	Finish
P9EX.1130	Phase 5 / Gen Yard - Install Foundations & Fencing	4	4	14-Oct-27	19-Oct-27
P9EX.1040	Phase 5 / Gen Yard - Install Cable Bus Structure	5	5	20-Oct-27	26-Oct-27
P9EX.1070	Phase 5 / Gen Yard - LV Cable Bus and Feeders - XFMRs to USBs	10	10	27-Oct-27	09-Nov-27
P9EX.1110	Phase 5 / Gen Yard - Energize Electrical - Site To Phase	0	0		09-Nov-27
P9EX.1190	Phase 5 / Gen Yard - LV Cable Bus and Feeders - Gens to USBs	15	15	10-Nov-27	02-Dec-27
Phase 5 - Electrical Room		129	129	30-Apr-27	01-Nov-27
P9ER.2010	Phase 5 / Elec Rm - Layout	1	1	30-Apr-27	30-Apr-27
P9ER.2240	Phase 5 / Elec Rm - Install DriClad	10	10	03-May-27	14-May-27
P9ER.1040	Phase 5 / Elec Rm - Wall Electric & Fire Alarm Rough-in	5	5	14-May-27	20-May-27
P9ER.1020	Phase 5 / Elec Rm - Stud Framing	4	4	17-May-27	20-May-27
P9ER.1060	Phase 5 / Elec Rm - Hang Drywall & Finish	5	5	21-May-27	27-May-27
P9ER.1380	Phase 5 / Elec Rm - Hangers	3	3	21-May-27	25-May-27
P9ER.1080	Phase 5 / Elec Rm - Prime & First Coat Paint	1	1	28-May-27	28-May-27
P9ER.1000	Phase 5 / Elec Rm - Pull TAHU Feeders	5	5	07-Jun-27	11-Jun-27
P9ER.1010	Phase 5 / Elec Rm - Pull Lighting Control Wiring	7	7	14-Jun-27	22-Jun-27
P9ER.1120	Phase 5 / Elec Rm - Install Split Systems & ERV	10	10	23-Jul-27	05-Aug-27
P9ER.2020	Phase 5 / Elec Rm - Fire Protection Rough In	3	3	23-Jul-27	27-Jul-27
P9ER.2030	Phase 5 / Elec Rm - Install OH Conduit / Mechanical Feeders	5	5	23-Jul-27	29-Jul-27
P9ER.2220	Phase 5 / Elec Rm - Pull / Term HUPPs	2	2	28-Jul-27	29-Jul-27
P9ER.2040	Phase 5 / Elec Rm - Set USB (LV Gear)	5	5	07-Sep-27	13-Sep-27
P9ER.1140	Phase 5 / Elec Rm - Install AMCOP Panels	1	1	14-Sep-27	14-Sep-27
P9ER.2060	Phase 5 / Elec Rm - Doors & Hardware	5	5	14-Sep-27	20-Sep-27
P9ER.2070	Phase 5 / Elec Rm - Breaker Testing USB	5	5	14-Sep-27	20-Sep-27
P9ER.2050	Phase 5 / Elec Rm - Fill Buck Out	4	4	14-Sep-27	17-Sep-27
P9ER.2080	Phase 5 / Elec Rm - Install Cable Tray	7	7	14-Sep-27	22-Sep-27
P9ER.1210	Phase 5 / Elec Rm - Set SCCS Setting for Breakers	1	1	21-Sep-27	21-Sep-27
P9ER.1110	Phase 5 / Elec Rm - Set OFCI Electrical Panels	5	5	23-Sep-27	29-Sep-27
P9ER.2100	Phase 5 / Elec Rm - Fire Alarm / VESDA	5	5	23-Sep-27	29-Sep-27
P9ER.2120	Phase 5 / Elec Rm - Install Bus Duct	7	7	23-Sep-27	01-Oct-27
P9ER.2110	Phase 5 / Elec Rm - Install CRAC Unit & Exhaust Fan	5	5	23-Sep-27	29-Sep-27
P9ER.2230	Phase 5 / Elec Rm - Install Control Conduit	5	5	23-Sep-27	29-Sep-27
P9ER.1330	Phase 5 / Elec Rm - Pull & Term DLB Fiber	5	5	30-Sep-27	06-Oct-27
P9ER.2130	Phase 5 / Elec Rm - Install Electrical Raceways (Branch Conduits)	10	10	30-Sep-27	13-Oct-27

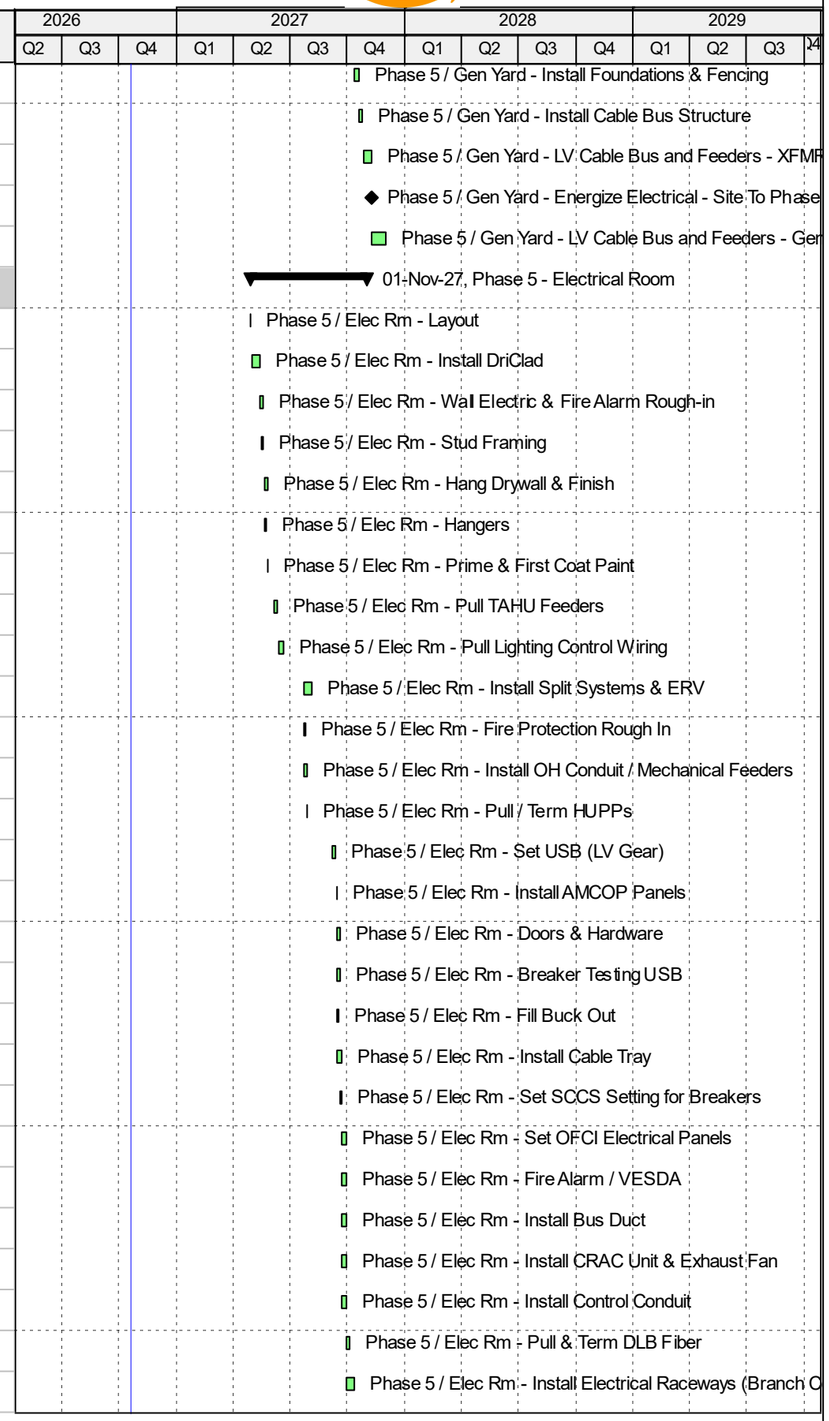


Activity ID	Activity Name	OD	RD	Start	Finish
P9ER.2140	Phase 5 / Elec Rm - OA Reference Piping	5	5	30-Sep-27	06-Oct-27
P5ER.2240	Phase 5 / Elec Rm - Install UPS	4	4	30-Sep-27	05-Oct-27
P9ER.1150	Phase 5 / Elec Rm - Pull PDC Feeders	5	5	01-Oct-27	07-Oct-27
P9ER.1160	Phase 5 / Elec Rm - Terminate LV Electrical Panels	5	5	05-Oct-27	11-Oct-27
P9ER.2150	Phase 5 / Elec Rm - Manufacturer Inspection USB	1	1	07-Oct-27	07-Oct-27
P9ER.1220	Phase 5 / Elec Rm - Install Lighting	3	3	08-Oct-27	12-Oct-27
P9ER.2170	Phase 5 / Elec Rm - Seismic Install	1	1	08-Oct-27	08-Oct-27
P9ER.2200	Phase 5 / Elec Rm - Test & Terminate PDC Feeders	5	5	08-Oct-27	14-Oct-27
P9ER.2180	Phase 5 / Elec Rm - Egress Lighting	3	3	08-Oct-27	12-Oct-27
P9ER.1180	Phase 5 / Elec Rm - BMS System	10	10	12-Oct-27	25-Oct-27
P9ER.2190	Phase 5 / Elec Rm - Trade Repair	3	3	14-Oct-27	18-Oct-27
P9ER.2210	Phase 5 / Elec Rm - Final Paint / Touch Up	1	1	19-Oct-27	19-Oct-27
P9ER.2160	Phase 5 / Elec Rm - Energize BMS Panels	1	1	26-Oct-27	26-Oct-27
P9ER.2090	Phase 5 / Elec Rm - Cable Bus Termination	4	4	27-Oct-27	01-Nov-27
Phase 5 - Data Hall		237	237	06-Apr-27	10-Mar-28
P5RP.1750	Phase 5 / Data Hall - Fire Protection Rough In	5	5	06-Apr-27	12-Apr-27
P9RP.1040	Phase 5 / Data Hall - Stud Framing (Data Hall / Elec Rm Wall)	5	5	17-May-27	21-May-27
P9RP.1440	Phase 5 / Data Hall - Stud Framing (Equipment Platform)	5	5	21-May-27	27-May-27
P5RP.1600	Phase 5 / Data Hall - OH Electric Rough In	5	5	28-May-27	04-Jun-27
P5RP.1590	Phase 5 / Data Hall - Install Temp Wall Bulkhead	5	5	14-Jun-27	18-Jun-27
P5RP.1720	Phase 5 / Data Hall - Above Ceiling Cable Tray	3	3	21-Jun-27	23-Jun-27
P5RP.1730	Phase 5 / Data Hall - Seismic Install	2	2	24-Jun-27	25-Jun-27
P9RP.1100	Phase 5 / Data Hall - Wall Elec & FA Rough-In (IMP)	4	4	23-Jul-27	28-Jul-27
P9RP.1450	Phase 5 / Data Hall - Wall Elec & FA Rough-In (Data Hall / Elec Rm)	4	4	23-Jul-27	28-Jul-27
P5RP.1610	Phase 5 / Data Hall - In Wall Rough In Inspection (Electrical / FA)	1	1	29-Jul-27	29-Jul-27
P9RP.1130	Phase 5 / Data Hall - Hang Drywall & Finish (Data Hall / Elec Rm)	5	5	30-Jul-27	05-Aug-27
P9RP.1190	Phase 5 / Data Hall - Prime & First Coat Paint	3	3	06-Aug-27	10-Aug-27
P9RP.1050	Phase 5 / Data Hall - Fire Protection Drops	5	5	11-Aug-27	17-Aug-27
P5RP.1120	Phase 5 / Data Hall - Install Backdraft Dampers	5	5	11-Aug-27	17-Aug-27
P9RP.1020	Phase 5 / Data Hall - MARS Racking	7	7	07-Sep-27	15-Sep-27
P9RP.1070	Phase 5 / Data Hall - Install Lighting Wiring & Fixtures	5	5	16-Sep-27	22-Sep-27
P9RP.1200	Phase 5 / Data Hall - Temp Wall Install	5	5	16-Sep-27	22-Sep-27
P9RP.1060	Phase 5 / Data Hall - Upper Polycarbonate Panels and Cold Aisle Cable Tray Arms	3	3	16-Sep-27	20-Sep-27

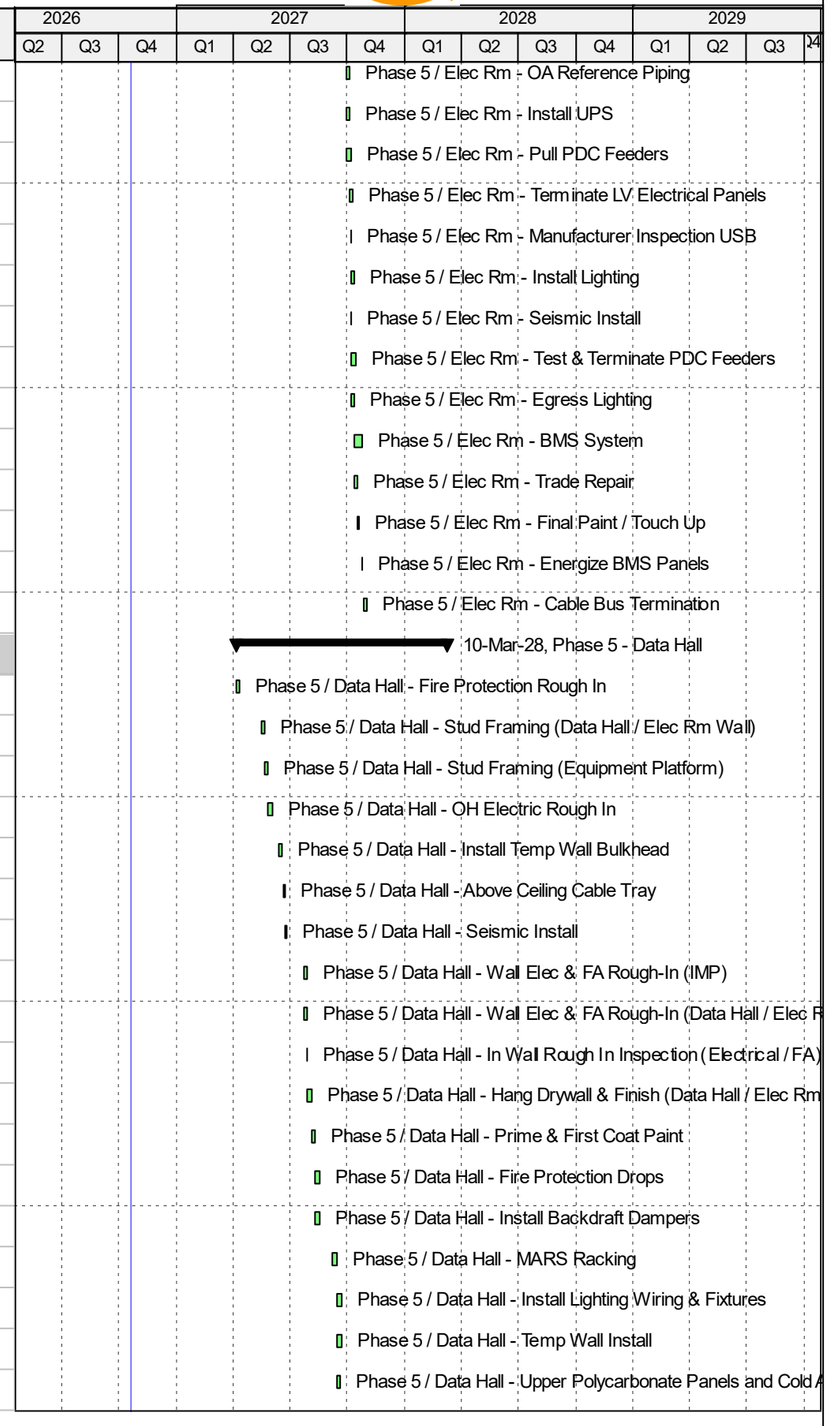

Activity ID	Activity Name	OD	RD	Start	Finish
P9RP.1230	Phase 5 / Data Hall - Install Control Dampers (PRD)	5	5	16-Sep-27	22-Sep-27
P9RP.1410	Phase 5 / Data Hall - Power PDC Whips	10	10	16-Sep-27	29-Sep-27
P5RP.1620	Phase 5 / Data Hall - ACT Grid Corridors	4	4	16-Sep-27	21-Sep-27
P5RP.1630	Phase 5 / Data Hall - Install Snubbers	5	5	16-Sep-27	22-Sep-27
P9RP.1030	Phase 5 / Data Hall - PDC Feeders Drops & Supports	10	10	16-Sep-27	29-Sep-27
P9RP.1210	Phase 5 / Data Hall - Fire Alarm VESDA	10	10	20-Sep-27	01-Oct-27
P5RP.1640	Phase 5 / Data Hall - ACT Grid Cold Aisles	5	5	20-Sep-27	24-Sep-27
P9RP.1120	Phase 5 / Data Hall - Perfect Position	4	4	21-Sep-27	24-Sep-27
P9RP.1250	Phase 5 / Data Hall - Doors and Hardware	2	2	23-Sep-27	24-Sep-27
P5RP.1650	Phase 5 / Data Hall - Install Control Wiring	5	5	23-Sep-27	29-Sep-27
P9RP.1280	Phase 5 / Data Hall - Install Fire Protection Heads Avenue	2	2	27-Sep-27	28-Sep-27
P9RP.1160	Phase 5 / Data Hall - Cold Aisle Basket/Cable Tray	3	3	27-Sep-27	29-Sep-27
P9RP.1360	Phase 5 / Data Hall - Avenue Basket/Cable Tray (South)	2	2	27-Sep-27	28-Sep-27
P5RP.1660	Phase 5 / Data Hall - ACT Borders For Corridors	1	1	27-Sep-27	27-Sep-27
P5RP.1740	Phase 5 / Data Hall - Install Fire Protection Heads Cold Aisle	2	2	27-Sep-27	28-Sep-27
P5RP.1670	Phase 5 / Data Hall - ACT Borders For Cold Aisles	1	1	28-Sep-27	28-Sep-27
P9RP.1290	Phase 5 / Data Hall - Avenue Basket/Cable Tray (North)	2	2	29-Sep-27	30-Sep-27
P9RP.1310	Phase 5 / Data Hall - Structural Overhead Inspection (Avenue)	1	1	29-Sep-27	29-Sep-27
P5RP.1690	Phase 5 / Data Hall - ACT Remaining Tile Drops Post Inspection	3	3	30-Sep-27	04-Oct-27
P5RP.1680	Phase 5 / Data Hall - Touch Up Paint	4	4	30-Sep-27	05-Oct-27
P9RP.1420	Phase 5 / Data Hall - CAT6 Cable Install	3	3	01-Oct-27	05-Oct-27
P9RP.1080	Phase 5 / Data Hall - Set PDC Cabinets	3	3	05-Oct-27	07-Oct-27
P9RP.1110	Phase 5 / Data Hall - BMS	15	15	08-Oct-27	28-Oct-27
P9RP.1270	Phase 5 / Data Hall - PDC Feeders Test & Terminate	10	10	08-Oct-27	21-Oct-27
P9RP.1430	Phase 5 / Data Hall - EPMS	15	15	08-Oct-27	28-Oct-27
P9RP.1180	Phase 5 / Data Hall - Lower Polycarbonate Panels	5	5	29-Oct-27	04-Nov-27
P9RP.1090	Phase 5 / Data Hall - NEA Finalization	20	20	25-Jan-28	21-Feb-28
P9RP.1140	Phase 5 / Data Hall - H2C Readiness Coordination	14	14	22-Feb-28	10-Mar-28
Phase 5 - TAHU Gallery		142	142	30-Mar-27	18-Oct-27
P9DG.1250	Phase 5 / TAHU - Fire Protection Rough In	5	5	30-Mar-27	05-Apr-27
P9DG.1170	Phase 5 / TAHU - Sound Attenuator	10	10	23-Jul-27	05-Aug-27
P9DG.1180	Phase 5 / TAHU - Seismic Install	2	2	23-Jul-27	26-Jul-27
P9DG.1190	Phase 5 / TAHU - Hang Outside Stairwell / Lobby Drywall	4	4	23-Jul-27	28-Jul-27

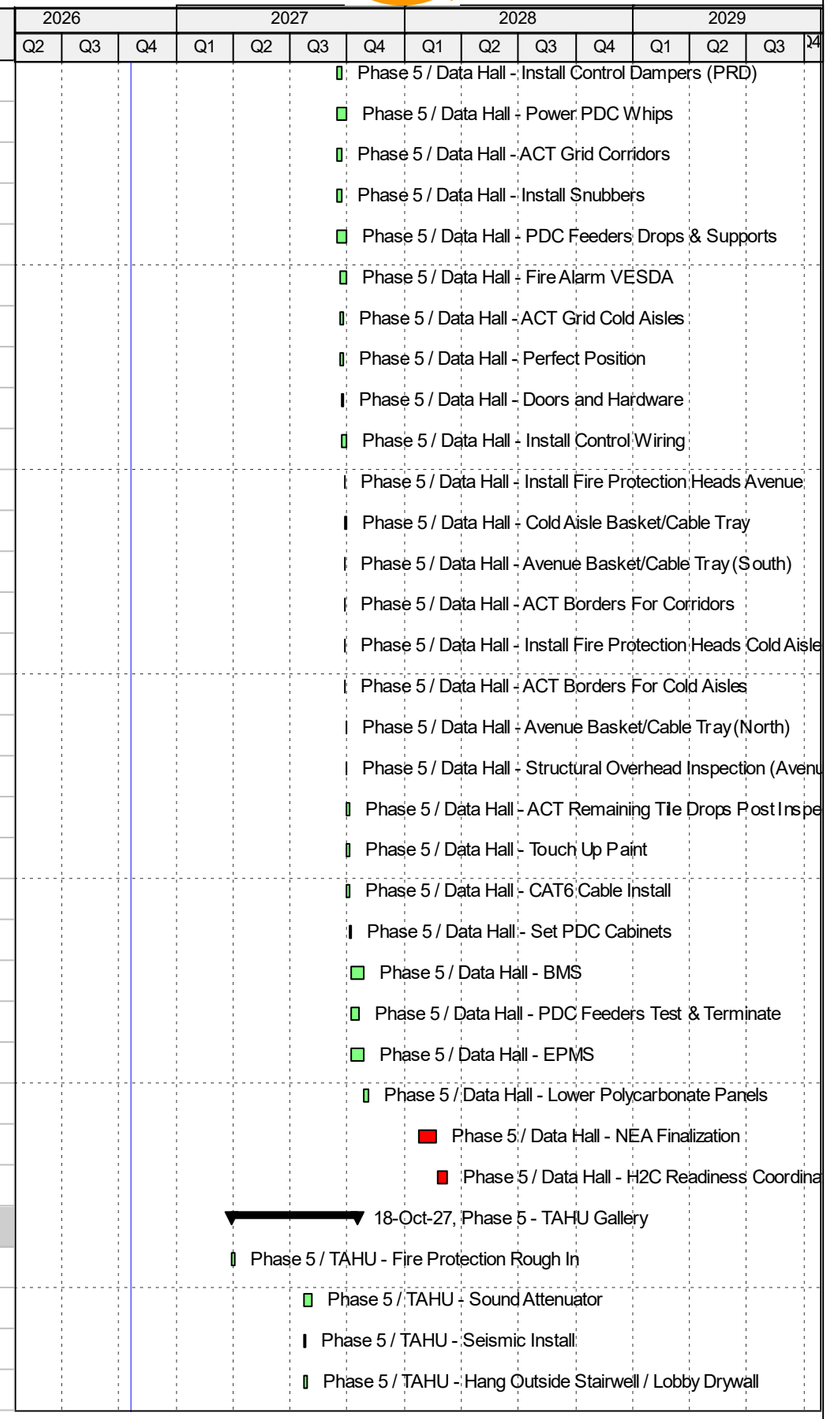

Activity ID	Activity Name	OD	RD	Start	Finish
P9DG.1200	Phase 5 / TAHU - Install CFMF IMP Support	10	10	23-Jul-27	05-Aug-27
P9DG.1040	Phase 5 / TAHU - Install IMP Panels	6	6	06-Aug-27	13-Aug-27
P9DG.1080	Phase 5 / TAHU - Prime & Paint Drywall	3	3	16-Aug-27	18-Aug-27
P9DG.1030	Phase 5 / TAHU - Wall Elec & Fire Alarm Rough-In	5	5	16-Aug-27	20-Aug-27
P9DG.1110	Phase 5 / TAHU - BMS Controls Rough In	10	10	16-Aug-27	27-Aug-27
P9DG.1130	Phase 5 / TAHU - Fire Alarm (VESDA)	5	5	16-Aug-27	20-Aug-27
P9DG.1090	Phase 5 / TAHU - Control Dampers	5	5	19-Aug-27	25-Aug-27
P9DG.1050	Phase 5 / TAHU - Pull & Terminate Fire Alarm Cable	5	5	23-Aug-27	27-Aug-27
P9DG.1070	Phase 5 / TAHU - Set TAHUs	2	2	07-Sep-27	08-Sep-27
P9DG.1140	Phase 5 / TAHU - Doors and Hardware	3	3	09-Sep-27	13-Sep-27
P9DG.1060	Phase 5 / TAHU - IW Supply Piping at TAHUs	10	10	09-Sep-27	22-Sep-27
P9DG.1220	Phase 5 / TAHU - TAHU Trim	10	10	09-Sep-27	22-Sep-27
P9DG.1230	Phase 5 / TAHU - Paint Doors & Frames	2	2	14-Sep-27	15-Sep-27
P9DG.1150	Phase 5 / TAHU - Lighting	5	5	23-Sep-27	29-Sep-27
P9DG.1100	Phase 5 / TAHU - Tie In TAHUs	10	10	23-Sep-27	06-Oct-27
P9DG.1210	Phase 5 / TAHU - BMS Tie In	2	2	05-Oct-27	06-Oct-27
P9DG.1120	Phase 5 / TAHU - IW Drain Piping at TAHUs	5	5	07-Oct-27	13-Oct-27
P9DG.1240	Phase 5 / TAHU - Terminate Power To TAHUs	3	3	14-Oct-27	18-Oct-27
Phase 5 - Cx		230	230	06-May-27	31-Mar-28
P9CX.1100	Phase 5 / Cx - EC L2 Cx Review for MV Switchgear	1	1	06-May-27	06-May-27
P9CX.1080	Phase 5 / Cx - EC L2 Cx Review for MV XFMRs	1	1	07-May-27	07-May-27
P9CX.1090	Phase 5 / Cx - EC L3 Cx for MV XFMRs	5	5	10-May-27	14-May-27
P9CX.1350	Phase 5 / Cx - Eaton XFMR Testing	3	3	10-May-27	12-May-27
P9CX.1130	Phase 5 / Cx - EC L3 Cx for MV	3	3	13-May-27	17-May-27
P9CX.1410	Phase 5 / Cx - Fuel System Cx	7	7	02-Jul-27	13-Jul-27
P9CX.1180	Phase 5 / Cx - Construction Power To Generator	3	3	09-Sep-27	13-Sep-27
P9CX.1030	Phase 5 / Cx - CAT L2 Cx Generators	2	2	14-Sep-27	15-Sep-27
P9CX.1120	Phase 5 / Cx - EC 3rd Party Testing & Inspection USB (L2)	3	3	14-Sep-27	16-Sep-27
P9CX.1160	Phase 5 / Cx - HUPPS Panelboards Energized	1	1	30-Sep-27	30-Sep-27
P9CX.1000	Phase 5 / Cx - EC 3rd Party LV Panelboard Testing (L2)	3	3	30-Sep-27	04-Oct-27
P9CX.1320	Phase 5 / Cx - AMCOP / BACOP Start Up & Cx	5	5	30-Sep-27	06-Oct-27
P9CX.1360	Phase 5 / Cx - Energize Control Network Arch	1	1	01-Oct-27	01-Oct-27
P9CX.1390	Phase 5 / Cx - EPMS Point to Point (USB)	4	4	04-Oct-27	07-Oct-27

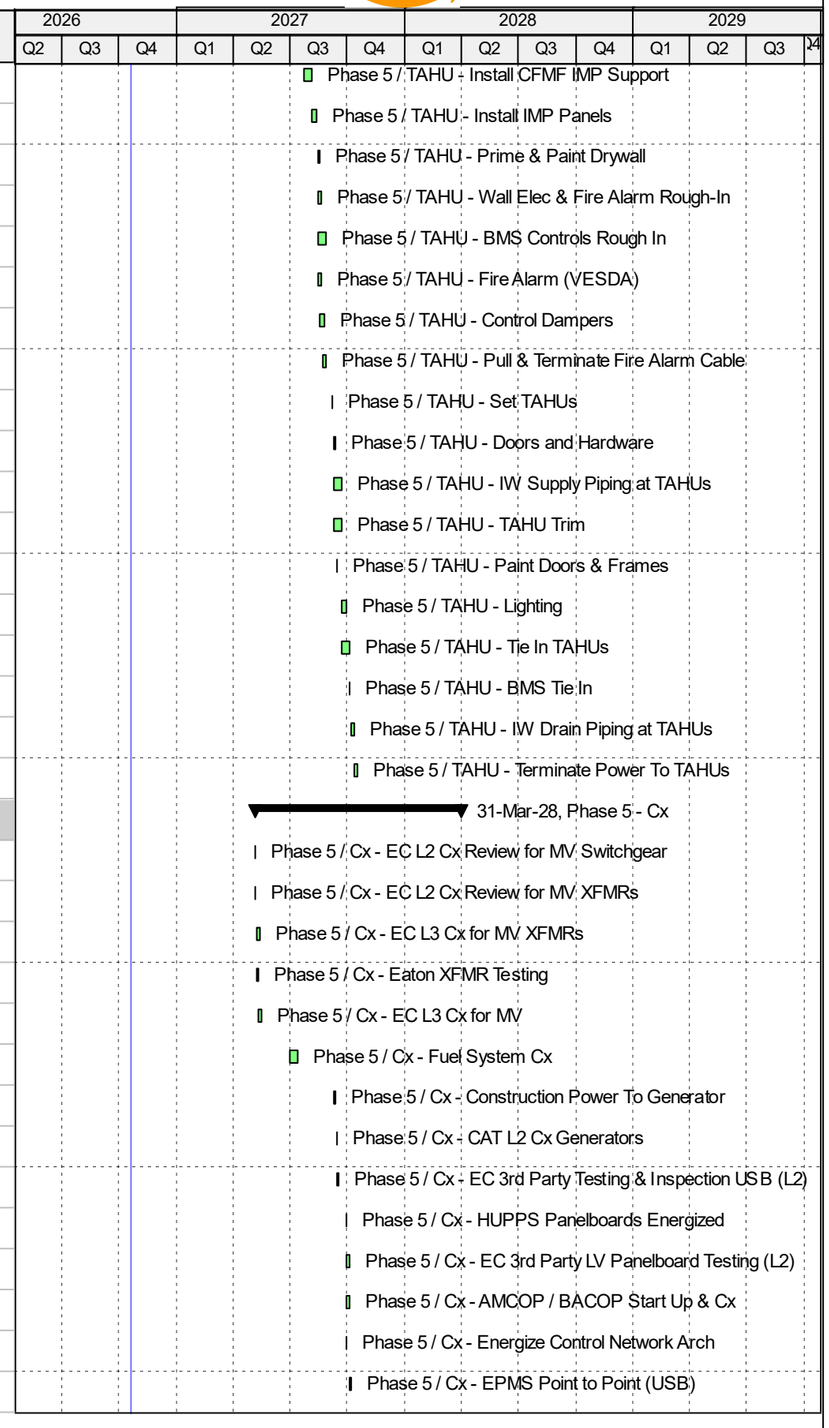


Gray

CMH139
Preliminary Schedule

aws

Activity ID	Activity Name	OD	RD	Start	Finish
P9CX.1470	Phase 5 / Cx - Fire Alarm Programming & Pretest	2	2	04-Oct-27	05-Oct-27
P9CX.1230	Phase 5 / Cx - EC 3rd Party Busway Bus Plug Testing (L2)	2	2	04-Oct-27	05-Oct-27
P9MCM.5010	Phase 5 / Cx - Tie in MOP C1	2	2	06-Oct-27	07-Oct-27
P9MCM.5020	Phase 5 / Cx - Eaton DLB Programming & Test (FLORES)	5	5	07-Oct-27	13-Oct-27
P9MCM.5030	Phase 5 / Cx - Tie in MOP C2	2	2	08-Oct-27	11-Oct-27
P9CX.1140	Phase 5 / Cx - EC 3rd Party Busway C1 / C2 Testing	2	2	12-Oct-27	13-Oct-27
P9CX.1190	Phase 5 / Cx - EC L2 Cx Review for LV Panelboard	2	2	12-Oct-27	13-Oct-27
P9MS.180	Phase 5 / Cx - Life Safety Walkthrough	1	1	13-Oct-27	13-Oct-27
P9CX.1260	Phase 5 / Cx - EC L3 Cx LV Panelboard	1	1	14-Oct-27	14-Oct-27
P9CX.1170	Phase 5 / Cx - EC Busway C1 / C2 L2 Cx Review	1	1	14-Oct-27	14-Oct-27
P9CX.1220	Phase 5 / Cx - EC Busway C1 L3 Cx	2	2	15-Oct-27	18-Oct-27
P9CX.1380	Phase 5 / Cx - EPMS Point to Point (PDC)	4	4	15-Oct-27	20-Oct-27
P9CX.1210	Phase 5 / Cx - MC TAHU L2 Cx	5	5	19-Oct-27	25-Oct-27
P9CX.1480	Phase 5 / Cx - EC Busway C2 L3 Cx	2	2	19-Oct-27	20-Oct-27
P9CX.1370	Phase 5 / Cx - BMS Point to Point (TAHUs)	5	5	26-Oct-27	01-Nov-27
P9CX.1150	Phase 5 / Cx - EC L3 Cx USBs	2	2	10-Nov-27	11-Nov-27
P9CX.1250	Phase 5 / Cx - Vendor UPS Start Up & Cx	9	9	12-Nov-27	24-Nov-27
P9CX.1310	Phase 5 / Cx - ATS L3 Cx	1	1	12-Nov-27	12-Nov-27
P9CX.1420	Phase 5 / Cx - Eaton DLB Testing	2	2	12-Nov-27	15-Nov-27
P9CX.1400	Phase 5 / Cx - Energize MSDBs	1	1	15-Nov-27	15-Nov-27
P9CX.1290	Phase 5 / Cx - Split System Startup & Commissioning	10	10	16-Nov-27	01-Dec-27
P9CX.1280	Phase 5 / Cx - ERV Startup & Commissioning	10	10	16-Nov-27	01-Dec-27
P9CX.1270	Phase 5 / Cx - EDH Startup & Commissioning	4	4	16-Nov-27	19-Nov-27
P9CX.1010	Phase 5 / Cx - IW System L2 Cx	2	2	16-Nov-27	17-Nov-27
P9CX.1020	Phase 5 / Cx - IW System L3 Cx	10	10	18-Nov-27	03-Dec-27
P9CX.1040	Phase 5 / Cx - EC L2 Cx Review for Generator	1	1	03-Dec-27	03-Dec-27
P9CX.1070	Phase 5 / Cx - EC L3 Cx Generators	3	3	06-Dec-27	08-Dec-27
P9CX.1060	Phase 5 / Cx - CAT L3 Cx Generators Testing	5	5	06-Dec-27	10-Dec-27
P9CX.1240	Phase 5 / Cx - Vendor TAHU L3 Cx	10	10	06-Dec-27	17-Dec-27
P9CX.1330	Phase 5 / Cx - Test & Balance	5	5	20-Dec-27	27-Dec-27
P9CX.1430	Phase 5 / Cx - L4 / L5 Cx	15	15	13-Mar-28	31-Mar-28
Phase 6 (ROMP10 & 12)		257	257	27-Apr-27	28-Apr-28
Phase 6 - Gen Yard		153	153	27-Apr-27	02-Dec-27

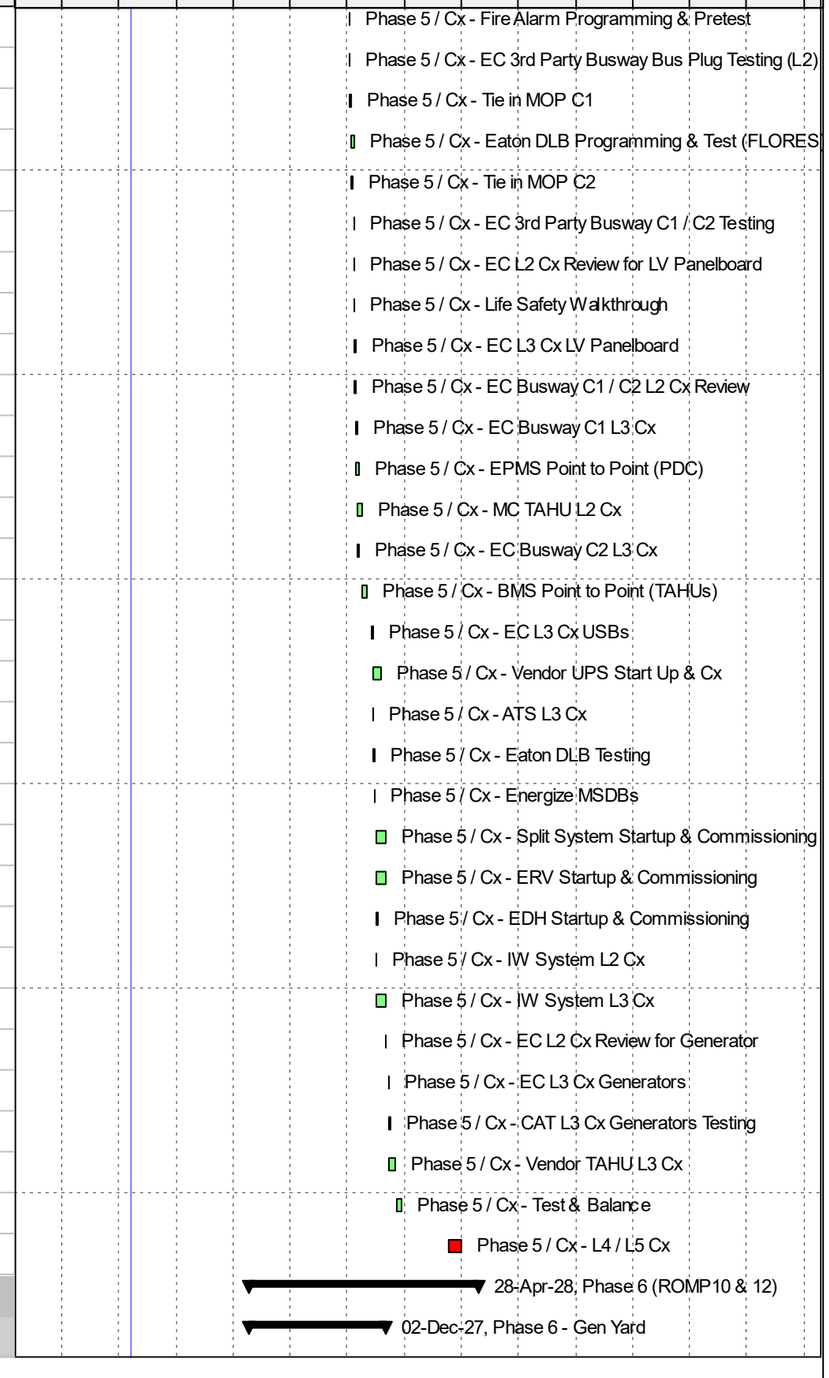


Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

Run Date: 15-Oct-26 14:16
Data Date: 19-Oct-26

Activity ID	Activity Name	OD	RD	Start	Finish
P10EX.1030	Phase 6 / Gen Yard - Set Transformers	2	2	27-Apr-27	28-Apr-27
P10EX.1050	Phase 6 / Gen Yard - Pull, Term & Test MV through XFMRs	7	7	29-Apr-27	07-May-27
P10EX.1100	Phase 6 / Gen Yard - Pull In FLORES Loop	5	5	10-May-27	14-May-27
P10EX.1370	Phase 6 / Gen Yard - Install Fuel Piping	30	30	20-May-27	01-Jul-27
P10EX.1380	Phase 6 / Gen Yard - Install Fuel System Control Conduit	10	10	04-Jun-27	17-Jun-27
P10EX.1120	Phase 6 / Gen Yard - Pour Sidewalk	5	5	18-Jun-27	24-Jun-27
P10EX.1060	Phase 6 / Gen Yard - Set Generators	2	2	12-Oct-27	13-Oct-27
P10EX.1090	Phase 6 / Gen Yard - Set Exhaust Stack and Shroud	12	12	14-Oct-27	29-Oct-27
P10EX.1040	Phase 6 / Gen Yard - Install Cable Bus Structure	5	5	20-Oct-27	26-Oct-27
P10EX.1070	Phase 6 / Gen Yard - LV Cable Bus and Feeders - XFMRs to USBs	10	10	27-Oct-27	09-Nov-27
P10EX.1390	Phase 6 / Gen Yard - Grounding / Lightning Protection	2	2	01-Nov-27	02-Nov-27
P10EX.1110	Phase 6 / Gen Yard - Energize Electrical - Site To Phase	0	0		09-Nov-27
P10EX.1190	Phase 6 / Gen Yard - LV Cable Bus and Feeders - Gens to USBs	15	15	10-Nov-27	02-Dec-27
P10EX.1080	Phase 6 / Gen Yard - Install Generator Platforms	5	5	11-Nov-27	17-Nov-27
P10EX.1130	Phase 6 / Gen Yard - Install Foundations & Fencing	4	4	18-Nov-27	23-Nov-27
Phase 6 - Electrical Room		147	147	05-May-27	02-Dec-27
P10ER.2220	Phase 6 / Elec Rm - Layout	1	1	05-May-27	05-May-27
P10ER.2450	Phase 6 / Elec Rm - Install DriClad	10	10	06-May-27	19-May-27
P10ER.1040	Phase 6 / Elec Rm - Wall Electric & Fire Alarm Rough-in	5	5	19-May-27	25-May-27
P10ER.1020	Phase 6 / Elec Rm - Stud Framing	4	4	20-May-27	25-May-27
P10ER.1380	Phase 6 / Elec Rm - Hangers	3	3	26-May-27	28-May-27
P10ER.1060	Phase 6 / Elec Rm - Hang Drywall & Finish	5	5	27-Aug-27	02-Sep-27
P10ER.1000	Phase 6 / Elec Rm - Pull TAHU Feeders	5	5	27-Aug-27	02-Sep-27
P10ER.2230	Phase 6 / Elec Rm - Fire Protection Rough In	3	3	27-Aug-27	31-Aug-27
P10ER.2240	Phase 6 / Elec Rm - Install OH Conduit / Mechanical Feeders	5	5	27-Aug-27	02-Sep-27
P10ER.1390	Phase 6 / Elec Rm - Pull / Term HUPPs	2	2	01-Sep-27	02-Sep-27
P10ER.1080	Phase 6 / Elec Rm - Prime & First Coat Paint	1	1	03-Sep-27	03-Sep-27
P10ER.1010	Phase 6 / Elec Rm - Pull Lighting Control Wiring	7	7	03-Sep-27	14-Sep-27
P10ER.1120	Phase 6 / Elec Rm - Install Split Systems & ERV	10	10	07-Sep-27	20-Sep-27
P10ER.2250	Phase 6 / Elec Rm - Set USB (LV Gear)	5	5	12-Oct-27	18-Oct-27
P10ER.1140	Phase 6 / Elec Rm - Install AMCOP Panels	1	1	19-Oct-27	19-Oct-27
P10ER.2270	Phase 6 / Elec Rm - Doors & Hardware	5	5	19-Oct-27	25-Oct-27
P10ER.2280	Phase 6 / Elec Rm - Breaker Testing USB	5	5	19-Oct-27	25-Oct-27



Activity ID	Activity Name	OD	RD	Start	Finish
P10ER.2260	Phase 6 / Elec Rm - Fill Buck Out	4	4	19-Oct-27	22-Oct-27
P10ER.2290	Phase 6 / Elec Rm - Install Cable Tray	7	7	19-Oct-27	27-Oct-27
P10ER.2320	Phase 6 / Elec Rm - Install CRAC Unit & Exhaust Fan	5	5	21-Oct-27	27-Oct-27
P10ER.1210	Phase 6 / Elec Rm - Set SCCS Setting for Breakers	1	1	26-Oct-27	26-Oct-27
P10ER.2300	Phase 6 / Elec Rm - Cable Bus Termination	4	4	27-Oct-27	01-Nov-27
P10ER.1110	Phase 6 / Elec Rm - Set OFCI Electrical Panels	5	5	28-Oct-27	03-Nov-27
P10ER.2310	Phase 6 / Elec Rm - Fire Alarm / VESDA	5	5	28-Oct-27	03-Nov-27
P10ER.2330	Phase 6 / Elec Rm - Install Bus Duct	7	7	28-Oct-27	05-Nov-27
P10ER.2350	Phase 6 / Elec Rm - OA Reference Piping	5	5	28-Oct-27	03-Nov-27
P10ER.2430	Phase 6 / Elec Rm - Install Control Conduit	5	5	28-Oct-27	03-Nov-27
P10ER.1330	Phase 6 / Elec Rm - Pull & Term DLB Fiber	5	5	04-Nov-27	10-Nov-27
P10ER.2340	Phase 6 / Elec Rm - Install Electrical Raceways (Branch Conduits)	10	10	04-Nov-27	17-Nov-27
P10ER.2440	Phase 6 / Elec Rm - Install UPS	4	4	04-Nov-27	09-Nov-27
P10ER.1150	Phase 6 / Elec Rm - Pull PDC Feeders	5	5	05-Nov-27	11-Nov-27
P10ER.1160	Phase 6 / Elec Rm - Terminate LV Electrical Panels	5	5	09-Nov-27	15-Nov-27
P10ER.2360	Phase 6 / Elec Rm - Manufacturer Inspection USB	1	1	11-Nov-27	11-Nov-27
P10ER.1220	Phase 6 / Elec Rm - Install Lighting	3	3	12-Nov-27	16-Nov-27
P10ER.2380	Phase 6 / Elec Rm - Seismic Install	1	1	12-Nov-27	12-Nov-27
P10ER.2410	Phase 6 / Elec Rm - Test & Terminate PDC Feeders	5	5	12-Nov-27	18-Nov-27
P10ER.2390	Phase 6 / Elec Rm - Egress Lighting	3	3	12-Nov-27	16-Nov-27
P10ER.1180	Phase 6 / Elec Rm - BMS System	10	10	16-Nov-27	01-Dec-27
P10ER.2400	Phase 6 / Elec Rm - Trade Repair	3	3	18-Nov-27	22-Nov-27
P10ER.2420	Phase 6 / Elec Rm - Final Paint / Touch Up	1	1	23-Nov-27	23-Nov-27
P10ER.2370	Phase 6 / Elec Rm - Energize BMS Panels	1	1	02-Dec-27	02-Dec-27
Phase 6 - Data Hall		225	225	20-May-27	07-Apr-28
P10RP.1040	Phase 6 / Data Hall - Stud Framing (Data Hall / Elec Rm Wall)	5	5	20-May-27	26-May-27
P10RP.1700	Phase 6 / Data Hall - Stud Framing (Equipment Platform)	5	5	26-May-27	02-Jun-27
P10RP.1600	Phase 6 / Data Hall - OH Electric Rough In	5	5	03-Jun-27	09-Jun-27
P10RP.1760	Phase 6 / Data Hall - Fire Protection Rough In	5	5	30-Jun-27	07-Jul-27
P10RP.1100	Phase 6 / Data Hall - Wall Elec & FA Rough-In (IMP)	4	4	27-Aug-27	01-Sep-27
P10RP.1710	Phase 6 / Data Hall - Wall Elec & FA Rough-In (Data Hall / Elec Rm)	4	4	27-Aug-27	01-Sep-27
P10RP.1610	Phase 6 / Data Hall - In Wall Rough In Inspection (Electrical / FA)	1	1	02-Sep-27	02-Sep-27
P10RP.1130	Phase 6 / Data Hall - Hang Drywall & Finish (Data Hall / Elec Rm)	5	5	03-Sep-27	10-Sep-27

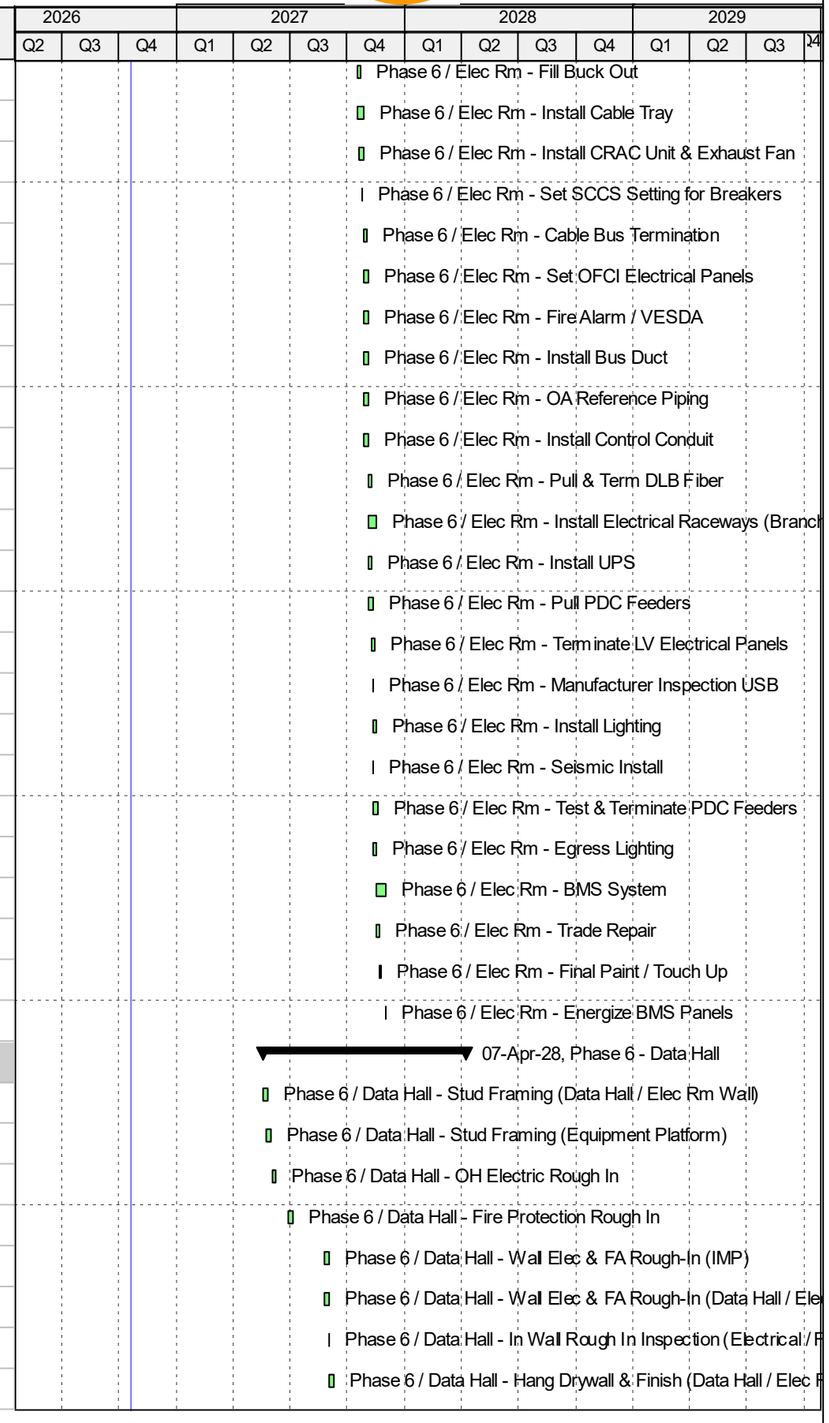


Gray

CMH139
Preliminary Schedule

aws


Activity ID	Activity Name	OD	RD	Start	Finish
P10RP.1590	Phase 6 / Data Hall - Install Temp Wall Bulkhead	5	5	03-Sep-27	10-Sep-27
P10RP.1190	Phase 6 / Data Hall - Prime & First Coat Paint	3	3	13-Sep-27	15-Sep-27
P10RP.1720	Phase 6 / Data Hall - Above Ceiling Cable Tray	3	3	13-Sep-27	15-Sep-27
P10RP.1050	Phase 6 / Data Hall - Fire Protection Drops	5	5	16-Sep-27	22-Sep-27
P10RP.1730	Phase 6 / Data Hall - Seismic Install	2	2	16-Sep-27	17-Sep-27
P10RP.1750	Phase 6 / Data Hall - Install Backdraft Dampers	5	5	16-Sep-27	22-Sep-27
P10RP.1020	Phase 6 / Data Hall - MARS Racking	7	7	12-Oct-27	20-Oct-27
P10RP.1070	Phase 6 / Data Hall - Install Lighting Wiring & Fixtures	5	5	21-Oct-27	27-Oct-27
P10RP.1200	Phase 6 / Data Hall - Temp Wall Install	5	5	21-Oct-27	27-Oct-27
P10RP.1060	Phase 6 / Data Hall - Upper Polycarbonate Panels and Cold Aisle Cable Tray Arms	3	3	21-Oct-27	25-Oct-27
P10RP.1230	Phase 6 / Data Hall - Install Control Dampers (PRD)	5	5	21-Oct-27	27-Oct-27
P10RP.1410	Phase 6 / Data Hall - Power PDC Whips	10	10	21-Oct-27	03-Nov-27
P10RP.1620	Phase 6 / Data Hall - ACT Grid Corridors	4	4	21-Oct-27	26-Oct-27
P10RP.1630	Phase 6 / Data Hall - Install Snubbers	5	5	21-Oct-27	27-Oct-27
P10RP.1030	Phase 6 / Data Hall - PDC Feeders Drops & Supports	10	10	21-Oct-27	03-Nov-27
P10RP.1210	Phase 6 / Data Hall - Fire Alarm VESDA	10	10	25-Oct-27	05-Nov-27
P10RP.1640	Phase 6 / Data Hall - ACT Grid Cold Aisles	5	5	25-Oct-27	29-Oct-27
P10RP.1140	Phase 6 / Data Hall - Perfect Position	4	4	26-Oct-27	29-Oct-27
P10RP.1250	Phase 6 / Data Hall - Doors and Hardware	2	2	28-Oct-27	29-Oct-27
P10RP.1650	Phase 6 / Data Hall - Install Control Wiring	5	5	28-Oct-27	03-Nov-27
P10RP.1280	Phase 6 / Data Hall - Install Fire Protection Heads Avenue	2	2	01-Nov-27	02-Nov-27
P10RP.1160	Phase 6 / Data Hall - Cold Aisle Basket/Cable Tray	3	3	01-Nov-27	03-Nov-27
P10RP.1360	Phase 6 / Data Hall - Avenue Basket/Cable Tray (South)	2	2	01-Nov-27	02-Nov-27
P10RP.1660	Phase 6 / Data Hall - ACT Borders For Corridors	1	1	01-Nov-27	01-Nov-27
P10RP.1740	Phase 6 / Data Hall - Install Fire Protection Heads Cold Aisle	2	2	01-Nov-27	02-Nov-27
P10RP.1670	Phase 6 / Data Hall - ACT Borders For Cold Aisles	1	1	02-Nov-27	02-Nov-27
P10RP.1290	Phase 6 / Data Hall - Avenue Basket/Cable Tray (North)	2	2	03-Nov-27	04-Nov-27
P10RP.1310	Phase 6 / Data Hall - Structural Overhead Inspection (Avenue)	1	1	03-Nov-27	03-Nov-27
P10RP.1690	Phase 6 / Data Hall - ACT Remaining Tile Drops Post Inspection	3	3	04-Nov-27	08-Nov-27
P10RP.1680	Phase 6 / Data Hall - Touch Up Paint	4	4	04-Nov-27	09-Nov-27
P10RP.1420	Phase 6 / Data Hall - CAT6 Cable Install	3	3	05-Nov-27	09-Nov-27
P10RP.1080	Phase 6 / Data Hall - Set PDC Cabinets	3	3	09-Nov-27	11-Nov-27
P10RP.1110	Phase 6 / Data Hall - BMS	15	15	12-Nov-27	06-Dec-27

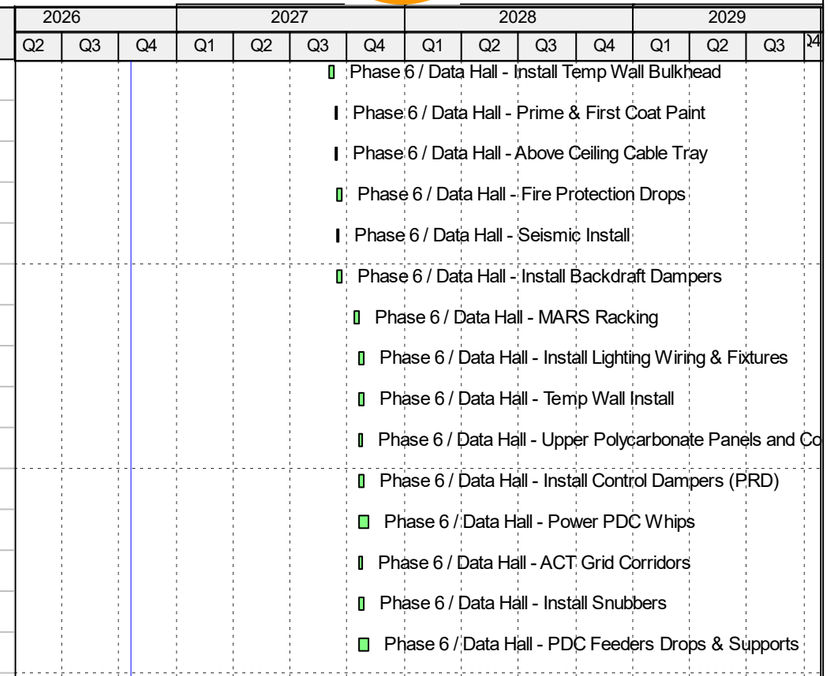

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary


Run Date: 15-Oct-26 14:16
Data Date: 19-Oct-26

Activity ID	Activity Name	OD	RD	Start	Finish
P10RP.1270	Phase 6 / Data Hall - PDC Feeders Test & Terminate	10	10	12-Nov-27	29-Nov-27
P10RP.1120	Phase 6 / Data Hall - EPMS	15	15	12-Nov-27	06-Dec-27
P10RP.1180	Phase 6 / Data Hall - Lower Polycarbonate Panels	5	5	07-Dec-27	13-Dec-27
P10RP.1090	Phase 6 / Data Hall - NEA Finalization	20	20	22-Feb-28	20-Mar-28
P10RP.1150	Phase 6 / Data Hall - H2C Readiness Coordination	14	14	21-Mar-28	07-Apr-28
Phase 6 - TAHU Gallery		112	112	23-Jun-27	01-Dec-27
P10DG.1250	Phase 6 / TAHU - Fire Protection Rough In	5	5	23-Jun-27	29-Jun-27
P10DG.1170	Phase 6 / TAHU - Sound Attenuator	10	10	27-Aug-27	10-Sep-27
P10DG.1180	Phase 6 / TAHU - Seismic Install	2	2	27-Aug-27	30-Aug-27
P10DG.1190	Phase 6 / TAHU - Hang Outside Stairwell / Lobby Drywall	4	4	13-Sep-27	16-Sep-27
P10DG.1200	Phase 6 / TAHU - Install CFMF IMP Support	10	10	13-Sep-27	24-Sep-27
P10DG.1040	Phase 6 / TAHU - Install IMP Panels	6	6	27-Sep-27	04-Oct-27
P10DG.1080	Phase 6 / TAHU - Prime & Paint Drywall	3	3	05-Oct-27	07-Oct-27
P10DG.1030	Phase 6 / TAHU - Wall Elec & Fire Alarm Rough-In	5	5	05-Oct-27	11-Oct-27
P10DG.1110	Phase 6 / TAHU - BMS Controls Rough In	10	10	05-Oct-27	18-Oct-27
P10DG.1130	Phase 6 / TAHU - Fire Alarm (VESDA)	5	5	05-Oct-27	11-Oct-27
P10DG.1090	Phase 6 / TAHU - Control Dampers	5	5	08-Oct-27	14-Oct-27
P10DG.1050	Phase 6 / TAHU - Pull & Terminate Fire Alarm Cable	5	5	12-Oct-27	18-Oct-27
P10DG.1070	Phase 6 / TAHU - Set TAHUs	2	2	19-Oct-27	20-Oct-27
P10DG.1140	Phase 6 / TAHU - Doors and Hardware	3	3	21-Oct-27	25-Oct-27
P10DG.1060	Phase 6 / TAHU - IW Supply Piping at TAHUs	10	10	21-Oct-27	03-Nov-27
P10DG.1220	Phase 6 / TAHU - TAHU Trim	10	10	21-Oct-27	03-Nov-27
P10DG.1230	Phase 6 / TAHU - Paint Doors & Frames	2	2	26-Oct-27	27-Oct-27
P10DG.1150	Phase 6 / TAHU - Lighting	5	5	28-Oct-27	03-Nov-27
P10DG.1100	Phase 6 / TAHU - Tie In TAHUs	10	10	04-Nov-27	17-Nov-27
P10DG.1210	Phase 6 / TAHU - BMS Tie In	2	2	16-Nov-27	17-Nov-27
P10DG.1120	Phase 6 / TAHU - IW Drain Piping at TAHUs	5	5	18-Nov-27	24-Nov-27
P10DG.1240	Phase 6 / TAHU - Terminate Power To TAHUs	3	3	29-Nov-27	01-Dec-27
Phase 6 - Cx		248	248	10-May-27	28-Apr-28
P10CX.1100	Phase 6 / Cx - EC L2 Cx Review for MV Switchgear	1	1	10-May-27	10-May-27
P10CX.1080	Phase 6 / Cx - EC L2 Cx Review for MV XFMRs	1	1	11-May-27	11-May-27
P10CX.1090	Phase 6 / Cx - EC L3 Cx for MV XFMRs	5	5	12-May-27	18-May-27
P10CX.1350	Phase 6 / Cx - Eaton XFMR Testing	3	3	12-May-27	14-May-27

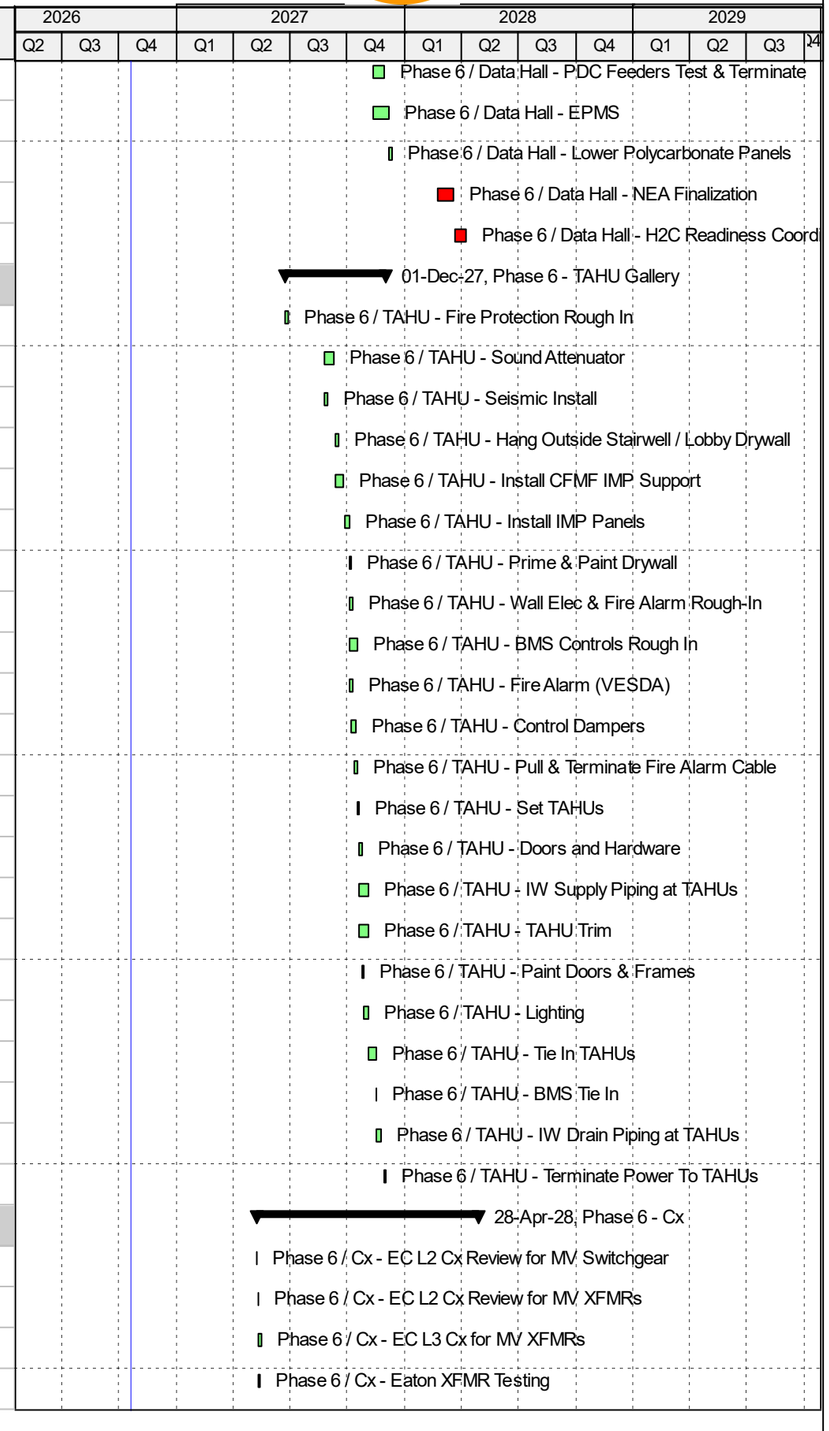

CMH139
Preliminary Schedule

Activity ID	Activity Name	OD	RD	Start	Finish
P10CX.1130	Phase 6 / Cx - EC L3 Cx for MV	3	3	17-May-27	19-May-27
P10CX.1200	Phase 6 / Cx - Fuel System Cx	7	7	02-Jul-27	13-Jul-27
P10CX.1180	Phase 6 / Cx - Construction Power To Generator	3	3	14-Oct-27	18-Oct-27
P10CX.1030	Phase 6 / Cx - CAT L2 Cx Generators	2	2	19-Oct-27	20-Oct-27
P10CX.1120	Phase 6 / Cx - EC 3rd Party Testing & Inspection USB (L2)	3	3	19-Oct-27	21-Oct-27
P10CX.1160	Phase 6 / Cx - HUPPS Panelboards Energized	1	1	04-Nov-27	04-Nov-27
P10CX.1000	Phase 6 / Cx - EC 3rd Party LV Panelboard Testing (L2)	3	3	04-Nov-27	08-Nov-27
P10CX.1320	Phase 6 / Cx - AMCOP / BACOP Start Up & Cx	5	5	04-Nov-27	10-Nov-27
P10CX.1360	Phase 6 / Cx - Energize Control Network Arch	1	1	05-Nov-27	05-Nov-27
P10CX.1390	Phase 6 / Cx - EPMS Point to Point (USB)	4	4	08-Nov-27	11-Nov-27
P10CX.1470	Phase 6 / Cx - Fire Alarm Programming & Pretest	2	2	08-Nov-27	09-Nov-27
P10CX.1230	Phase 6 / Cx - EC 3rd Party Busway Bus Plug Testing (L2)	2	2	08-Nov-27	09-Nov-27
P10MCM.5010	Phase 6 / Cx - Tie in MOP C1	2	2	10-Nov-27	11-Nov-27
P10MCM.5020	Phase 6 / Cx - Eaton DLB Programming & Test (FLORES)	5	5	11-Nov-27	17-Nov-27
P10MCM.5050	Phase 6 / Cx - Tie in MOP C2	2	2	12-Nov-27	15-Nov-27
P10CX.1140	Phase 6 / Cx - EC 3rd Party Busway C1 / C2 Testing	2	2	16-Nov-27	17-Nov-27
P10CX.1190	Phase 6 / Cx - EC L2 Cx Review for LV Panelboard	2	2	16-Nov-27	17-Nov-27
P10MS.180	Phase 6 / Cx - Life Safety Walkthrough	1	1	17-Nov-27	17-Nov-27
P10CX.1260	Phase 6 / Cx - EC L3 Cx LV Panelboard	1	1	18-Nov-27	18-Nov-27
P10CX.1170	Phase 6 / Cx - EC Busway C1 / C2 L2 Cx Review	1	1	18-Nov-27	18-Nov-27
P10CX.1220	Phase 6 / Cx - EC Busway C1 L3 Cx	2	2	19-Nov-27	22-Nov-27
P10CX.1380	Phase 6 / Cx - EPMS Point to Point (PDC)	4	4	19-Nov-27	24-Nov-27
P10CX.1480	Phase 6 / Cx - EC Busway C2 L3 Cx	2	2	23-Nov-27	24-Nov-27
P10CX.1150	Phase 6 / Cx - EC L3 Cx USBs	2	2	29-Nov-27	30-Nov-27
P10CX.1250	Phase 6 / Cx - Vendor UPS Start Up & Cx	9	9	01-Dec-27	13-Dec-27
P10CX.1310	Phase 6 / Cx - ATS L3 Cx	1	1	01-Dec-27	01-Dec-27
P10CX.1420	Phase 6 / Cx - Eaton DLB Testing	2	2	01-Dec-27	02-Dec-27
P10CX.1210	Phase 6 / Cx - MC TAHU L2 Cx	5	5	02-Dec-27	08-Dec-27
P10CX.1370	Phase 6 / Cx - BMS Point to Point (TAHUs)	5	5	02-Dec-27	08-Dec-27
P10CX.1400	Phase 6 / Cx - Energize MSDBs	1	1	02-Dec-27	02-Dec-27
P10CX.1040	Phase 6 / Cx - EC L2 Cx Review for Generator	1	1	03-Dec-27	03-Dec-27
P10CX.1290	Phase 6 / Cx - Split System Startup & Commissioning	10	10	03-Dec-27	16-Dec-27
P10CX.1280	Phase 6 / Cx - ERV Startup & Commissioning	10	10	03-Dec-27	16-Dec-27

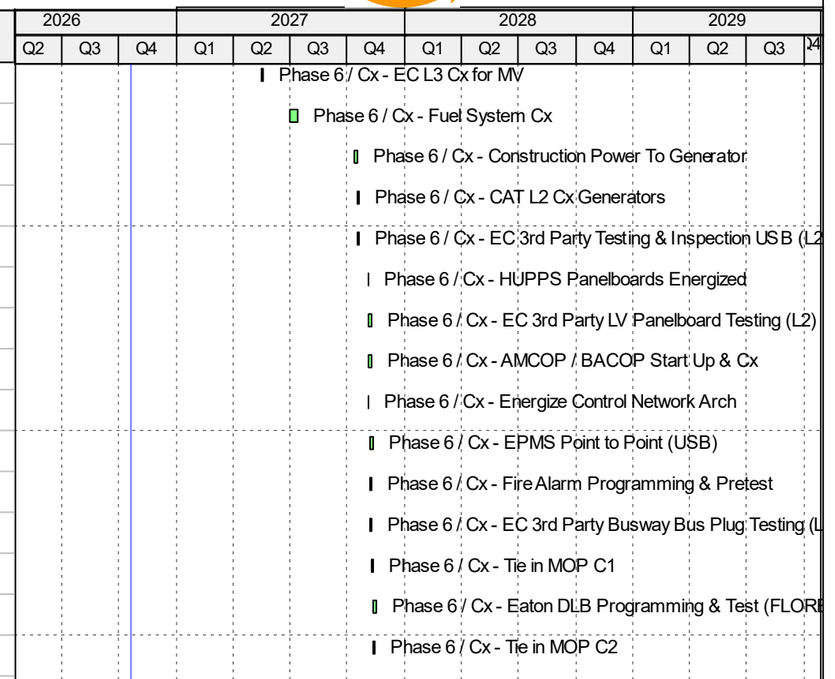

Activity ID	Activity Name	OD	RD	Start	Finish
P10CX.1270	Phase 6 / Cx - EDH Startup & Commissioning	4	4	03-Dec-27	08-Dec-27
P10MCM.5030	Phase 6 / Cx - IW System L2 Cx	2	2	03-Dec-27	06-Dec-27
P10CX.1070	Phase 6 / Cx - EC L3 Cx Generators	3	3	06-Dec-27	08-Dec-27
P10CX.1060	Phase 6 / Cx - CAT L3 Cx Generators Testing	5	5	06-Dec-27	10-Dec-27
P10MCM.5040	Phase 6 / Cx - IW System L3 Cx	10	10	07-Dec-27	20-Dec-27
P10CX.1240	Phase 6 / Cx - Vendor TAHU L3 Cx	10	10	21-Dec-27	05-Jan-28
P10CX.1330	Phase 6 / Cx - Test & Balance	5	5	06-Jan-28	12-Jan-28
P10CX.1430	Phase 6 / Cx - L4 / L5 Cx	15	15	10-Apr-28	28-Apr-28
Graveyard		27	0	08-Oct-26 A	08-Oct-26 A
SH.1770	Structure / Interior - L1 Fire Sprinkler Rough In	20	0	08-Oct-26 A	08-Oct-26 A
SH.1780	Structure / Interior - L2 Fire Sprinkler Rough In	20	0	08-Oct-26 A	08-Oct-26 A

